



AMERICAN
STRUCTUREPOINT
INC.



M MILLER
PIPELINE



LICKING COUNTY, OHIO HANOVER WATERLINE EXTENSION – PHASE 1

Recent Progress – (5-11-26 to 5-16-26)

- Finished TEMP asphalt paving repairs on W HIGH
- Restoration crews along W High and falling back to BUTLER and SWANS
- 12” Watermain, Service runs, and Hydrants completed on DARLA
- Boring crew resumed boring 12” Watermain MARNE Rd. eastward from Albyn’s Nursery

Week Look Ahead – (5-18-26 to 5-23-26)

- ***Miller Pipeline ADDED 2nd Pavement Repair crew to expedite improving conditions.**
 - o Crew 1 working northward up DARLA;
 - o Crew 2 continues working eastward on BOLEN toward LICKING VALLEY Rd. intersection.
- **Watermain TIE-IN for TEE of NEW HOME & W HIGH.** A crew will work on New Home service runs and hydrants this week.
- 12” Mainline Crew made turn from DARLA to MEADOW toward ECHO DRIVE intersection and will be working southward on Meadow until full loop is connected back at W High. Miller Pipeline will attempt to bore portion(s) if existing gas main location allows.
- Lawn Restoration crew continues up Swans and then down Bolen
- To be determined if MARNE mainline crew resumes this mid-week week. Bore machine had a breakdown last week and waiting on repairs or new machine availability

Traffic Impacts.

1. Meadow = 1-lane, 2-way traffic with flaggers
2. Darla & Bolen = 1-lane, 2-way traffic around pavement repair crews.
3. New Home, Swans, Bolen = service and restoration crews moving operations, observe signs, cones and flagger when needed
4. Marne = to be determined, would be 1-lane, 2-way traffic with flaggers

Approximate project complete: Near 70% calendar, 50.0% of pipe installation

Looking EAST at Lawn Restoration crew in front of Legacy Park



Asphalt Pavement Repairs over 12" Mainline on W HIGH are caught up, maintenance of traffic warning devices in place, sidewalk backfilled level to maintain pedestrian access



Repairing any affected drain tiles or Sanitary Service laterals with proper approved materials and verifying slope for drainage before backfill. Crews continue to discuss keeping work areas cleaner as they proceed, picking up bottles etc from site and into trash bags



12" Watermain pipe installation turn from DARLA to MEADOW





AMERICAN
STRUCTUREPOINT
INC.



2550 Corporate Exchange Ct., Ste. 400 | Columbus, Ohio 43221
TEL: 614.722.2226
www.structurepoint.com

CONSTRUCTION DOCUMENTS
FOR
HANOVER WATER EXTENSION
PHASE 1
CITY OF HANOVER, LICKING COUNTY, OHIO
OVERALL PLAN

DESCRIPTION


SHEET NO.

DATE

REVISIONS

DATE:	5/15/2026
DRAWN BY:	MNA
CHECKED BY:	BJM
JOB NUMBER:	2022.03308

C100

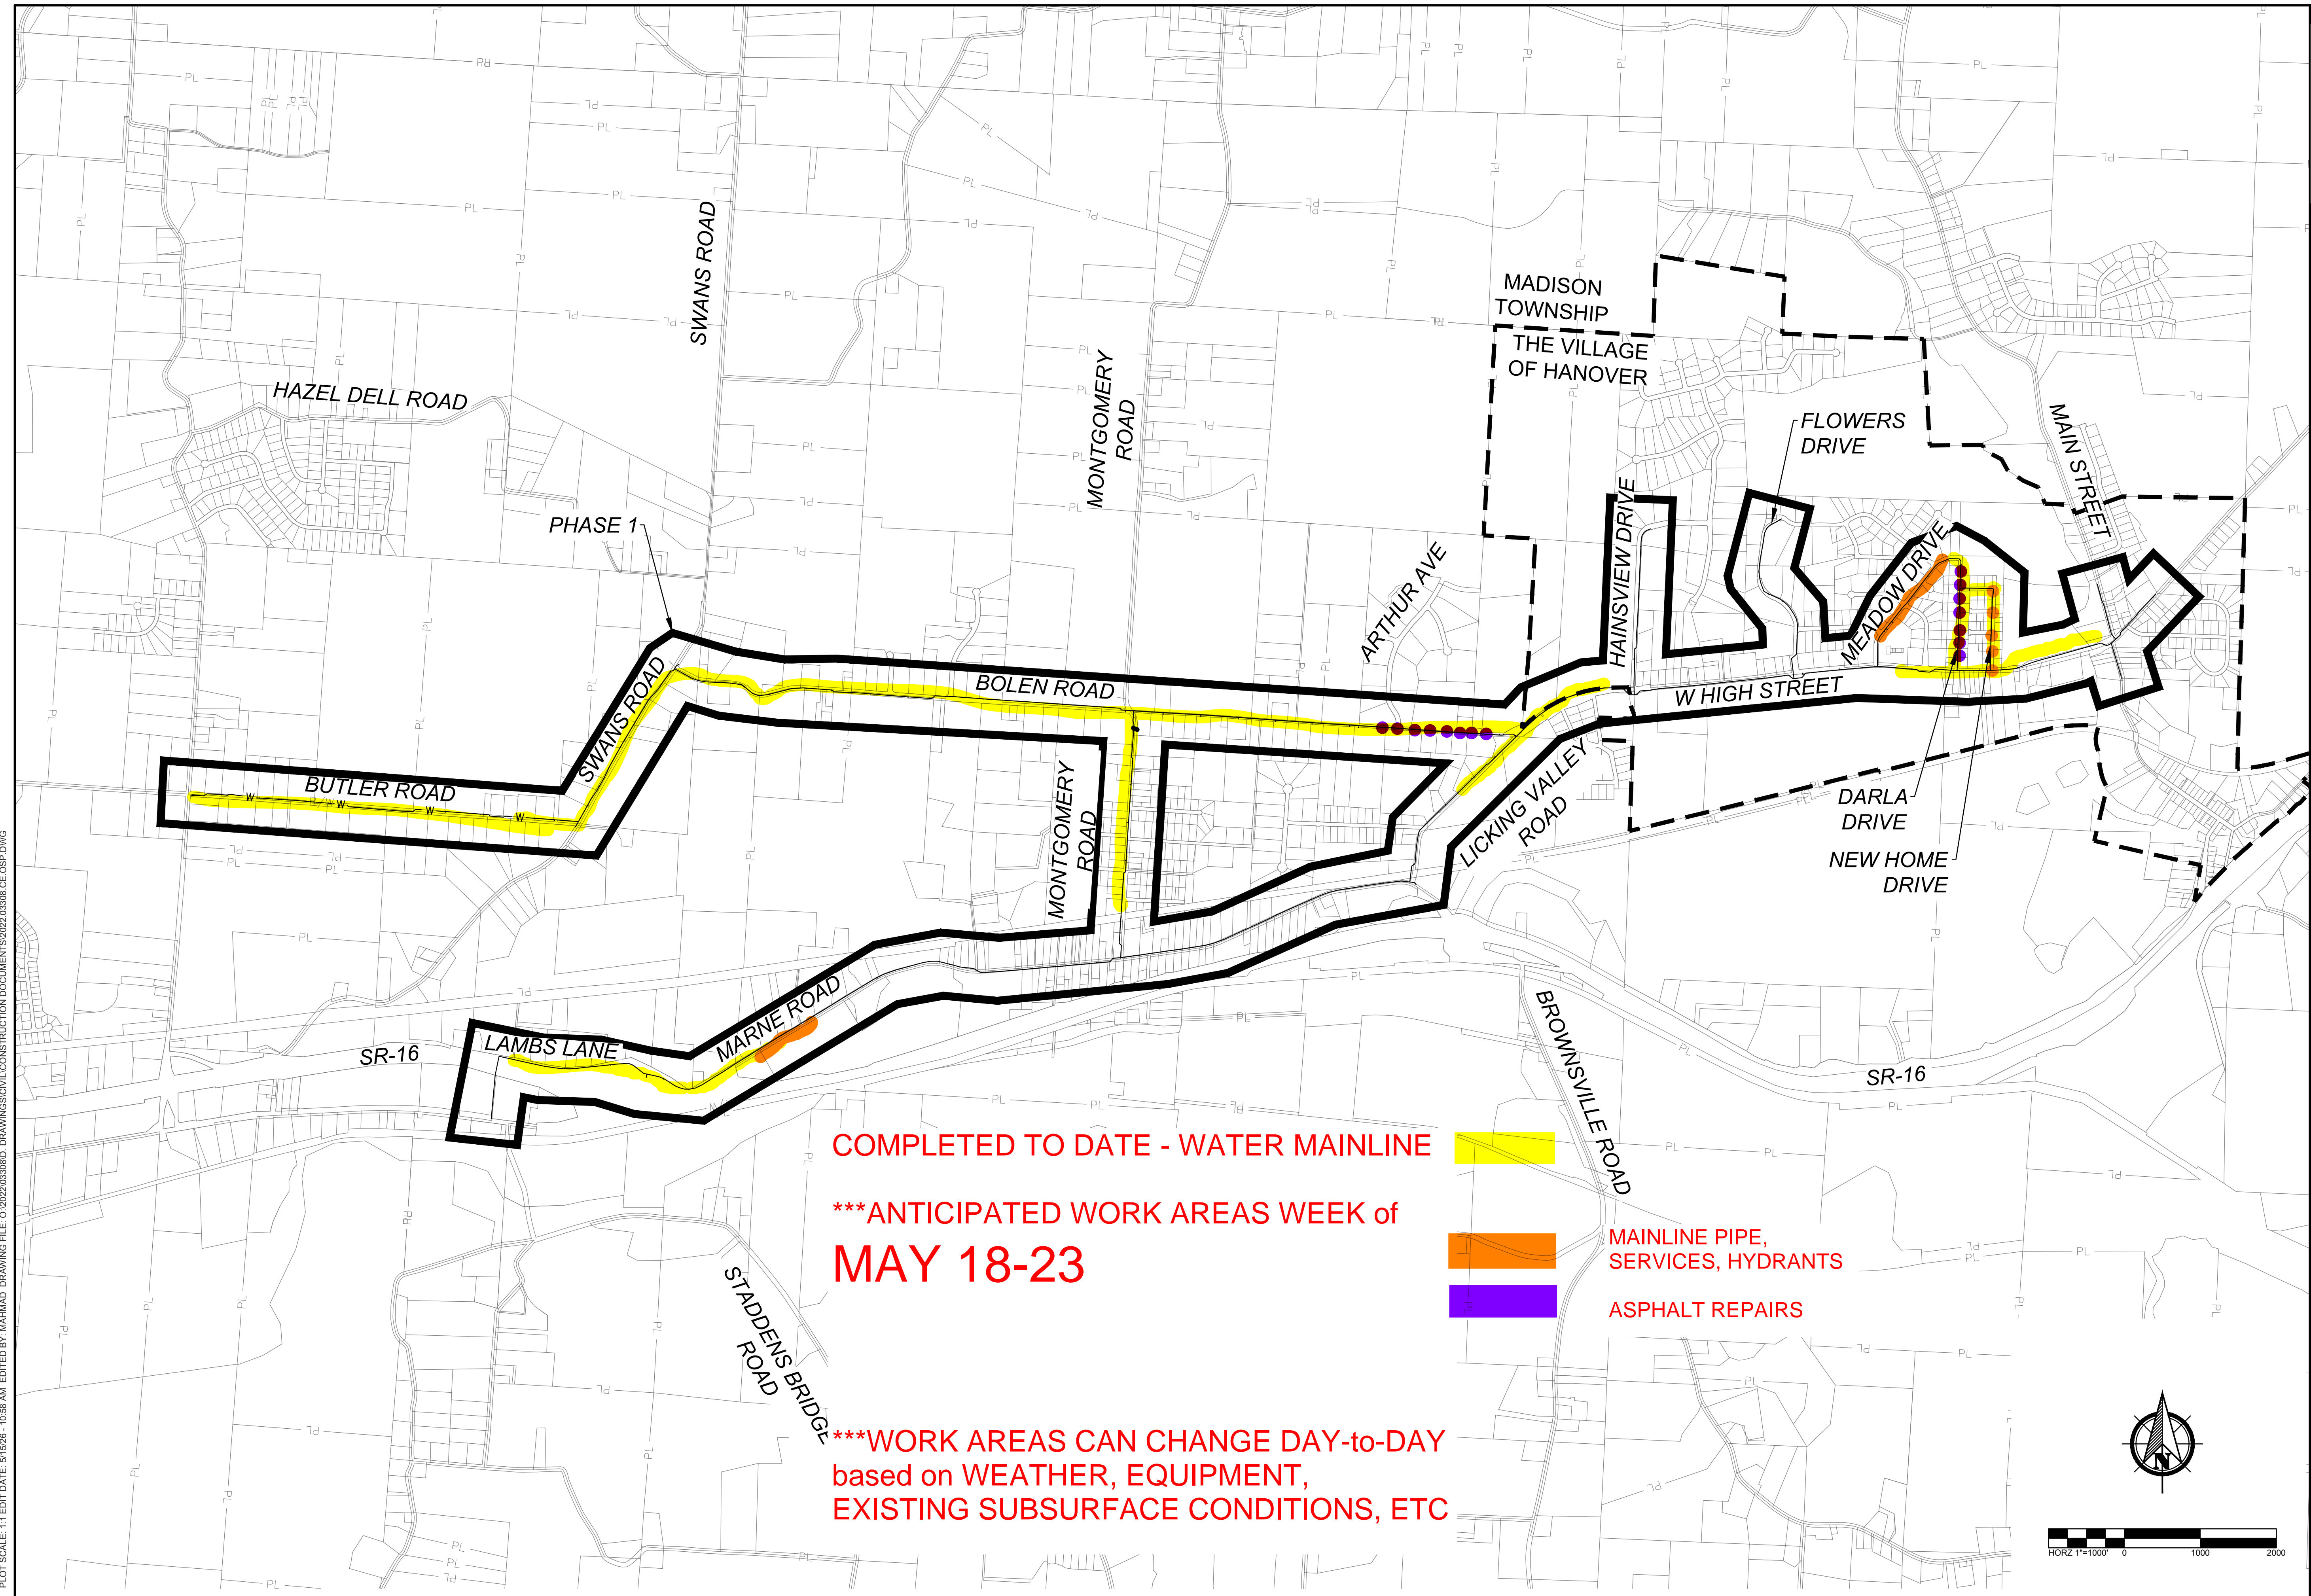

COMPLETED TO DATE - WATER MAINLINE


*****ANTICIPATED WORK AREAS WEEK of
MAY 18-23**

*****WORK AREAS CAN CHANGE DAY-to-DAY
based on WEATHER, EQUIPMENT,
EXISTING SUBSURFACE CONDITIONS, ETC**



**MAINLINE PIPE,
SERVICES, HYDRANTS**

ASPHALT REPAIRS



PLOT SCALE: 1:1 EDIT DATE: 5/15/26 - 10:58 AM EDITED BY: MAHMOUD DRAWING FILE: C:\2022\03308.D DRAWINGS\CIVIL\CONSTRUCTION\DOCUMENTS\2022.03308_CE_CSP.DWG
