



AMERICAN
STRUCTUREPOINT
INC.



M MILLER
PIPELINE



LICKING COUNTY, OHIO HANOVER WATERLINE EXTENSION – PHASE 1

Recent Progress – (6-03-26 to 6-09-26)

- 12” Water Main along MARNE Rd. bore installed to near MILLER RANCH Rd. that would be near 4,800 feet completed of 10,800 feet install to date on Marne Rd. from intersection to SR 16 / E Main intersection.
- 12” Water Main in MEADOW Dr. before intersection at W HIGH St. completed. All house services and hydrants on MEADOW, DARLA, NEW HOME complete for now to allow ongoing RESTORATION crew efforts for Asphalt and Lawns repairs
- BOLEN Rd. primary trench asphalt pavement repairs complete to Licking Valley Rd.
- 8” Water Main on BUTLER Rd. has PASSES pressure testing.

Week Look Ahead – (6-10-26 to 6-24-26)

- **Miller Pipeline two (2) Pavement Repair Crews**
 - o Crew 1 continues northward on DARLA, to turn and head southward down MEADOW.
 - o Crew 2 falling back to repair all spot asphalt locations on BOLEN eastward, then work behind Licking Valley Rd. install work for the...
- **12” Mainline crew on LICKING VALLEY RD.** in front of Middle School working back toward Bolen intersection, THEN jump to NW side at Hainsview intersection and cross over to the SW side of intersection and crossing the drive to the Primary School.
- **12” Mainline Crew on MARNE** continues working eastward from Miller Ranch Rd. boring all pipe installs underground as much as able.

Traffic Impacts. WORK HOURS can range from 7am – 7pm

1. Licking Valley Rd. = Mainline installs will have 1-lane, 2-way traffic with flaggers
2. Bolen = 1-lane, 2-way traffic around pavement repair crews
3. Marne = Mainline installs will have 1-lane, 2-way traffic with flaggers
4. Darla and Meadow = Asphalt repair work, local traffic please be aware to pass by or circle around as needed

Approximate project complete: Near 81% calendar, 60.0% of pipe installation

***American Structurepoint Inc. - On behalf of the Licking County project please reach out to Field Inspection Contacts for project related items for the most rapid assistance, a project inspector is on-site to help facilitate, including concerns within Village and Township areas, please reach out as needed.

ON-SITE Inspector = Mark Campbell - 740-566-2021 - mcampbell@structurepoint.com

Sr. Project Representative = Jacob Brooks - 330-720-1505 - jbrooks@structurepoint.com

***Residents/Property Owners please reach out to Inspector or Crew installing Water Service Boxes if staking for proposed Water Service location does not come into the correct side of house/business as your existing well system


New Home Water Service installs



MEADOW Water Service install



Hydrostatic Pressure Testing on Butler Rd. at 150+ PSI for 2 hours. Must hold with ZERO loss or within Specified and measurable range over that time to PASS.

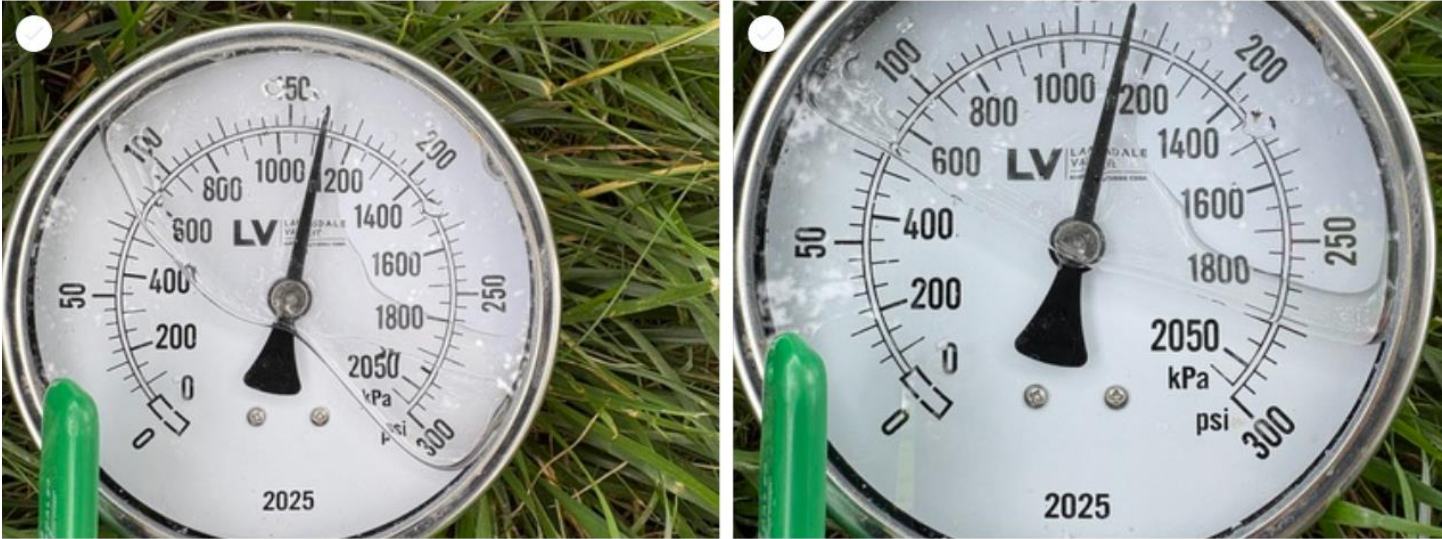

Bolen Rd. pavement replacement crew



Bolen Rd. main trench complete to LV Rd. falling back to begin spot hole repairs.




Preparing DARLA for full-depth pavement replacement



Typical Type B hydrant on New Home. Hydrant will be turned to face street at later date.



American Structurepoint Inspector walked W High Street with Village of Hanover Engineer Consultant to prepare a Punch List for that area to date. Same walkthroughs will be held with Licking County Depts., City of Newark, and Madison Township on their streets to note any needed project-related remediation work.

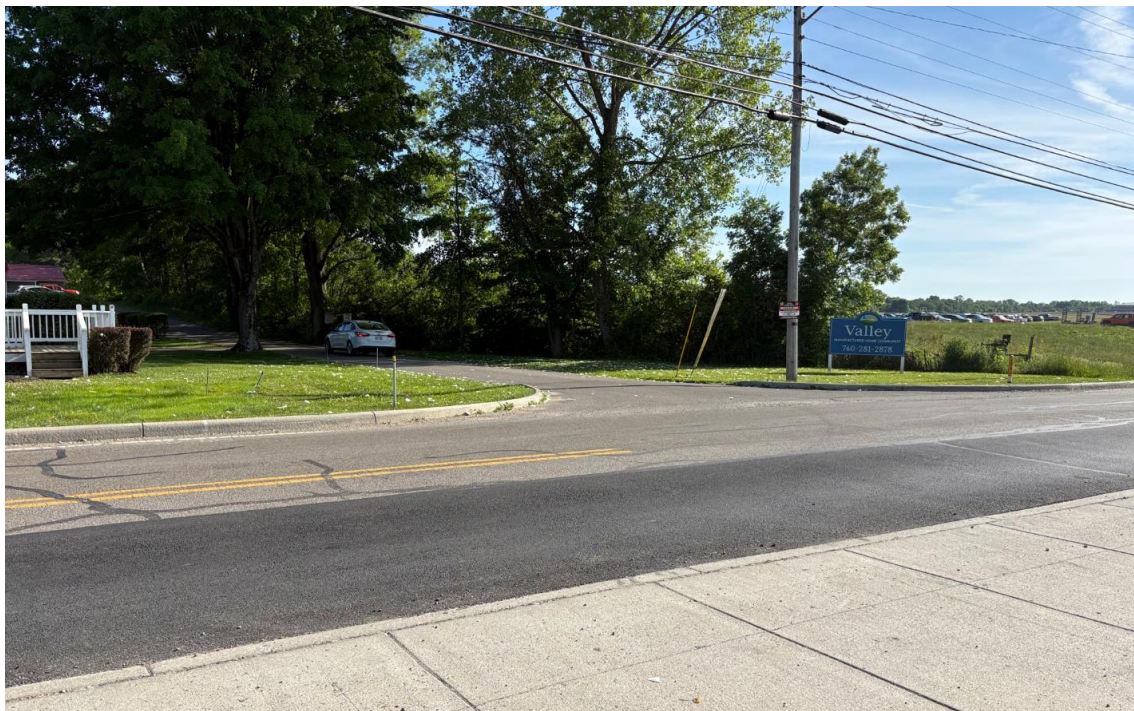



AMERICAN
STRUCTUREPOINT
INC.



2550 Corporate Exchange Ct., Ste. 400 | Columbus, Ohio 43221
TEL: 614.222.2226
www.structurepoint.com

CONSTRUCTION DOCUMENTS
FOR
HANOVER WATER EXTENSION
PHASE 1
CITY OF HANOVER, LICKING COUNTY, OHIO
OVERALL PLAN

DESCRIPTION

SHEET NO.


DATE

REVISIONS

DATE: 5/15/2026
DRAWN BY: MNA
CHECKED BY: BJM
JOB NUMBER: 2022.03308

C100

PLOT SCALE: 1:1 EDIT DATE: 5/15/26 - 10:58 AM EDITED BY: MAHMOUD DRAWING FILE: C:\2022\03308.D DRAWINGS\CIVIL\CONSTRUCTION\DOCUMENTS\2022.03308_CE_CSP.DWG

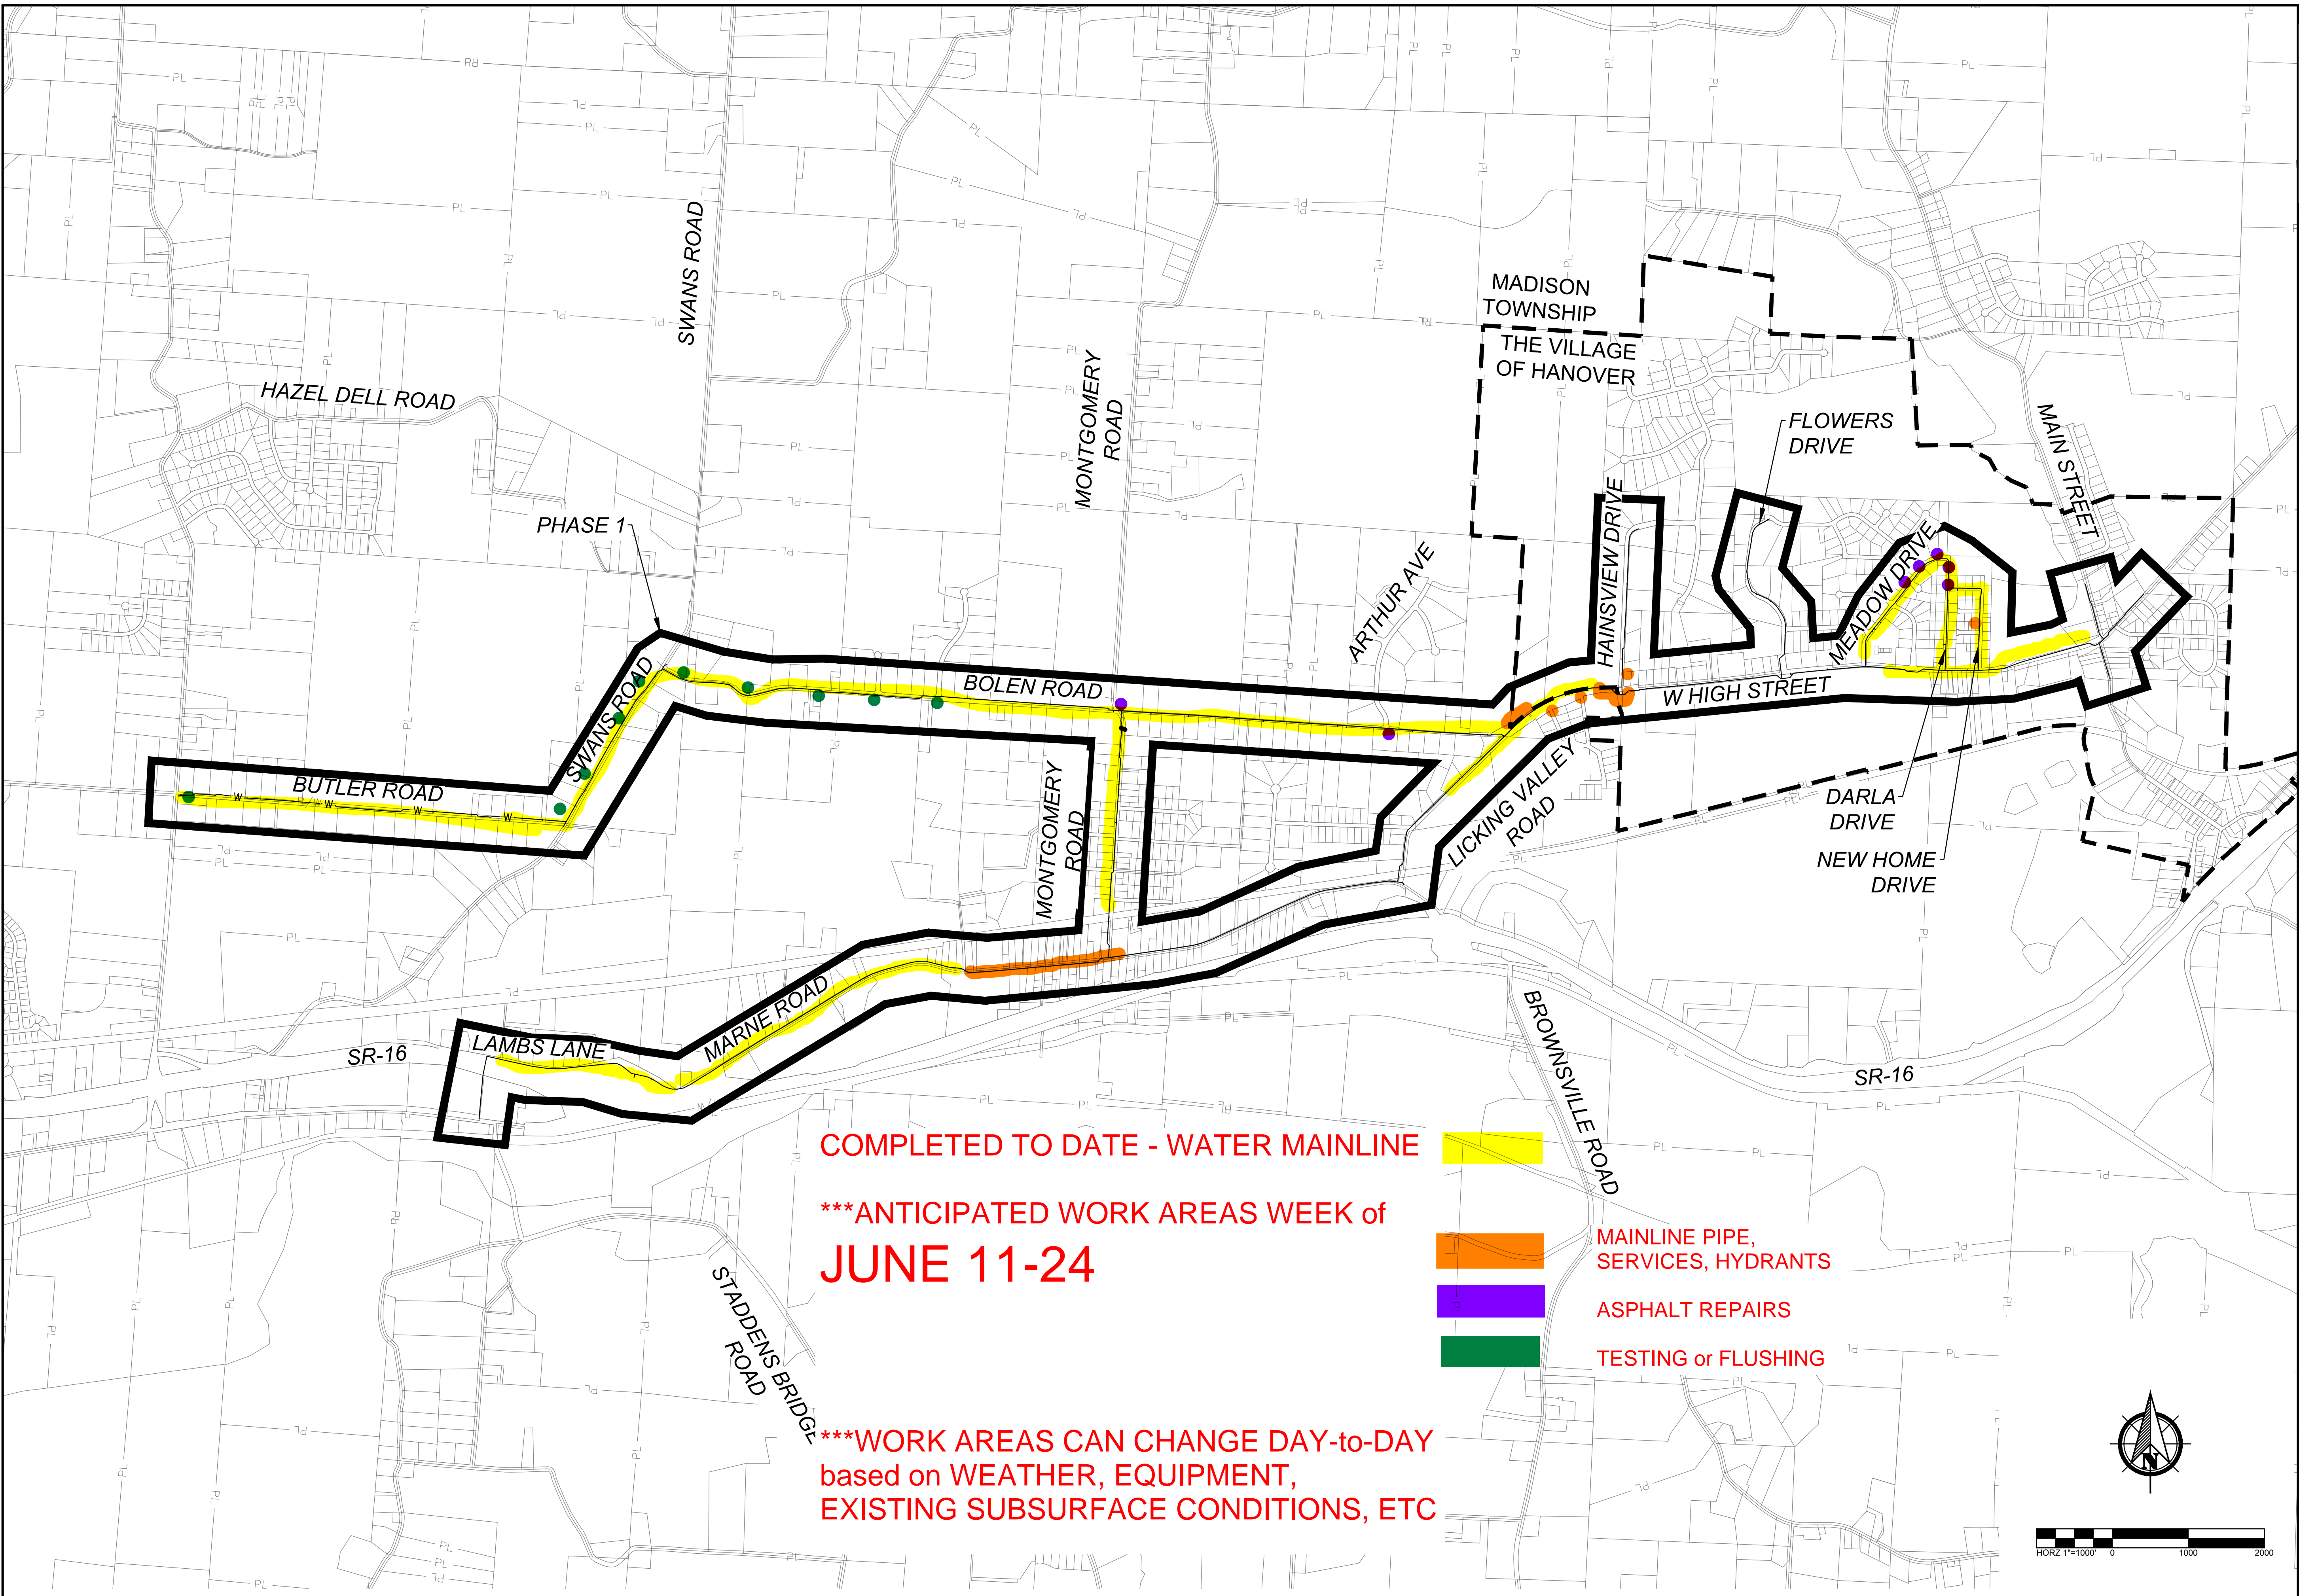


COMPLETED TO DATE - WATER MAINLINE


***ANTICIPATED WORK AREAS WEEK of
JUNE 11-24

***WORK AREAS CAN CHANGE DAY-to-DAY
based on WEATHER, EQUIPMENT,
EXISTING SUBSURFACE CONDITIONS, ETC

- MAINLINE PIPE, SERVICES, HYDRANTS
- ASPHALT REPAIRS
- TESTING or FLUSHING



PLOT SCALE: 1:1 EDIT DATE: 5/15/26 - 11:00 AM EDITED BY: MAHMOUD DRAWING FILE: C:\2022\03308D DRAWINGS\CIVIL\CONSTRUCTION\DOCUMENTS\ARCHIVE\2026-05-15\2022.03308D.CE.OSPV.DWG

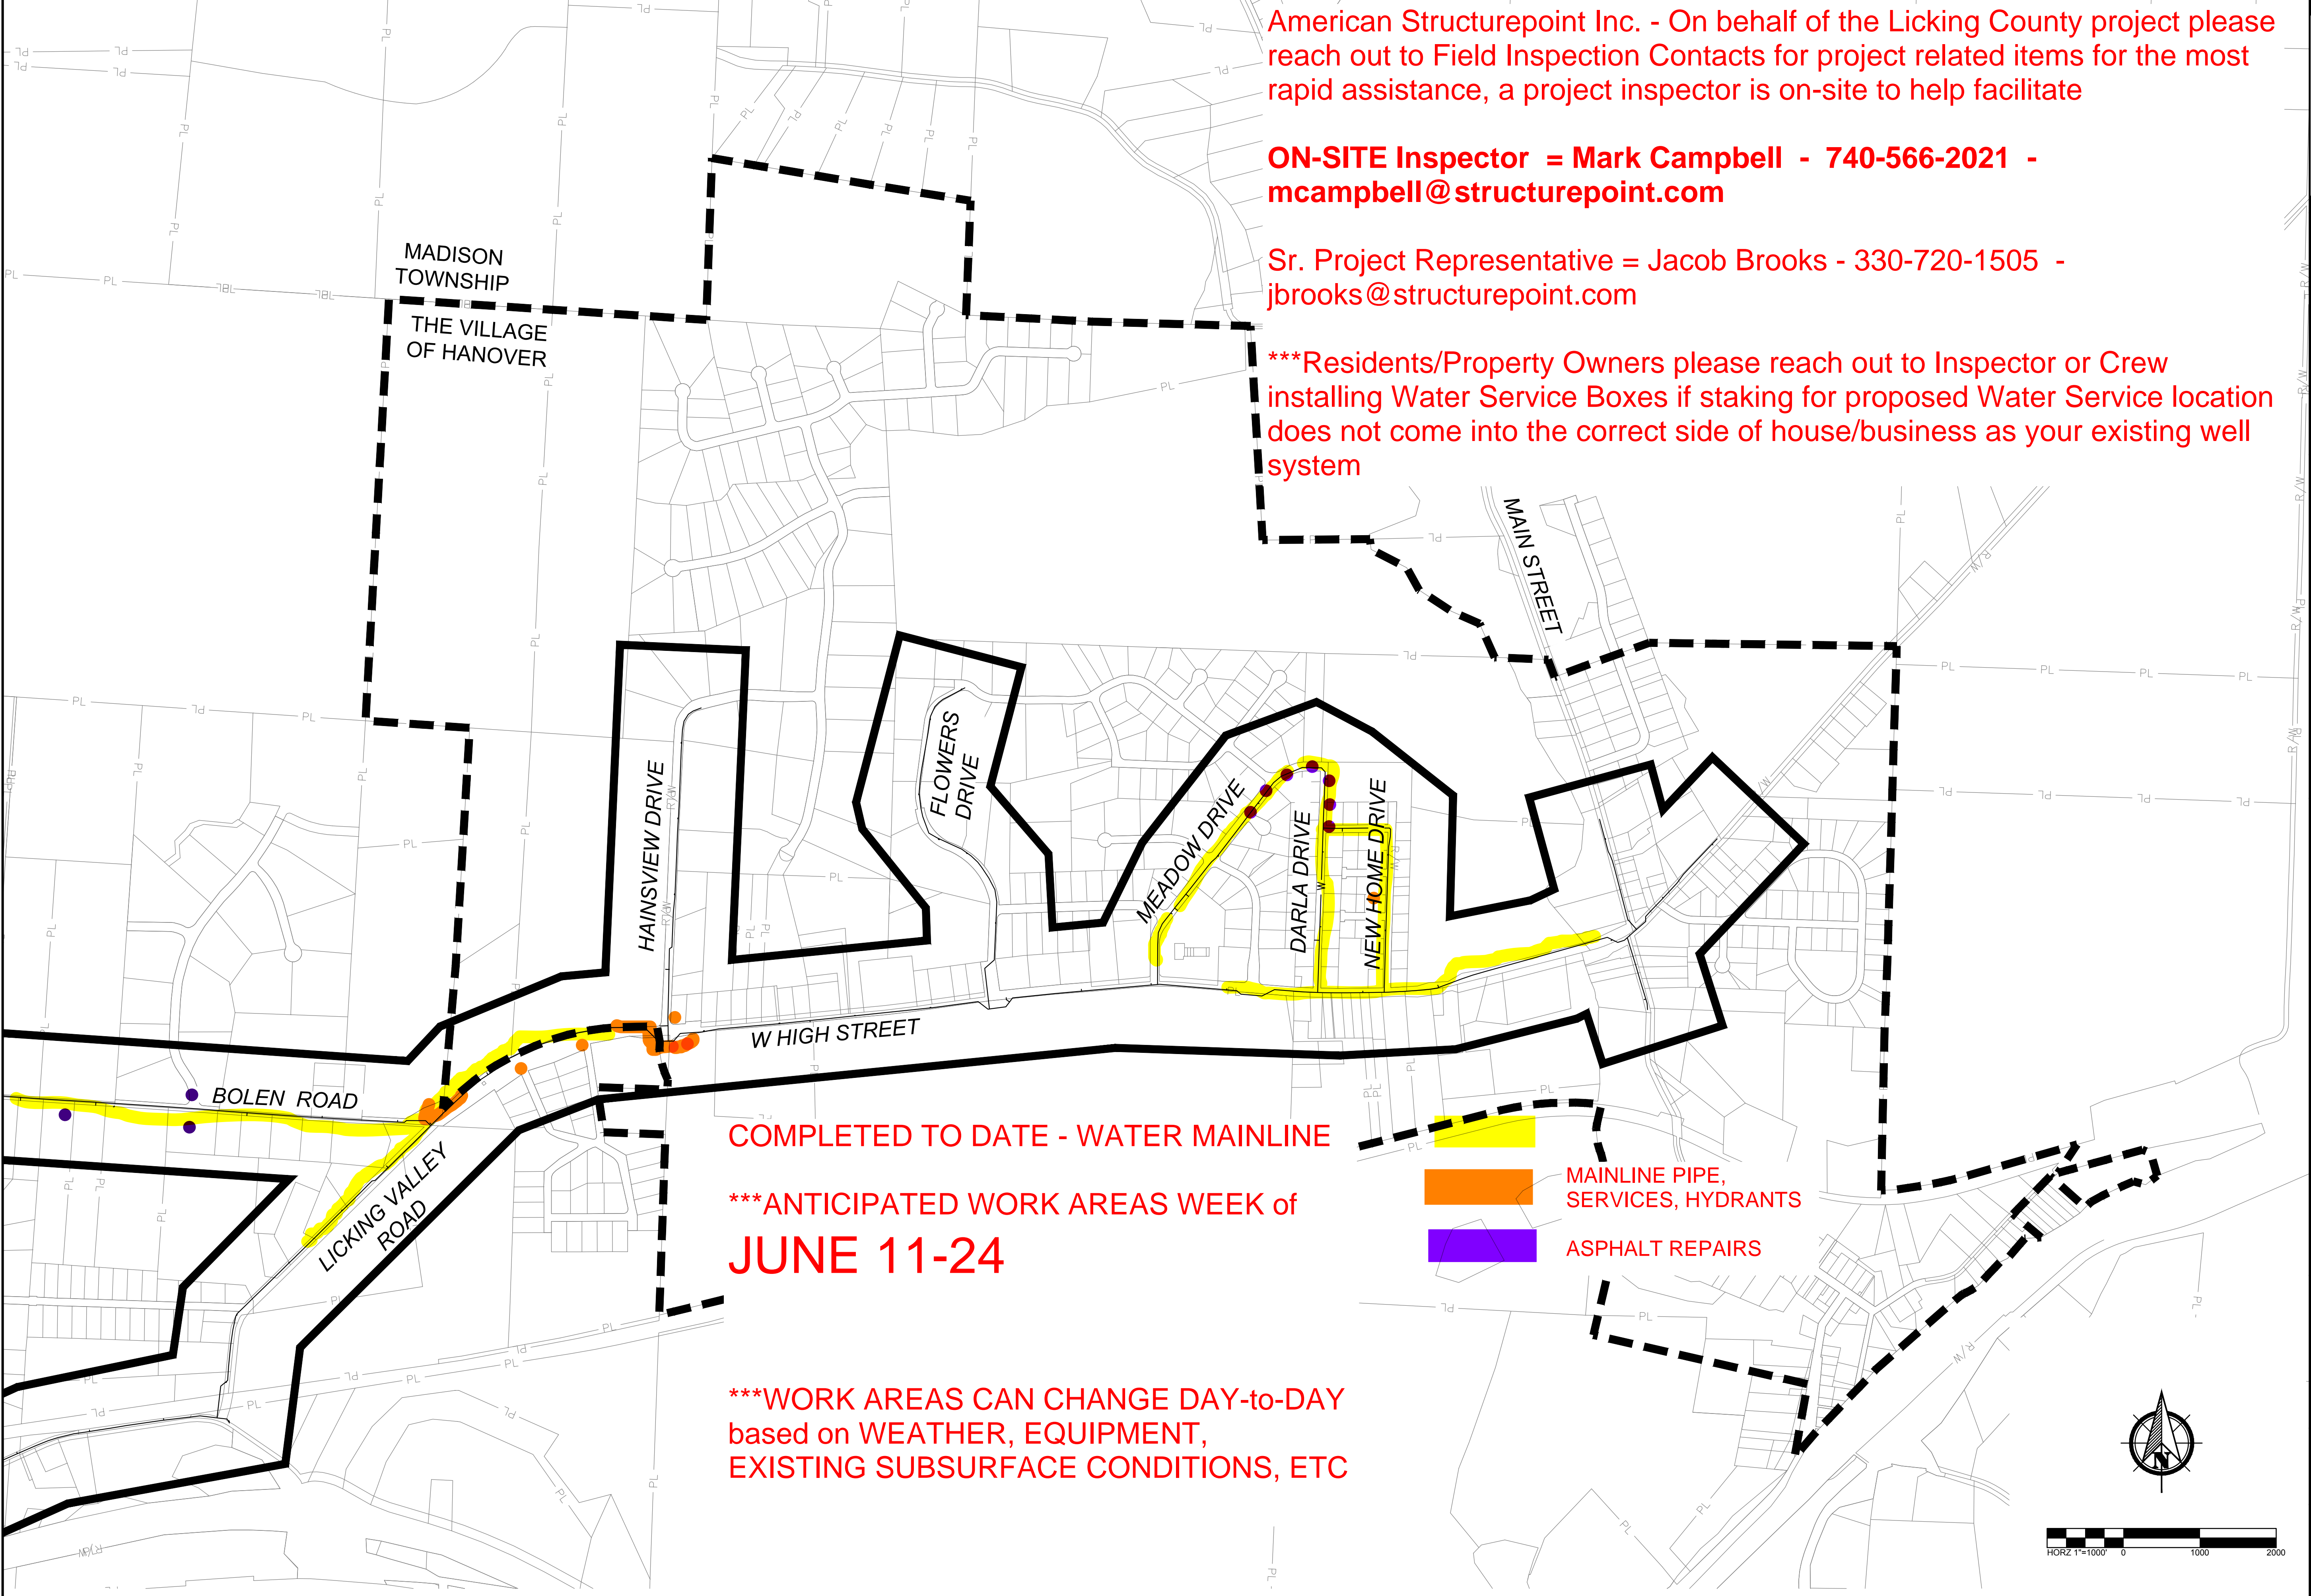

American Structurepoint Inc. - On behalf of the Licking County project please reach out to Field Inspection Contacts for project related items for the most rapid assistance, a project inspector is on-site to help facilitate

ON-SITE Inspector = Mark Campbell - 740-566-2021 - mcampbell@structurepoint.com

Sr. Project Representative = Jacob Brooks - 330-720-1505 - jbrooks@structurepoint.com



***Residents/Property Owners please reach out to Inspector or Crew installing Water Service Boxes if staking for proposed Water Service location does not come into the correct side of house/business as your existing well system

COMPLETED TO DATE - WATER MAINLINE

***ANTICIPATED WORK AREAS WEEK of
JUNE 11-24

***WORK AREAS CAN CHANGE DAY-to-DAY based on WEATHER, EQUIPMENT, EXISTING SUBSURFACE CONDITIONS, ETC

-  MAINLINE PIPE, SERVICES, HYDRANTS
-  MAINLINE PIPE, SERVICES, HYDRANTS
-  ASPHALT REPAIRS



CONSTRUCTION DOCUMENTS
FOR
HANOVER WATER EXTENSION
PHASE 1
CITY OF HANOVER, LICKING COUNTY, OHIO
OVERALL PLAN

| REVISIONS | DATE | SHEET NO. | DESCRIPTION |
|-----------|------|-----------|-------------|
| | | | |
| | | | |
| | | | |
| | | | |

| | |
|-------------|------------|
| DATE: | 5/15/2026 |
| DRAWN BY: | MNA |
| CHECKED BY: | BJM |
| JOB NUMBER: | 2022.03308 |

C100
