



AMERICAN
STRUCTUREPOINT
INC.



LICKING COUNTY, OHIO HANOVER WATERLINE EXTENSION – PHASE 1

Recent Progress – (6-10-26 to 6-17-26)

- 12” mainline trench crew on LICKING VALLEY Rd. completed tie-in from BOLEN Rd. intersection to near area for tie-in to pipe already installed in front of Middle School in late 2025.
- 12” mainline bore crew on MARNE Rd. completed installation crossing from MILLER RANCH Rd. north side of Marne to south side, now installing additional 840 feet of pipe east of Bowling Green Run to FIRST Street.
- Asphalt repair crew on MONTGOMERY Rd. Repairs at Madison, Oakland, Bolen.
- Concrete crew on W HIGH St. began replacing all missing walk panels and curb ahead of June 27th Parade and Fireworks
- 8” Watermain on SWANS has PASSED pressure testing and up to BOLEN Rd at Jin Joe Drive.

Week Look Ahead – (6-18-26 to 6-27-26)

- **Miller Pipeline Pavement Repair Crew**
 - Will have all stone or cold patch areas on W HIGH St. and LICKING VALLEY Rd. repaired with full asphalt ahead of June 27th festivities.
- **12” Mainline crew on LICKING VALLEY RD.** bore from NW side of Hainsview intersection to SW side. Then trench across driveway to Primary School. Then bore under W HIGH to go up E side of Hainsview. Goal is to bore under LV Rd./W High and avoid open trench on the main thoroughfare.
- **12” Mainline Crew on MARNE** continue boring and installs eastward from First Street, past Montgomery and toward Licking Valley Rd.
- **Flushing/Testing on BOLEN Rd. from Jin Joe eastward near 9,000 feet to reach LV Rd.**

Traffic Impacts. WORK HOURS can range from 7am – 7pm

1. Licking Valley Rd. = Mainline installs will have 1-lane, 2-way traffic with flaggers
2. Marne = Mainline installs will have 1-lane, 2-way traffic with flaggers
3. W High / LV Rd. = Asphalt and Concrete repair work 1-lane, 2-way traffic with flaggers

Approximate project complete: Near 82% calendar, 63.0% of pipe installation

***American Structurepoint Inc. - On behalf of the Licking County project please reach out to Field Inspection Contacts for project related items for the most rapid assistance, a project inspector is on-site to help facilitate, including concerns within Village and Township areas, please reach out as needed.

ON-SITE Inspector = Mark Campbell - 740-566-2021 - mcampbell@structurepoint.com

Sr. Project Representative = Jacob Brooks - 330-720-1505 - jbrooks@structurepoint.com

***Residents/Property Owners please reach out to Inspector or Crew installing Water Service Boxes if staking for proposed Water Service location does not come into the correct side of house/business as your existing well system

LICKING VALLEY Rd. 12" watermain trench installation from BOLEN Rd.

-Bolen Rd. access ROAD CLOSED parts of 2-days, work hours only, for pipe install.

*Expect another parts of 2-workday next week for Asphalt Repairs through intersection.



MARNE Rd. 12" watermain bore installation on S side of street



Asphalt Repairs MONTGOMERY at BOLEN intersection



Concrete walk and curb replaced on W HIGH Street



Restoration, grading and topsoil follow up on SWANS Rd.



Pressure (Hydrostatic) Testing setup on BOLEN Rd.



Reason for pressure testing, to find any problem area, bad joint found and repaired on SWANS



BOLEN Rd. flushing of all hydrants to remove any debris and air pockets



Letting a higher elevation hydrant flush on the section to remove extra air.





AMERICAN
STRUCTUREPOINT
INC.



2550 Corporate Exchange Ct., Ste. 400 | Columbus, Ohio 43221
TEL: 614.779.1226
www.structurepoint.com

CONSTRUCTION DOCUMENTS
FOR
HANOVER WATER EXTENSION
PHASE 1
CITY OF HANOVER, LICKING COUNTY, OHIO
OVERALL PLAN

DESCRIPTION


SHEET NO.

DATE

REVISIONS

DATE:	5/15/2026
DRAWN BY:	MNA
CHECKED BY:	BJM
JOB NUMBER:	2022.03308

C100

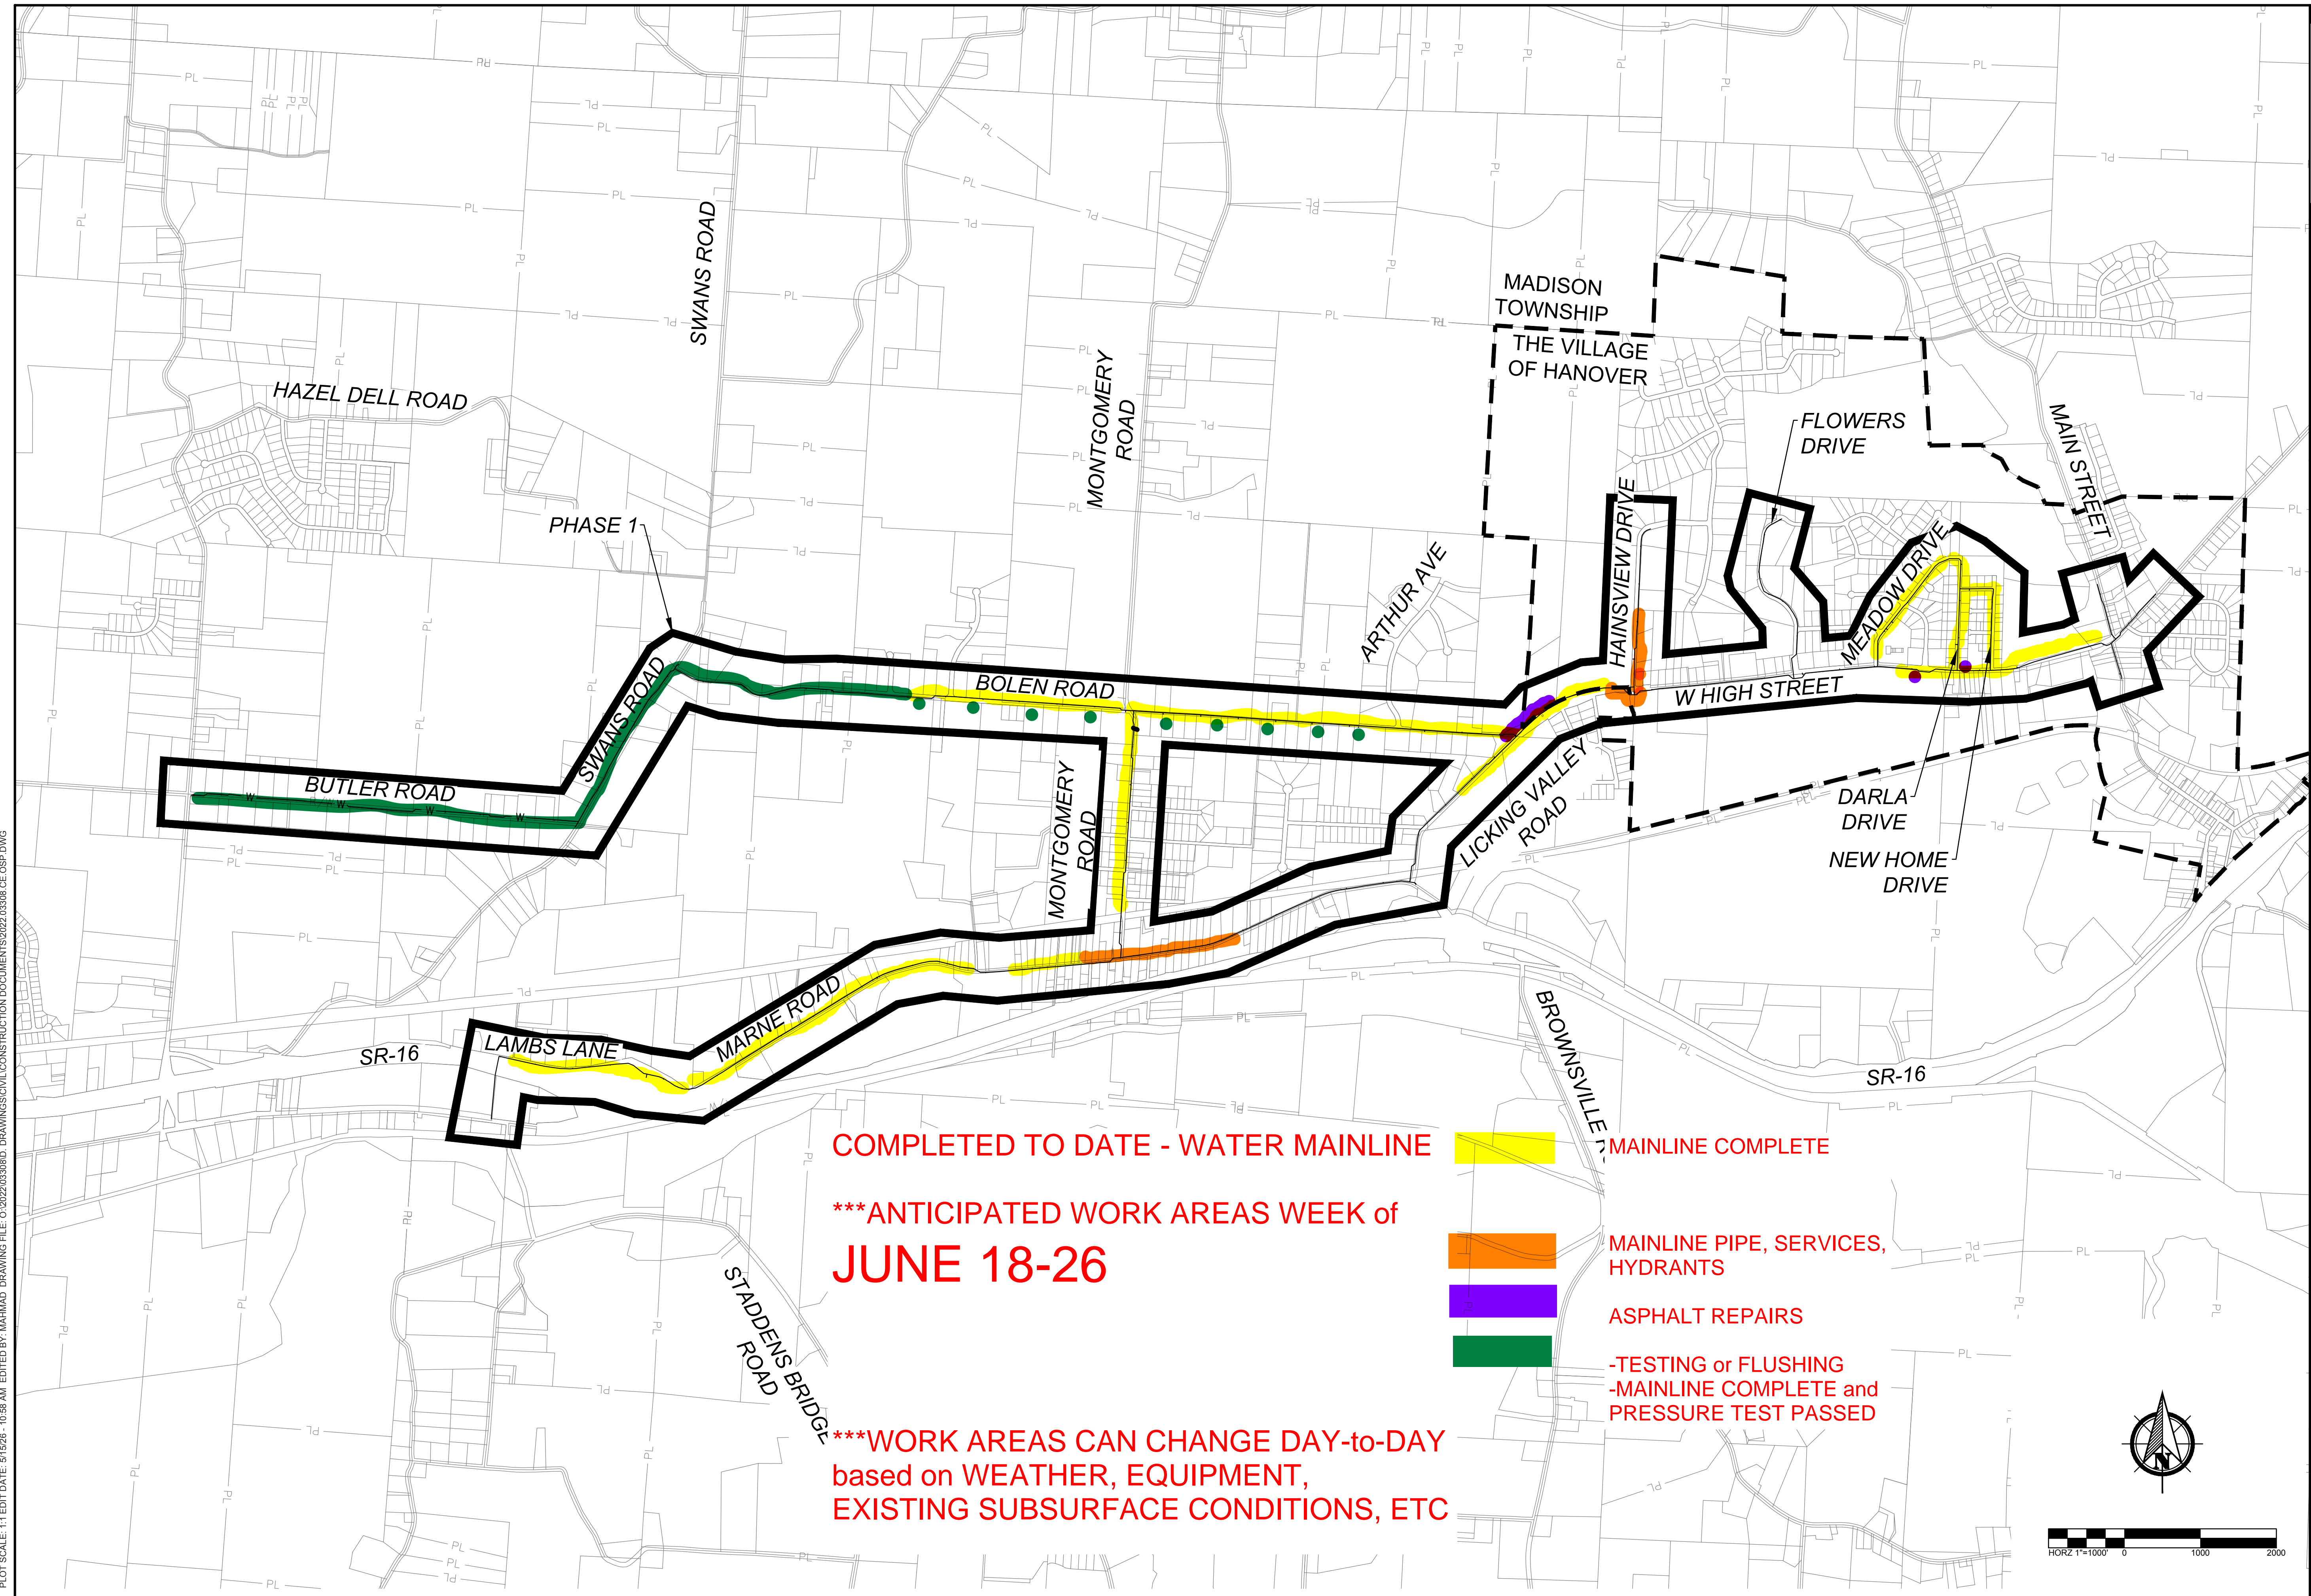

COMPLETED TO DATE - WATER MAINLINE

*****ANTICIPATED WORK AREAS WEEK of JUNE 18-26**


*****WORK AREAS CAN CHANGE DAY-to-DAY based on WEATHER, EQUIPMENT, EXISTING SUBSURFACE CONDITIONS, ETC**

MAINLINE COMPLETE

MAINLINE PIPE, SERVICES, HYDRANTS


ASPHALT REPAIRS

-TESTING or FLUSHING
-MAINLINE COMPLETE and PRESSURE TEST PASSED



PLOT SCALE: 1:1 EDIT DATE: 5/15/26 - 10:58 AM EDITED BY: MAHMOUD DRAWING FILE: C:\2022\03308.D DRAWINGS\CIVIL\CONSTRUCTION\DOCUMENTS\2022.03308_CE_CSP.DWG

PLOT SCALE: 1:1 EDIT DATE: 5/15/26 - 11:00 AM EDITED BY: MAHMOUD DRAWING FILE: C:\2022\03308D DRAWINGS\CIVIL\CONSTRUCTION\DOCUMENTS\ARCHIVE\2026-05-15\2022.03308D.CE.OSPV.DWG

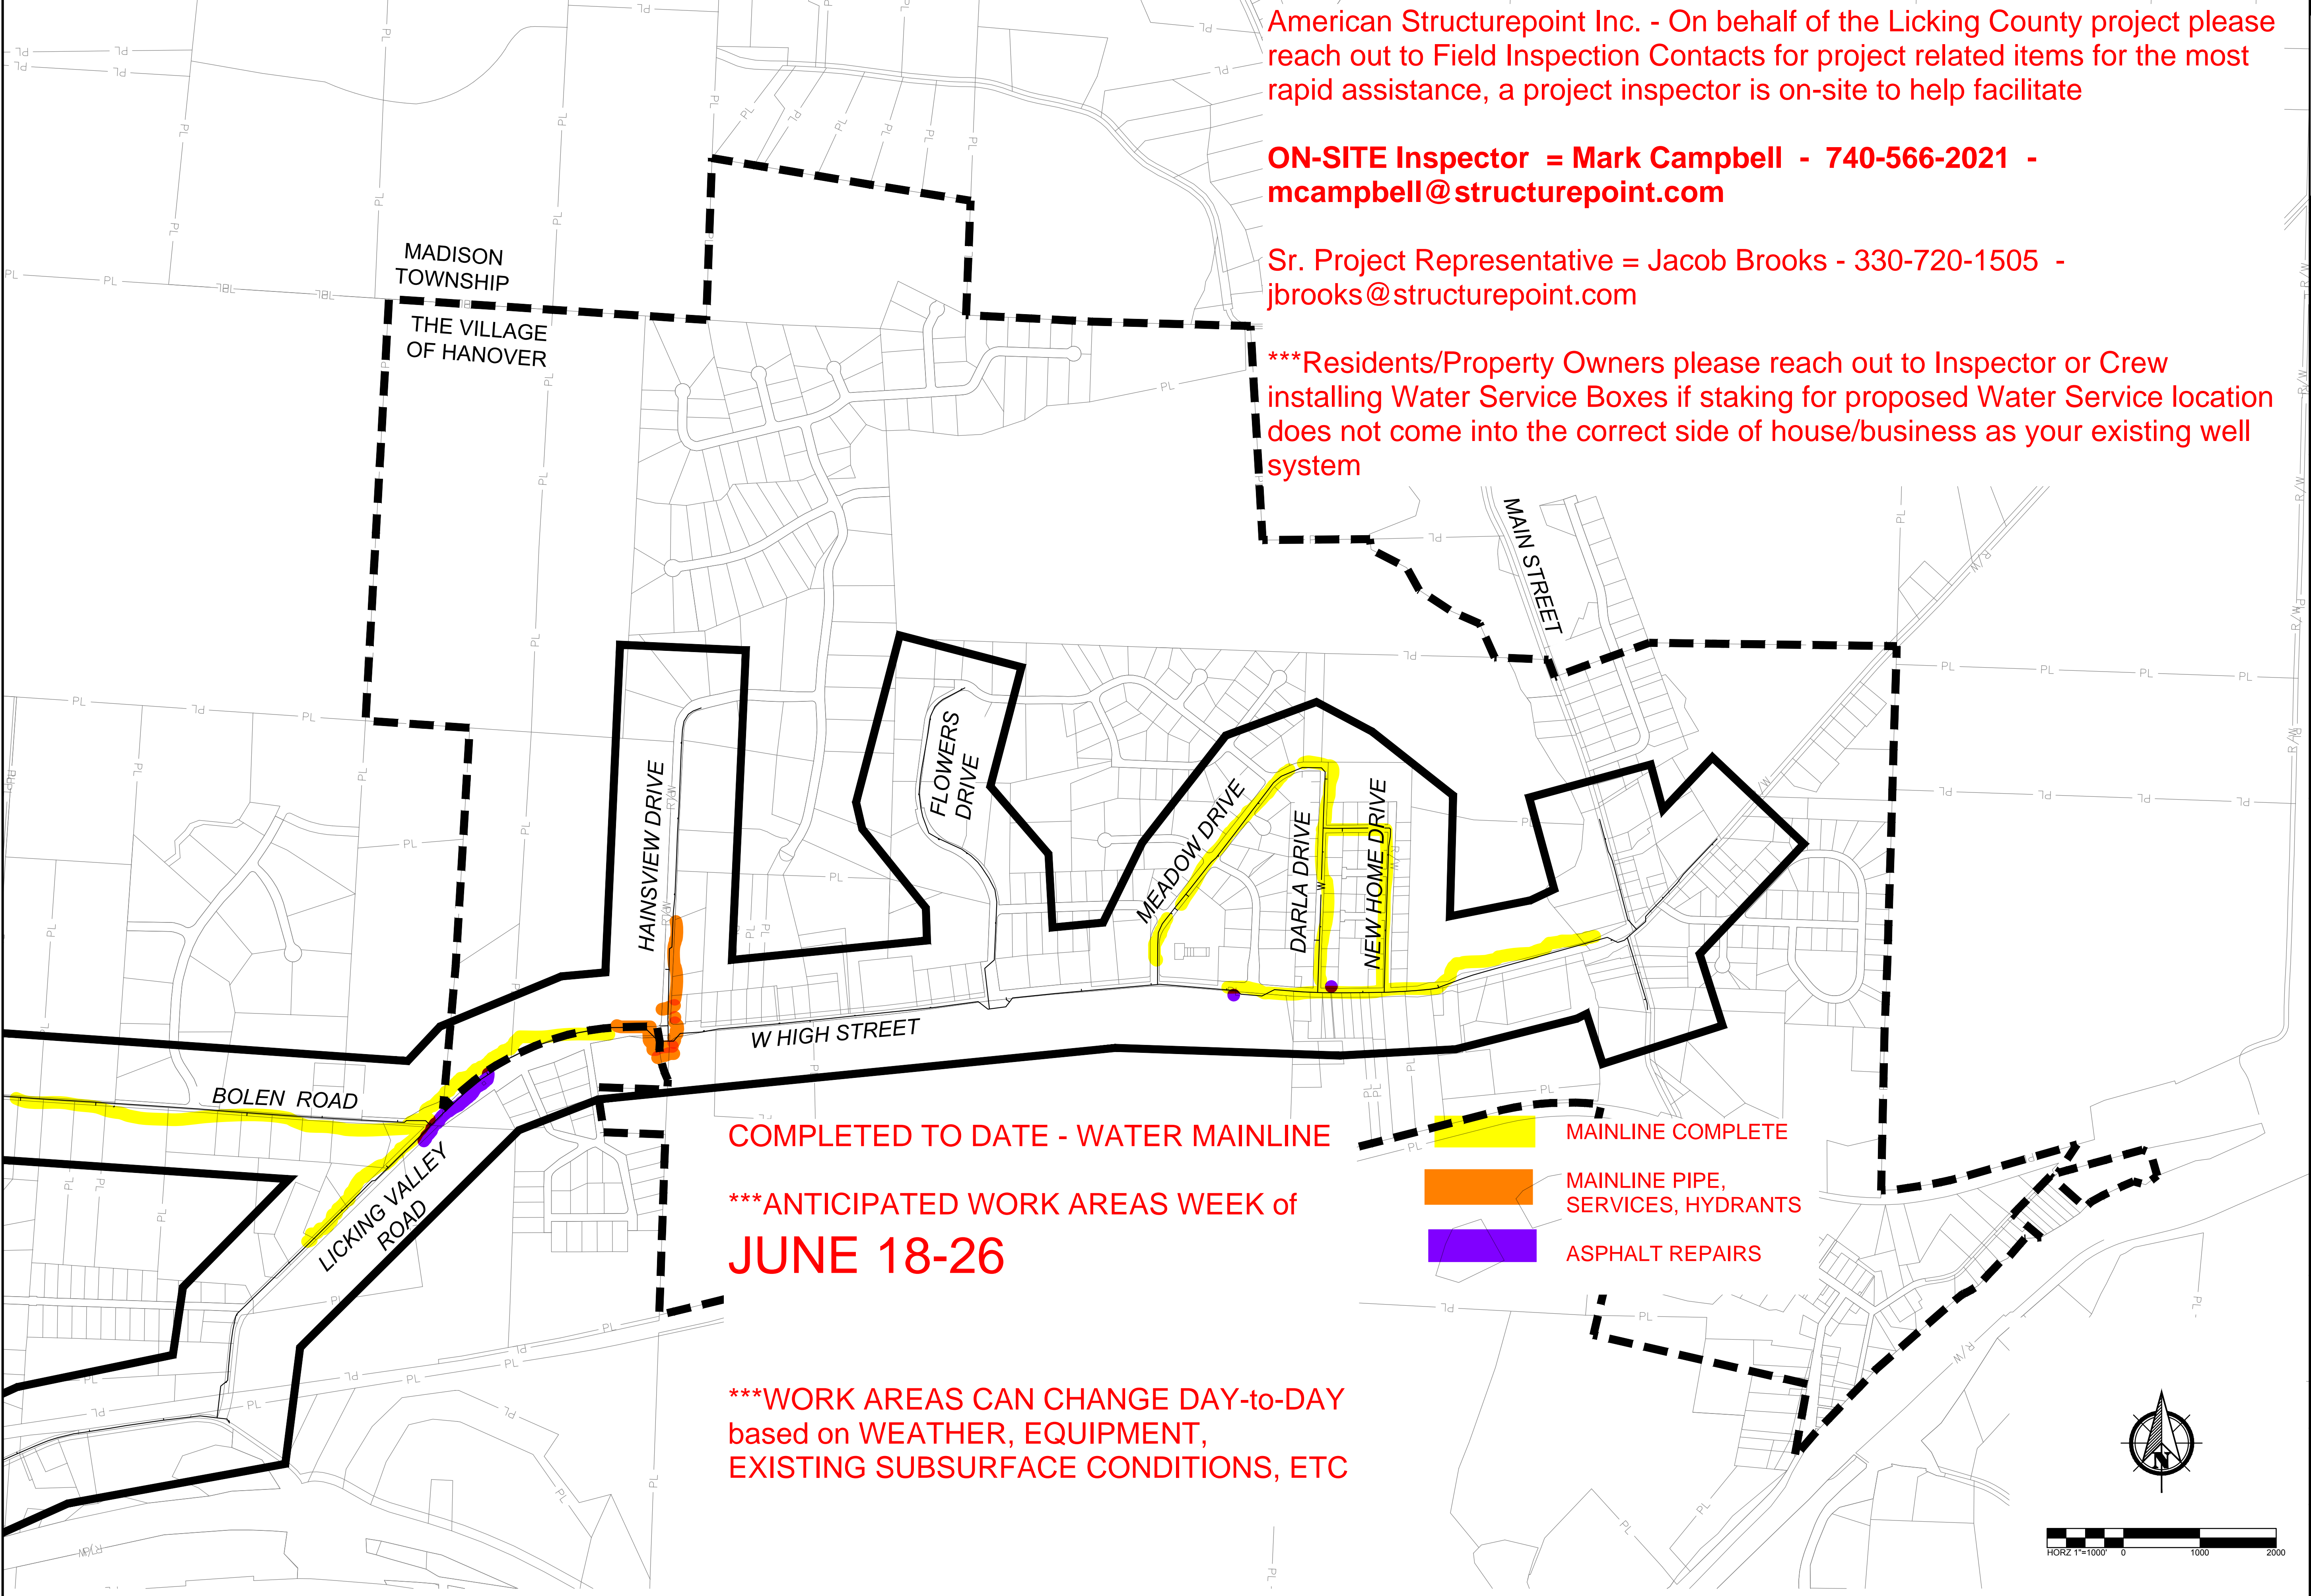

American Structurepoint Inc. - On behalf of the Licking County project please reach out to Field Inspection Contacts for project related items for the most rapid assistance, a project inspector is on-site to help facilitate

ON-SITE Inspector = Mark Campbell - 740-566-2021 - mcampbell@structurepoint.com

Sr. Project Representative = Jacob Brooks - 330-720-1505 - jbrooks@structurepoint.com



***Residents/Property Owners please reach out to Inspector or Crew installing Water Service Boxes if staking for proposed Water Service location does not come into the correct side of house/business as your existing well system

COMPLETED TO DATE - WATER MAINLINE

***ANTICIPATED WORK AREAS WEEK OF
JUNE 18-26

***WORK AREAS CAN CHANGE DAY-to-DAY based on WEATHER, EQUIPMENT, EXISTING SUBSURFACE CONDITIONS, ETC

-  MAINLINE COMPLETE
-  MAINLINE PIPE, SERVICES, HYDRANTS
-  ASPHALT REPAIRS



CONSTRUCTION DOCUMENTS
FOR
HANOVER WATER EXTENSION
PHASE 1
CITY OF HANOVER, LICKING COUNTY, OHIO
OVERALL PLAN

REVISIONS	DATE	SHEET NO.	DESCRIPTION

DATE: 5/15/2026
DRAWN BY: MNA
CHECKED BY: BJM
JOB NUMBER: 2022.03308

C100
