



AMERICAN
STRUCTUREPOINT
INC.



LICKING COUNTY, OHIO HANOVER WATERLINE EXTENSION – PHASE 1

Recent Progress – (6-22-26 to 7-02-26)

- 12” mainline trench crew on LICKING VALLEY Rd. at HAINSVIEW.
-Completed portion of watermain within the pavement of HAINSVIEW.
-Crossed along South side of intersection @ Primary School entrance and continue installing mainline Eastward on the South side of W HIGH ST. Completing water services and hydrants as they go.
- 12” mainline bore crew on MARNE Rd. completed installation crossing MONTGOMERY Rd. from South side of Marne now installing on the North side of Marne, installed to near across street from Panthers Storage (12886 Marne). Second service tap and hydrant crew working behind them.
- Asphalt repair crew at Licking Valley Rd. & Bolen completed remaining pavement repairs; until resurfacing asphalt and re-striping of pavement marks occurs later in season.
- 8” Watermain on BOLEN pre-testing on both west side and east of Montgomery and a couple repair locations located to be remedied next week.

▪ **Happy 250th Birthday America!**

Week Look Ahead – (7-06-26 to 7-11-26)

*****NO CREWS WORKING July 3-5**

- **Miller Pipeline Pavement Repair Crew**
 - MISC locations and continue northward on DARLA
- **12” Mainline crew on W HIGH ST.** installing on South side of street not in pavement
- **12” Mainline Crew on MARNE** continue boring and installs eastward toward Licking Valley Rd. intersection
- **Flushing/Testing on BOLEN Rd. from Jin Joe eastward near 9,000 feet to reach LV Rd.** Identified a couple repairs that will be made to hold pressure appropriately.

Traffic Impacts. WORK HOURS can range from 7am – 7pm

1. W HIGH St. = Mainline installs will have 1-lane, 2-way traffic with flaggers
2. Marne Rd. = Mainline installs will have 1-lane, 2-way traffic with flaggers
3. MISC township or Darla = Asphalt crew, proceed around local street work zone with caution

Approximate project complete: Near 85% calendar, 68.0% of pipe installation

***American Structurepoint Inc. - On behalf of the Licking County project please reach out to Field Inspection Contacts for project related items for the most rapid assistance, a project inspector is on-site to help facilitate, including concerns within Village and Township areas, please reach out as needed.

ON-SITE Inspector = Mark Campbell - 740-566-2021 - mcampbell@structurepoint.com

Sr. Project Representative = Jacob Brooks - 330-720-1505 - jbrooks@structurepoint.com

*****Residents/Property Owners please reach out to Inspector or Crew installing Water Service Boxes if staking for proposed Water Service location does not come into the correct side of house/business as your existing well system*****

Assembling vertical and combination bends on 12" c900 certa-lok pipe. Mega-lug mechanical joints and all-thread for additional top vertical bend restraint



Looking North at HAINSVIEW watermain tee into W HIGH ST. watermain (on the SE side of the intersection in the Primary School drive)



Looking West at 12" watermain that will go under located electric and communication conduits to Primary School



Pavement repair made on W HIGH Street in front of Legacy Park day before Hanover Boom



Pavement repairs on Licking Valley Rd. last full week of June. Rough grading along school frontage complete and erosion controls in place ready for seed and straw stabilization



American Structurepoint inspection testing compaction for County roadway.



Trench excavation continues on South side of W HIGH St. to the East. (toward village center).
Project working with utilities as proceeding. Determined that unmarked damaged conduit in
photo was abandoned in place previously





AMERICAN
STRUCTUREPOINT
INC.



2550 Corporate Exchange Ct., Ste. 400 | Columbus, Ohio 43221
TEL: 614.722.2226
www.structurepoint.com

CONSTRUCTION DOCUMENTS
FOR
HANOVER WATER EXTENSION
PHASE 1
CITY OF HANOVER, LICKING COUNTY, OHIO
OVERALL PLAN

DESCRIPTION

SHEET NO.

DATE

REVISIONS


DATE

DRAWN BY:

CHECKED BY:

JOB NUMBER:

C100

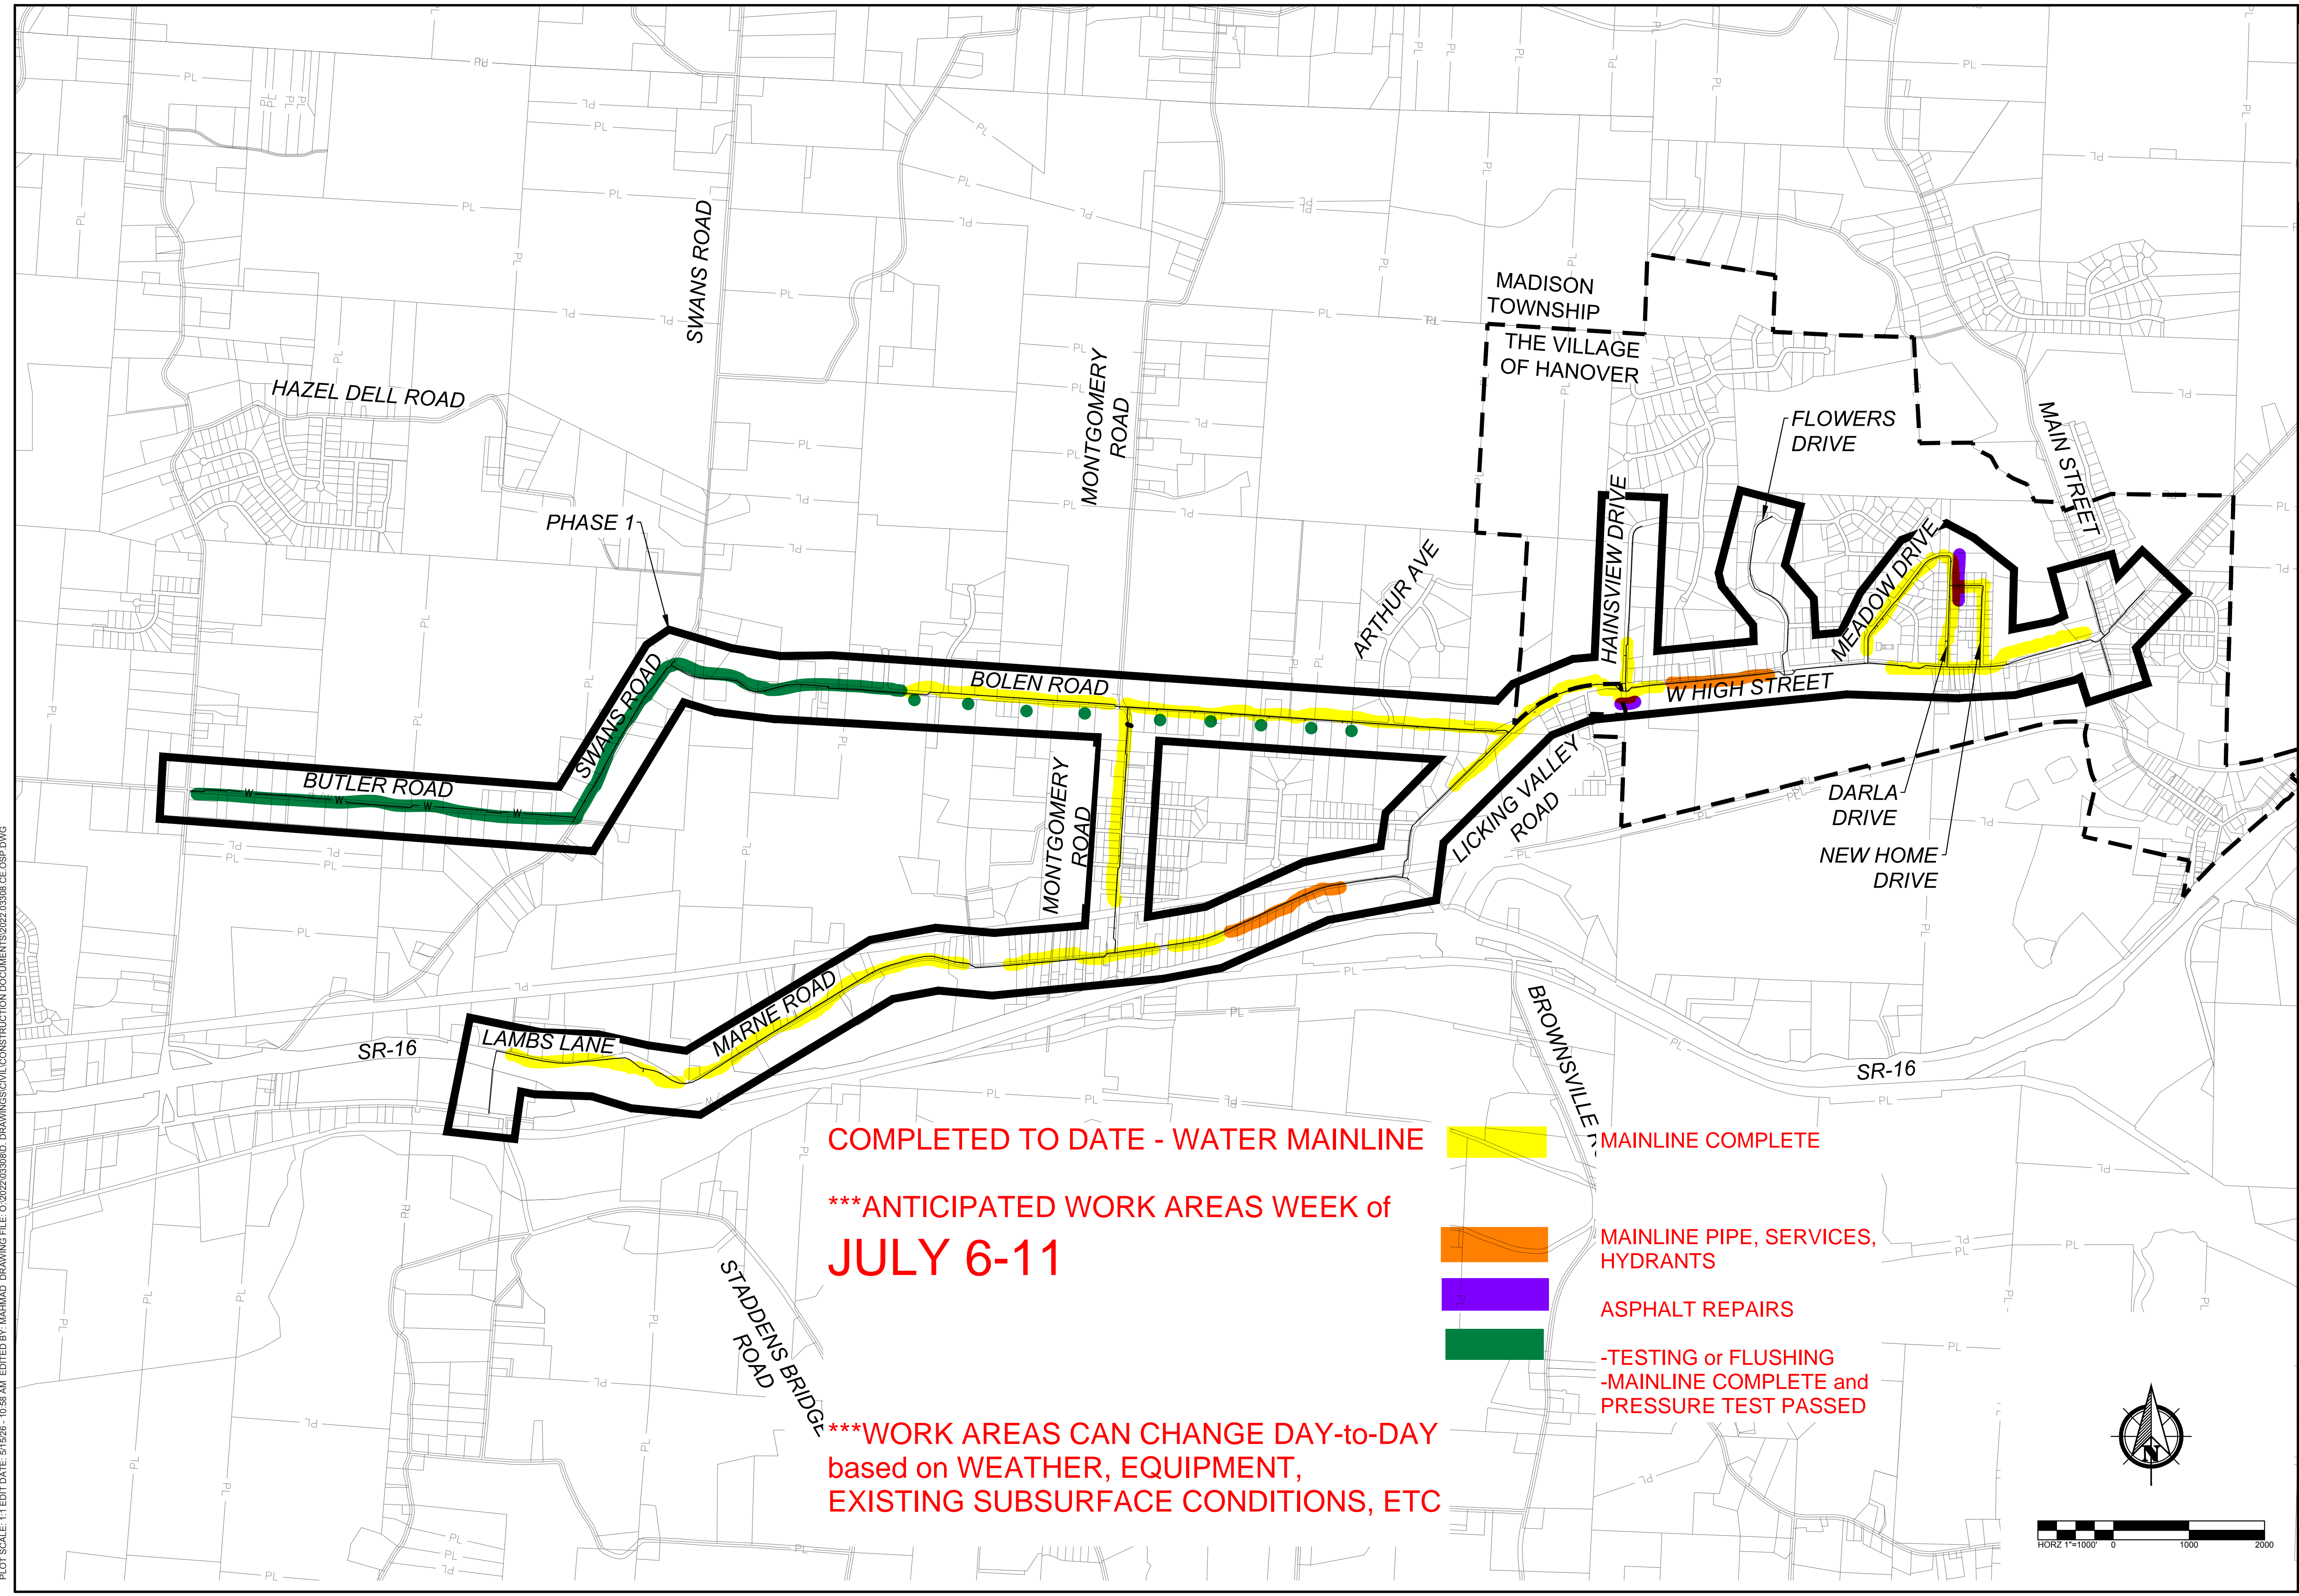

COMPLETED TO DATE - WATER MAINLINE

*****ANTICIPATED WORK AREAS WEEK of
JULY 6-11**


*****WORK AREAS CAN CHANGE DAY-to-DAY
based on WEATHER, EQUIPMENT,
EXISTING SUBSURFACE CONDITIONS, ETC**

MAINLINE COMPLETE

MAINLINE PIPE, SERVICES,
HYDRANTS


ASPHALT REPAIRS

-TESTING or FLUSHING
-MAINLINE COMPLETE and
PRESSURE TEST PASSED



PLOT SCALE: 1:1 EDIT DATE: 5/15/26 - 10:58 AM EDITED BY: MAHMOUD DRAWING FILE: C:\2022\03\308.D DRAWINGS\CIVIL\CONSTRUCTION\DOCUMENTS\2022\03\308_CE_CSP.DWG

PLOT SCALE: 1"=100' DATE: 5/15/26 - 11:00 AM EDITED BY: MAHMOUD DRAWING FILE: C:\2022\03308D DRAWINGS\CIVIL\CONSTRUCTION\DOCUMENTS\ARCHIVE\2026-05-15\2022.03308D.CE.OSPV.DWG

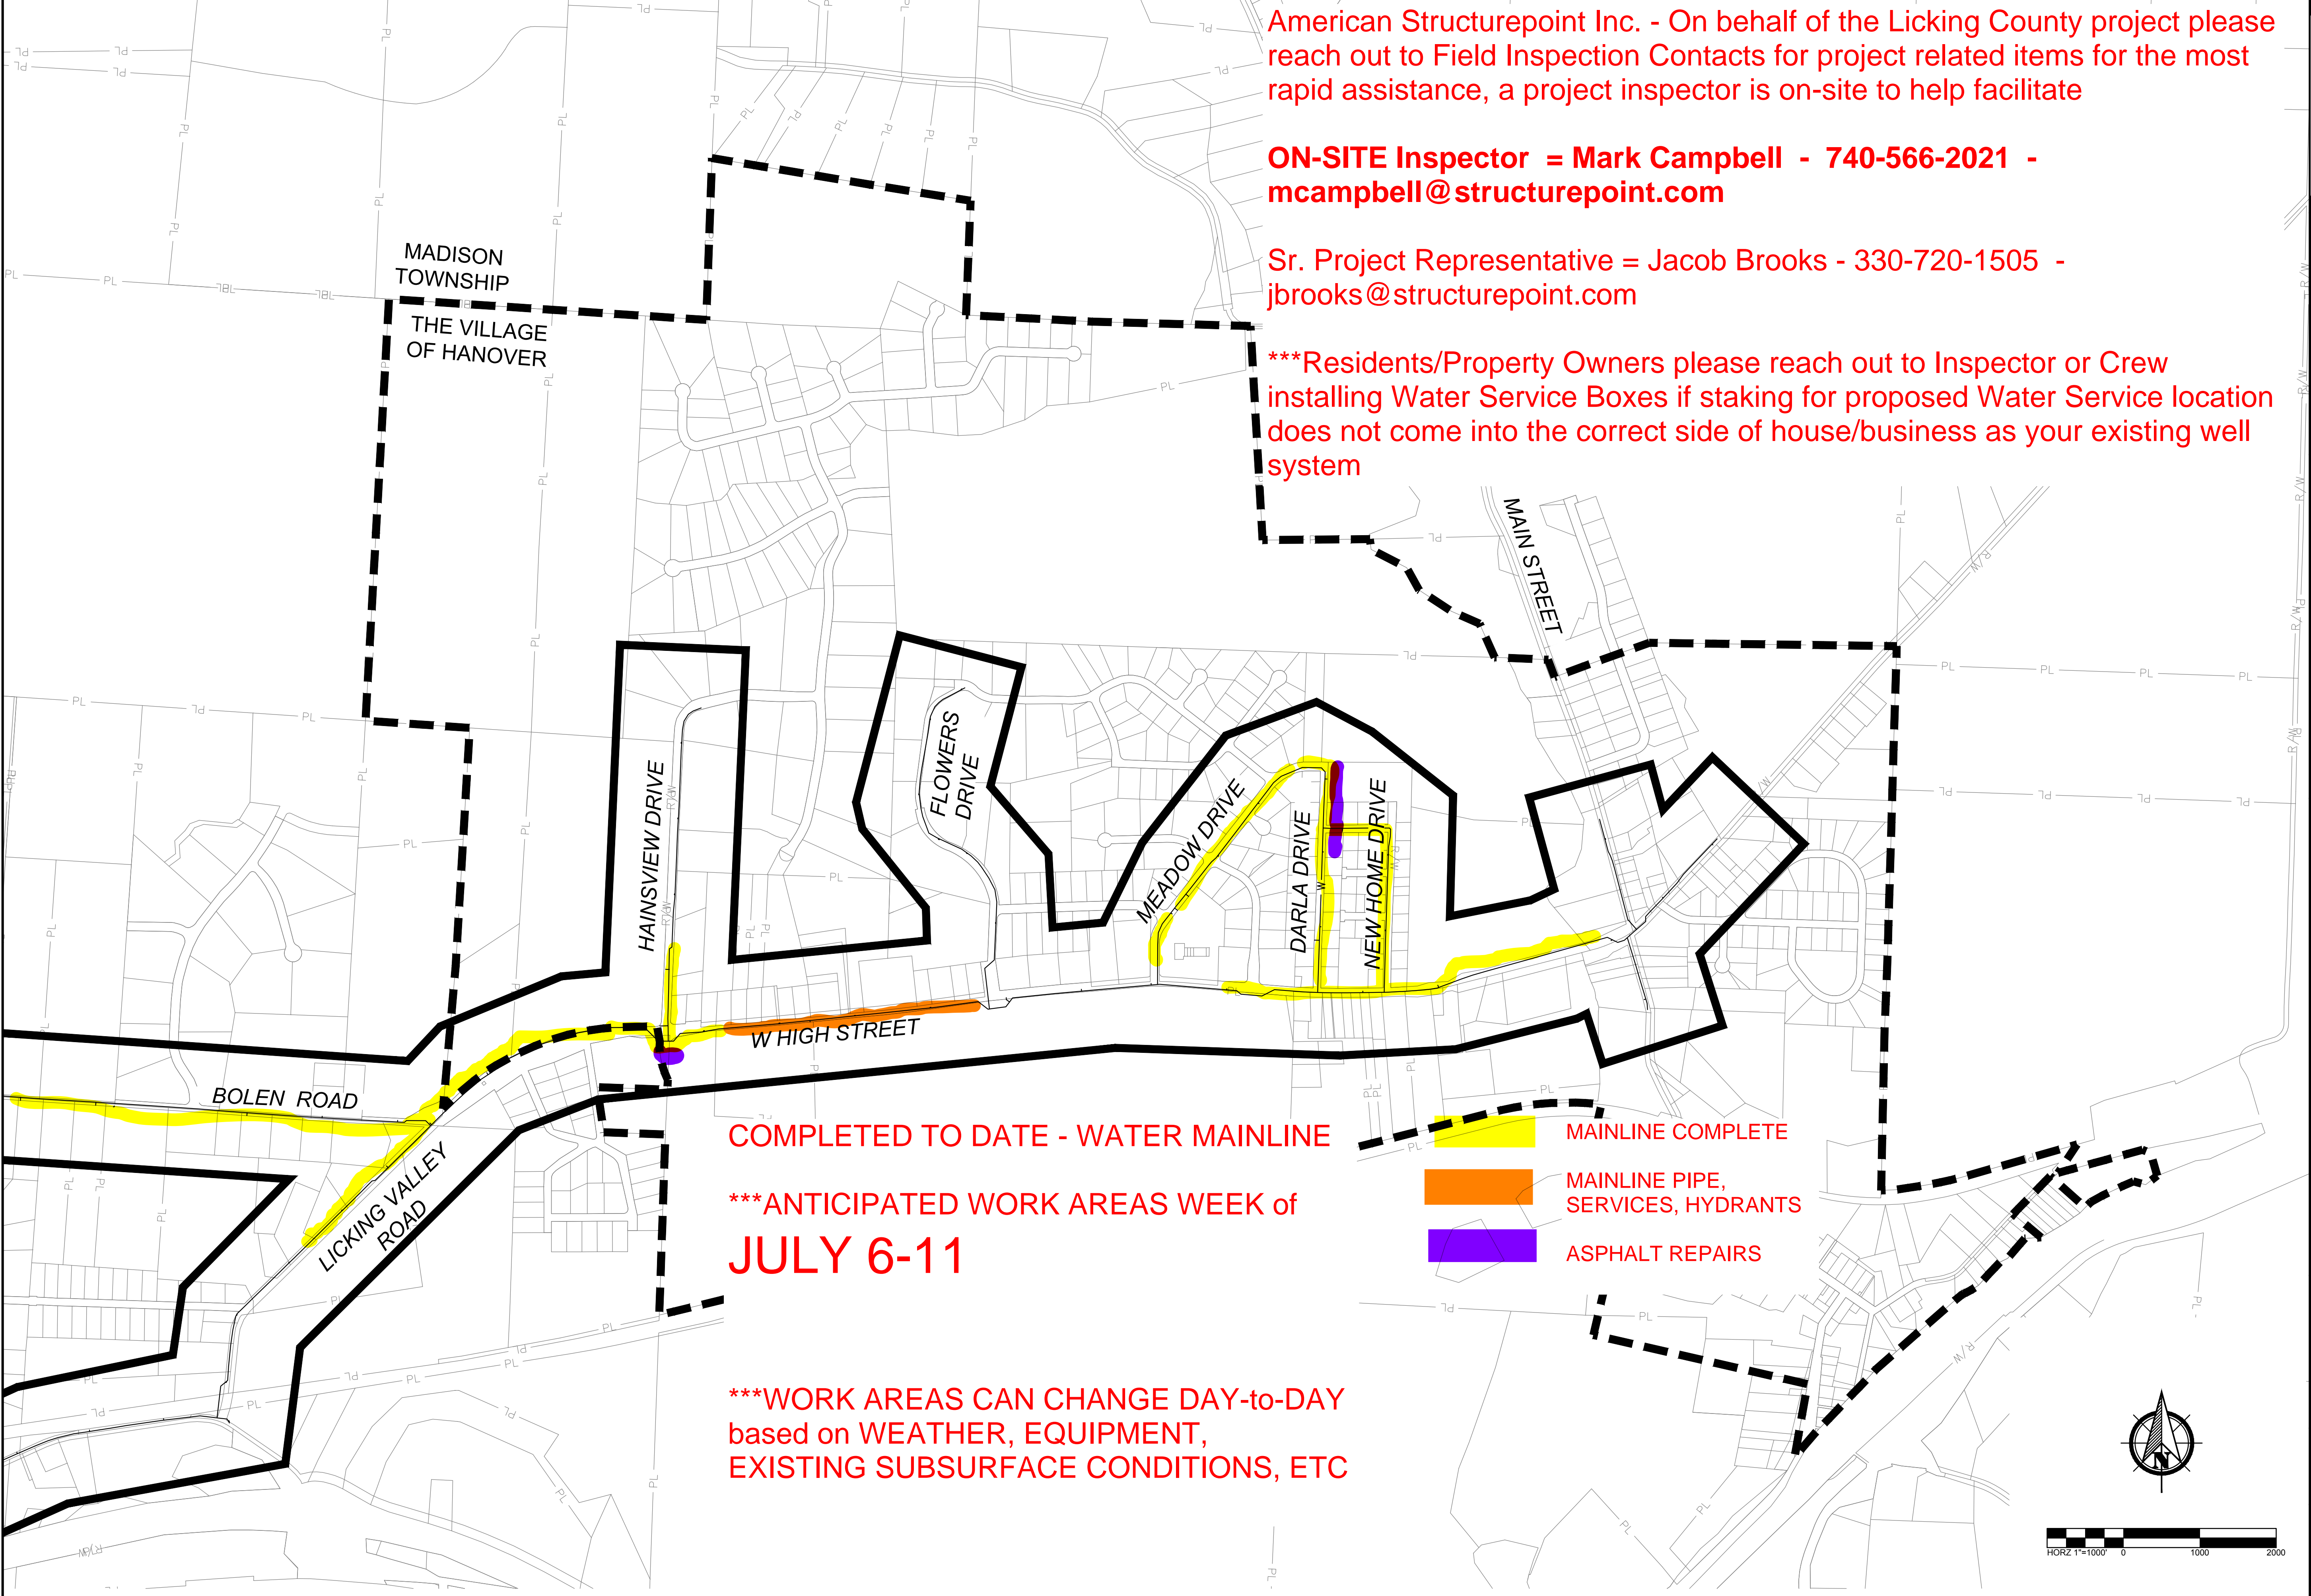

American Structurepoint Inc. - On behalf of the Licking County project please reach out to Field Inspection Contacts for project related items for the most rapid assistance, a project inspector is on-site to help facilitate

ON-SITE Inspector = Mark Campbell - 740-566-2021 - mcampbell@structurepoint.com

Sr. Project Representative = Jacob Brooks - 330-720-1505 - jbrooks@structurepoint.com



*****Residents/Property Owners please reach out to Inspector or Crew installing Water Service Boxes if staking for proposed Water Service location does not come into the correct side of house/business as your existing well system**

COMPLETED TO DATE - WATER MAINLINE

*****ANTICIPATED WORK AREAS WEEK OF JULY 6-11**

*****WORK AREAS CAN CHANGE DAY-to-DAY based on WEATHER, EQUIPMENT, EXISTING SUBSURFACE CONDITIONS, ETC**

- MAINLINE COMPLETE
- MAINLINE PIPE, SERVICES, HYDRANTS
- ASPHALT REPAIRS

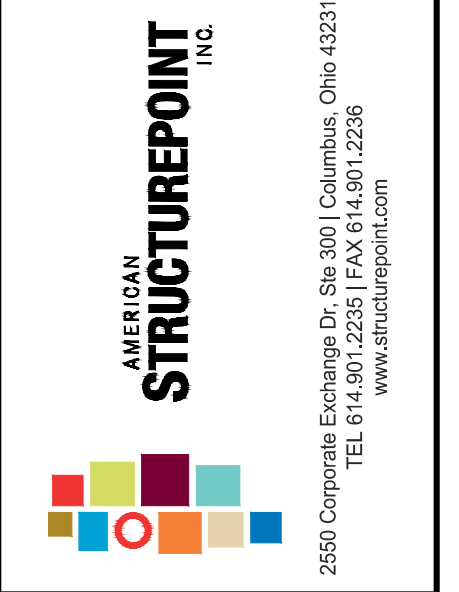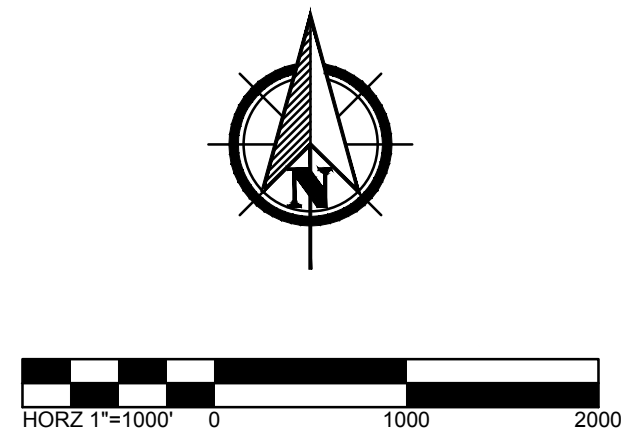

CONSTRUCTION DOCUMENTS
HANOVER WATER EXTENSION
PHASE 1
 CITY OF HANOVER, LICKING COUNTY, OHIO
OVERALL PLAN

REVISIONS	DATE	SHEET NO.	DESCRIPTION

DATE:	5/15/2026
DRAWN BY:	MNA
CHECKED BY:	BJM
JOB NUMBER:	2022.03308

C100
