



AMERICAN
STRUCTUREPOINT
INC.



LICKING COUNTY, OHIO HANOVER WATERLINE EXTENSION – PHASE 1

Recent Progress – (7-06-26 to 7-18-26)

- **12” mainline trench crew on W HIGH ST.** Installed from E of HAINSVIEW to E of FLOWERS.
-Installed crossing under W High for first portion going up Flowers
- **12” mainline bore crew on MARNE Rd.** completed installations on MARNE Rd. while jumping over two waterway crossings bores and arriving at LICKING VALLEY RD. intersection.
- **Asphalt repair crew** on N end of Meadow and began HAINSVIEW, N of flashing signalized intersection
- **8” Watermain pressure testing** on BOLEN and MONTGOMERY completed, except on section needing a repair near Bolen & Arthur Ave.

Week Look Ahead – (7-20-26 to 8-01-26)

- **Miller Pipeline Pavement Repair Crew**
 - Complete HAINSVIEW pavement repairs, then resume on MEADOW
- **12” Mainline Crew on W HIGH ST.** Complete installations of mainline, services, and hydrants on W HIGH to tie-in to previous stop point in front of Legacy Park.
THEN complete open-trench crossing across W HIGH at MEADOW
- **12” Mainline Crew on LICKING VALLEY RD.** on N side of railroad tracks boring up the W side of the street to tie-in to previous stop point at bottom of hill from Bolen intersection.
- **Flushing/Testing on LICKING VALLEY RD.** One section on BOLEN Rd. needs a repair to finish testing on Bolen.
- **Begin pushing chlorine from Dayton/Butler meter vault up Butler, up Swans, and to furthest pressure tested end of Bolen and Montgomery to prepare for potable water testing by County.**
- Casing pipes now on site for SR-16 and two Railroad crossings (at LV Rd. and Montgomery Rd). Jack-bore crew could be scheduled anytime to begin these activities.

Traffic Impacts. WORK HOURS can range from 7am – 7pm

1. W HIGH St. = Mainline installs will have 1-lane, 2-way traffic with flaggers
 - a. TEMPORARY Work-Hour CLOSURE at W High & MEADOWS intersection
2. LICKING VALLEY Rd. = Mainline installs will have 1-lane, 2-way traffic with flaggers
 - a. AUTOMATED SIGNAL in use for Work Zone between Valley Drive & Bolen
3. HAINVIEW = Asphalt crew will have 1-lane, 2-way traffic with flaggers

Approx. project progress: 75% calendar (164 days of 639 days), 70.0% of pipe installed

***American Structurepoint Inc. - On behalf of the Licking County project please reach out to Field Inspection Contacts for project related items for the most rapid assistance, a project inspector is on-site to help facilitate, including concerns within Village and Township areas, please reach out as needed.

ON-SITE Inspector = Mark Campbell - 740-566-2021 - mcampbell@structurepoint.com

Sr. Project Representative = Jacob Brooks - 330-720-1505 - jbrooks@structurepoint.com

*****Residents/Property Owners please reach out to Inspector or Crew installing Water Service Boxes if staking for proposed Water Service location does not come into the correct side of house/business as your existing well system*****

MARNE mainline crew reaching intersection at Licking Valley Rd.



Mainline installs along S side of W HIGH Street, and services and hydrants



Combination of bore and trench methods for installs on W HIGH Street




Pavement replacement preparation on HAINSVIEW looking North



MONTGOMERY Road flush and pressure testing N side of railroad



PLOT SCALE: 1"=100' DATE: 5/15/26 - 10:59 AM EDITED BY: MAHMOUD DRAWING FILE: C:\2022\03\308D_DRAININGS\CIVIL\CONSTRUCTION DOCUMENTS\2022.03308 CE.CSP.DWG

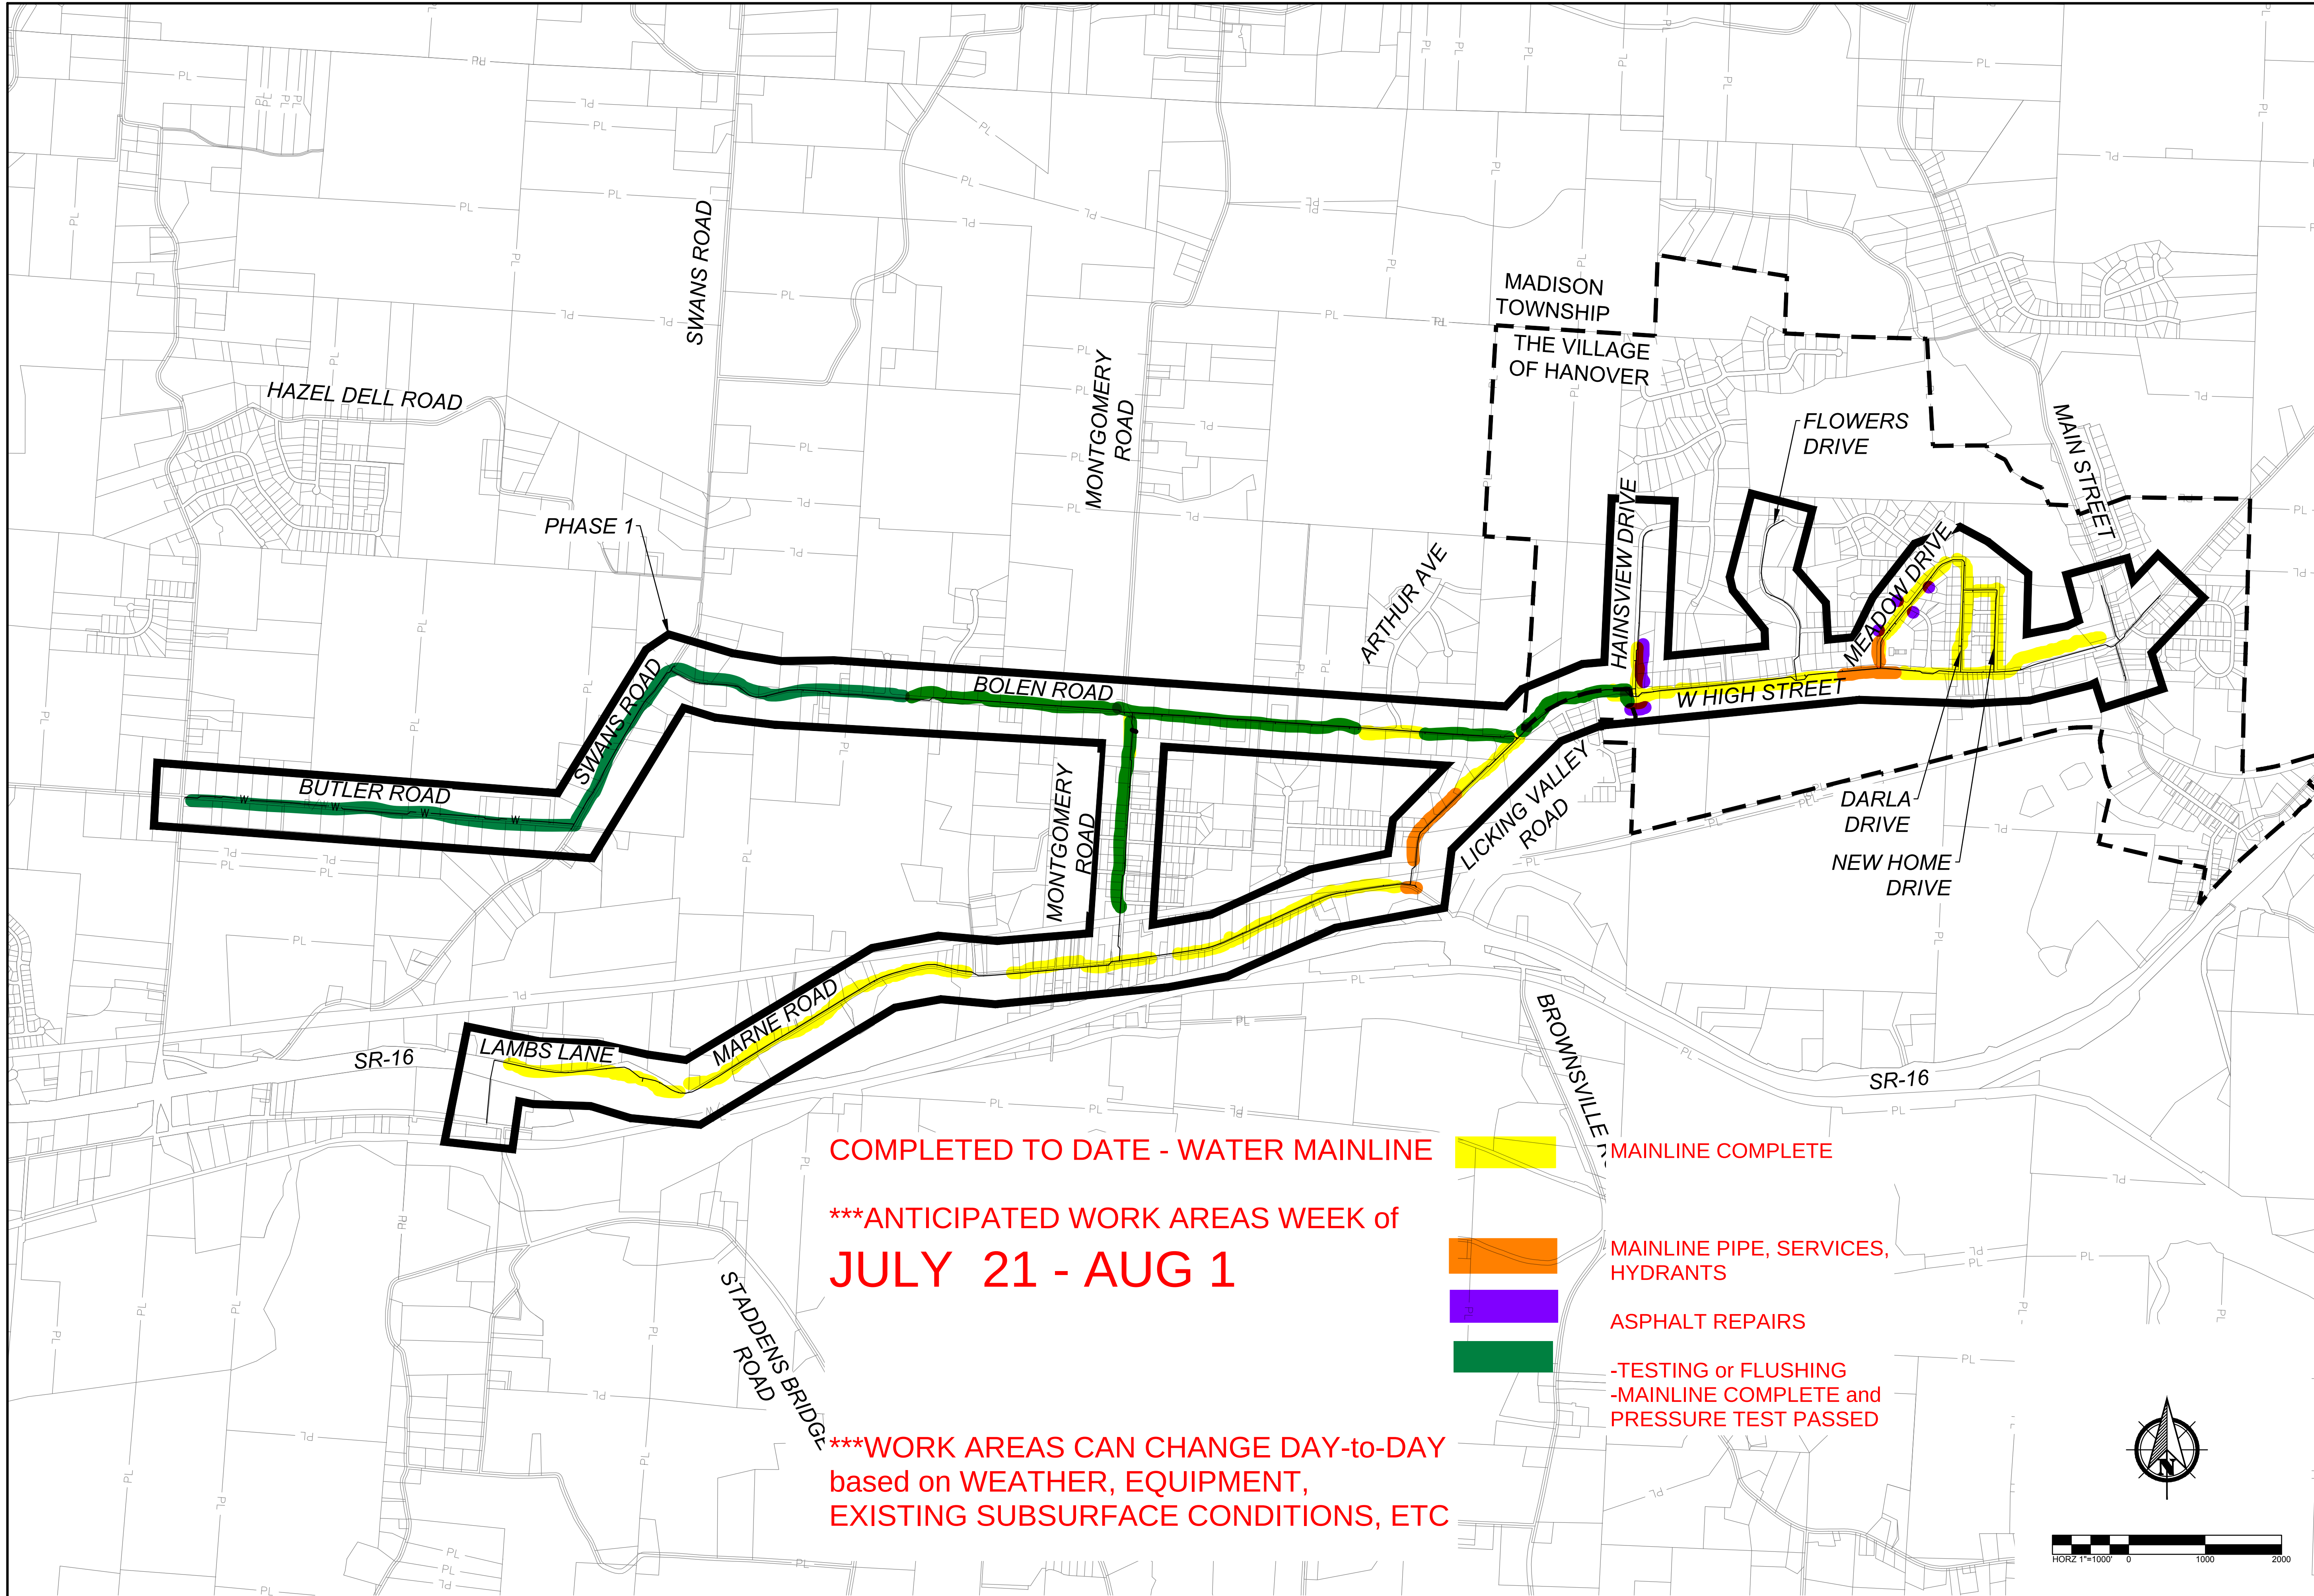


CONSTRUCTION DOCUMENTS
FOR
**HANOVER WATER EXTENSION
PHASE 1**
CITY OF HANOVER, LICKING COUNTY, OHIO
OVERALL PLAN

REVISIONS	DATE	SHEET NO.	DESCRIPTION

DATE:	5/15/2026
DRAWN BY:	MNA
CHECKED BY:	BJM
JOB NUMBER:	2022.03308

C100

PLOT SCALE: 1"=100' DATE: 5/15/26 - 11:00 AM EDITED BY: MAHMOUD DRAWING FILE: C:\2022\03\308D DRAWINGS\CIVIL\CONSTRUCTION\DOCUMENTS\ARCHIVE\2026-05-15\2022-03\308D CE OSPY.DWG

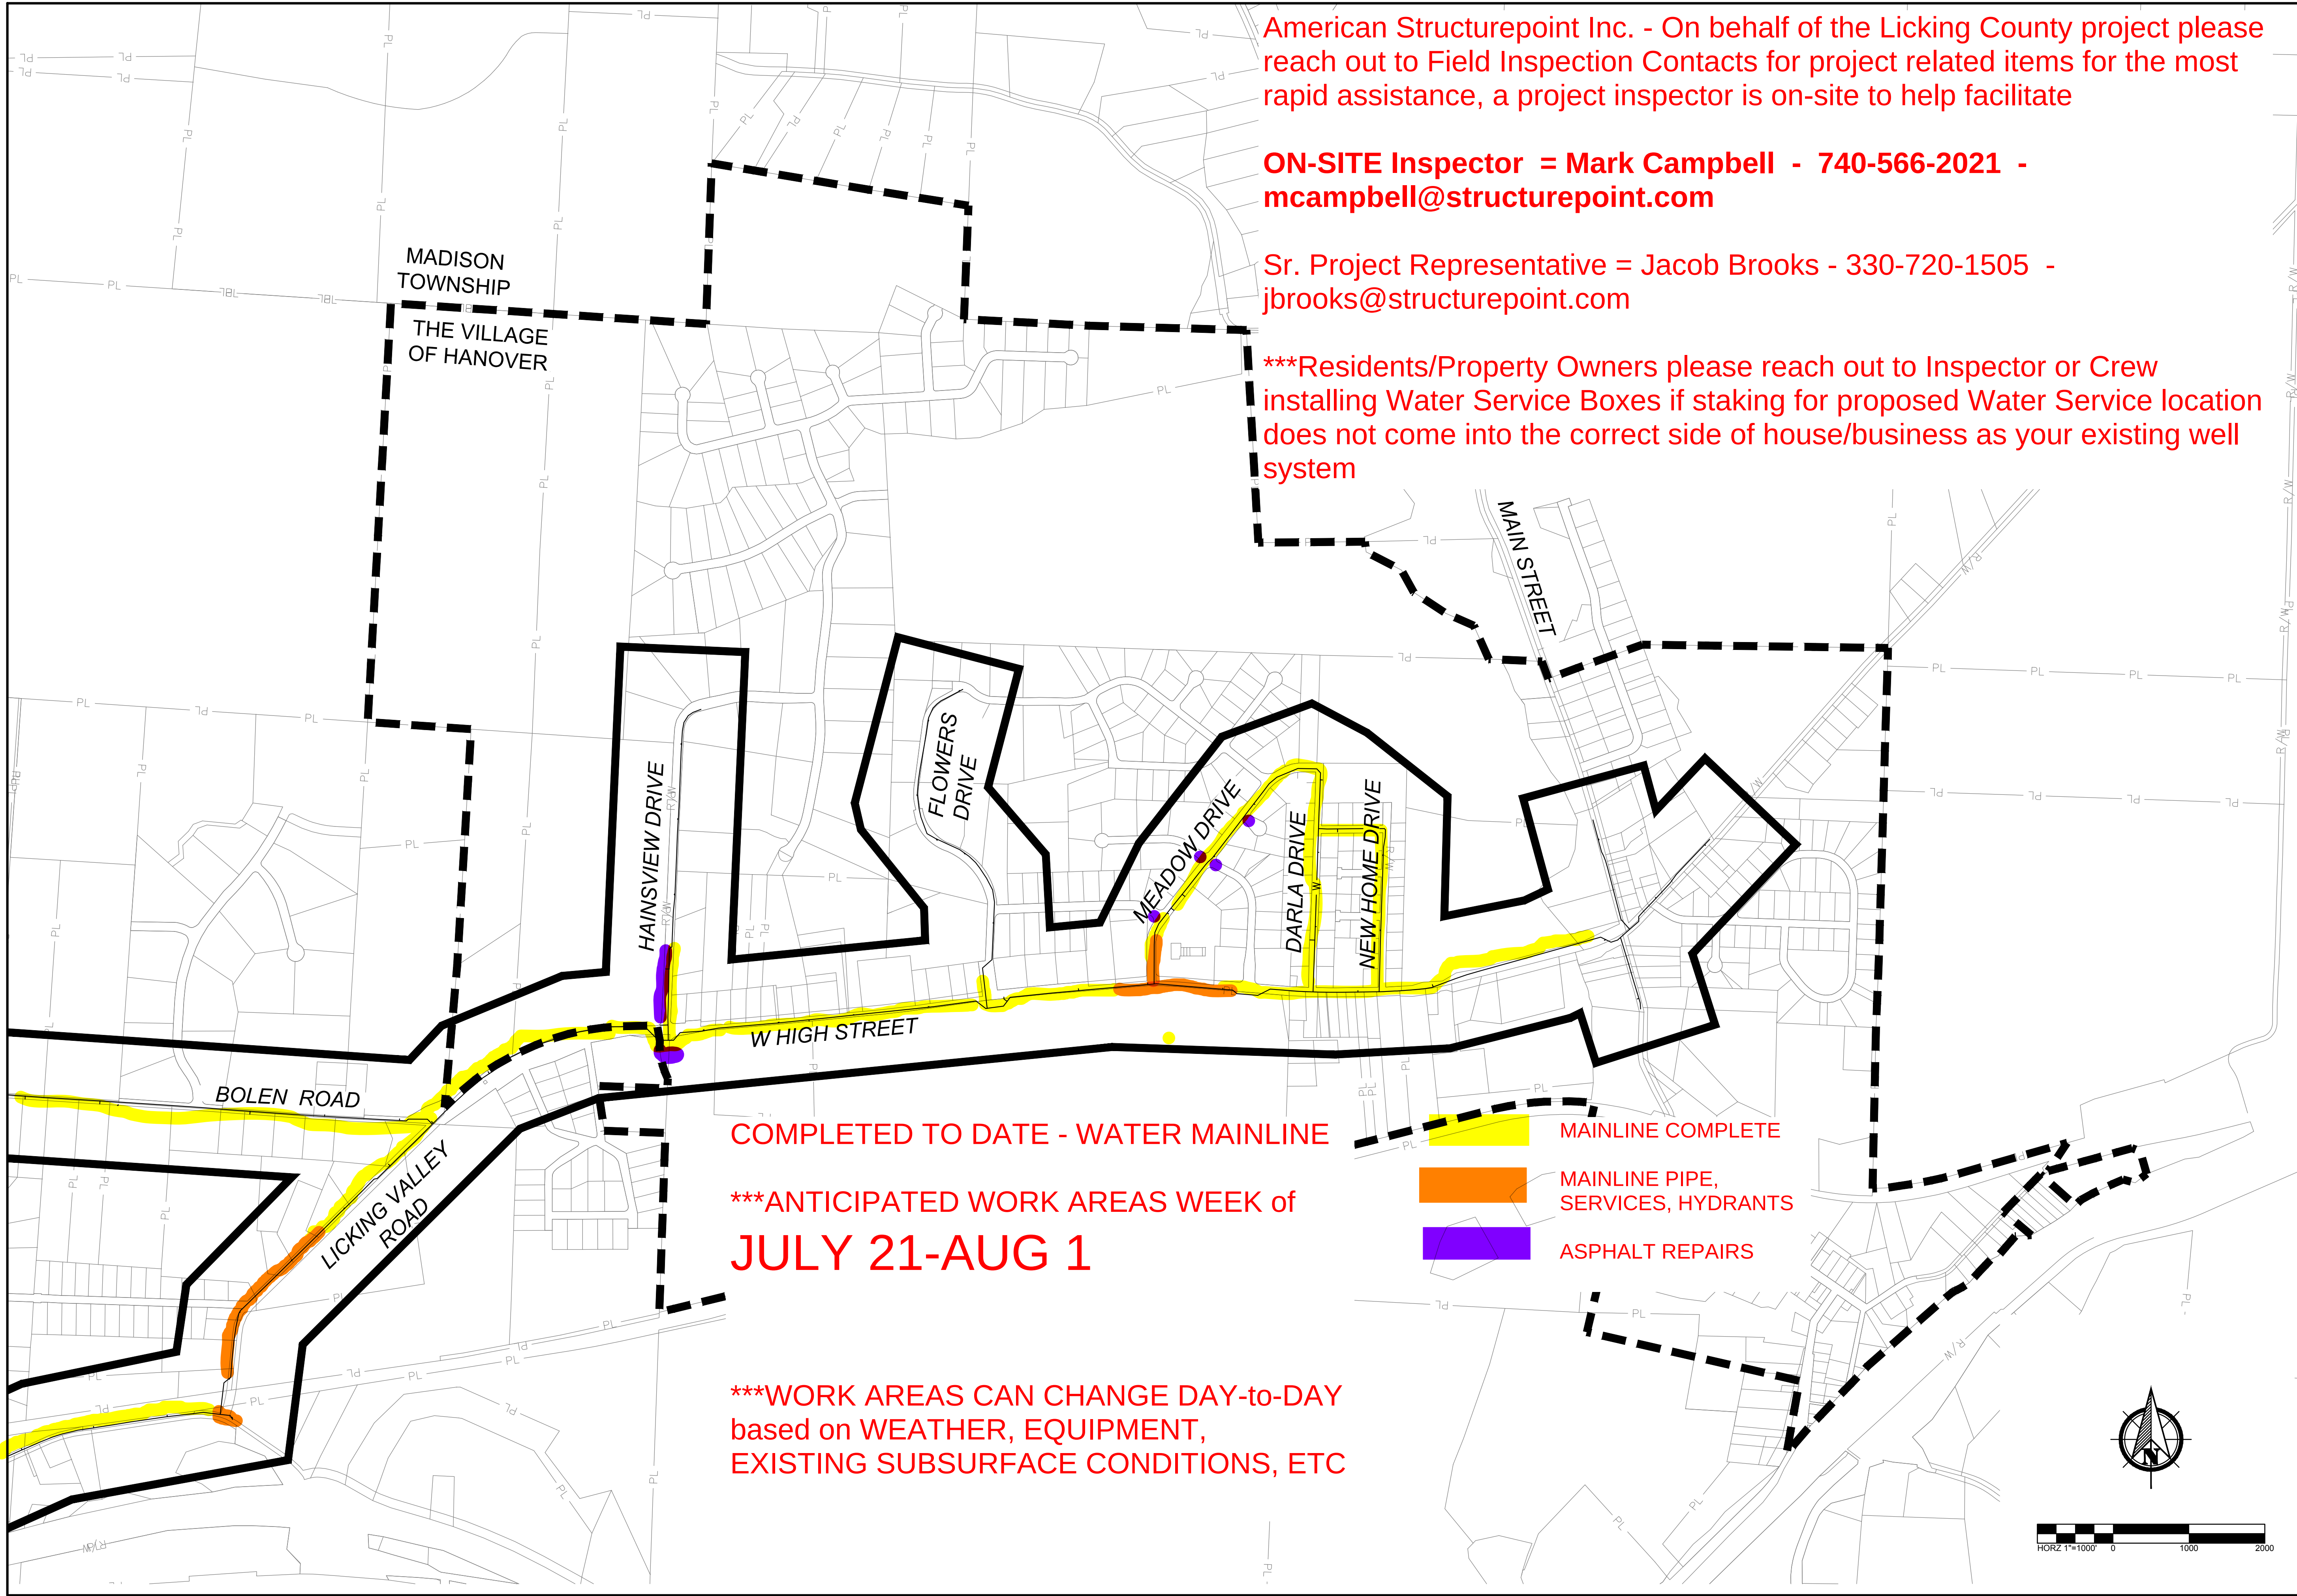

American Structurepoint Inc. - On behalf of the Licking County project please reach out to Field Inspection Contacts for project related items for the most rapid assistance, a project inspector is on-site to help facilitate

ON-SITE Inspector = Mark Campbell - 740-566-2021 - mcampbell@structurepoint.com

Sr. Project Representative = Jacob Brooks - 330-720-1505 - jbrooks@structurepoint.com

*****Residents/Property Owners please reach out to Inspector or Crew installing Water Service Boxes if staking for proposed Water Service location does not come into the correct side of house/business as your existing well system**



CONSTRUCTION DOCUMENTS
FOR
**HANOVER WATER EXTENSION
PHASE 1**
CITY OF HANOVER, LICKING COUNTY, OHIO
OVERALL PLAN

REVISIONS	DATE	SHEET NO.	DESCRIPTION

DATE: 5/15/2026
DRAWN BY: MNA
CHECKED BY: BJM
JOB NUMBER: 2022.03308

C100

