



AMERICAN
STRUCTUREPOINT
INC.



LICKING COUNTY, OHIO HANOVER WATERLINE EXTENSION – PHASE 1

Recent Progress – (7-27-26 to 8-8-26)

- **12” mainline trench/bore crew on FLOWERS DR ongoing** installed 1,660 feet of 12” watermain.
-Secondary crews installed water services and hydrants behind the main line crew.
- **12” mainline bore crew completed LICKING VALLEY RD** 1,540 feet of installations North of railroad and church drive. Completed water services, hydrants, and re-graded lawns & placed straw.
- **Asphalt repair crew** on N end of Meadow repairs completed to Valley intersection.
 - Removing all steel plates from Hainsview
- **12” Watermain pressure testing** completed on Licking Valley Rd. from Bolen to Darla. And sides streets of Meadow, Darla, and 6” water main on Chester, & New Home.
 - Last section on Bolen at Arthur lead found and passed testing.

Week Look Ahead – (8-10-26 to 8-15-26)

- **Miller Pipeline Pavement Repair Crew**
 - Complete MEADOW pavement repairs, address anything else project wide not yet repaired
- **12” Mainline Crew on FLOWERS** to complete installations of mainline, services, and hydrants
- **THEN MOBILIZE TO INSTALL WATER METER VAULT @ E MAIN STREET in the City of Newark**
- **12” Mainline Crew begin boring up along E side of Hainsview Drive near 1,630 LF of install remaining to end of Hainsview in this project.**
- **Flushing/Testing back on W and N side township side of project.** To run chlorine solution through passed watermain on Butler, Swans, Bolen for testing to verify system as potable and ready for active use section on BOLEN Rd. needs a repair to finish testing on Bolen.
- *Casing pipes now on site for SR-16 and two Railroad crossings (at LV Rd. and Montgomery Rd). Jack-bore crew could be scheduled anytime to begin these activities.*

Traffic Impacts. WORK HOURS can range from 7am – 7pm

1. FLOWERS = Mainline installs will have 1-lane, 2-way traffic with flaggers
2. HAINVIEW = Mainline installs will have 1-lane, 2-way traffic with flaggers
3. E MAIN in Newark = TBD a date for delivery and setting of meter vault, may require a planned 1-day closure and detour
4. MEADOW = local traffic around pavement repair crew coned work zone

Approx. project progress: 77% calendar (147 days of 639 days), 74.0% of pipe installed

***American Structurepoint Inc. - On behalf of the Licking County project please reach out to Field Inspection Contacts for project related items for the most rapid assistance, a project inspector is on-site to help facilitate, including concerns within Village and Township areas, please reach out as needed.

ON-SITE Inspector = Mark Campbell - 740-566-2021 - mcampbell@structurepoint.com

Sr. Project Representative = Jacob Brooks - 330-720-1505 - jbrooks@structurepoint.com

*****Residents/Property Owners please reach out to Inspector or Crew installing Water Service Boxes if staking for proposed Water Service location does not come into the correct side of house/business as your existing well system*****

Flowers at Fleming. Future stub for Fleming at NE corner of intersection




Restoration along Licking Valley Rd. south of Bolen



Pavement replacement on Meadow to Valley



PLOT SCALE: 1"=100' DATE: 5/15/26 - 10:59 AM EDITED BY: MAHMOUD DRAWING FILE: C:\2022\03308D - DRAWINGS\CIVIL\CONSTRUCTION DOCUMENTS\2022.03308D CE.CSP.DWG

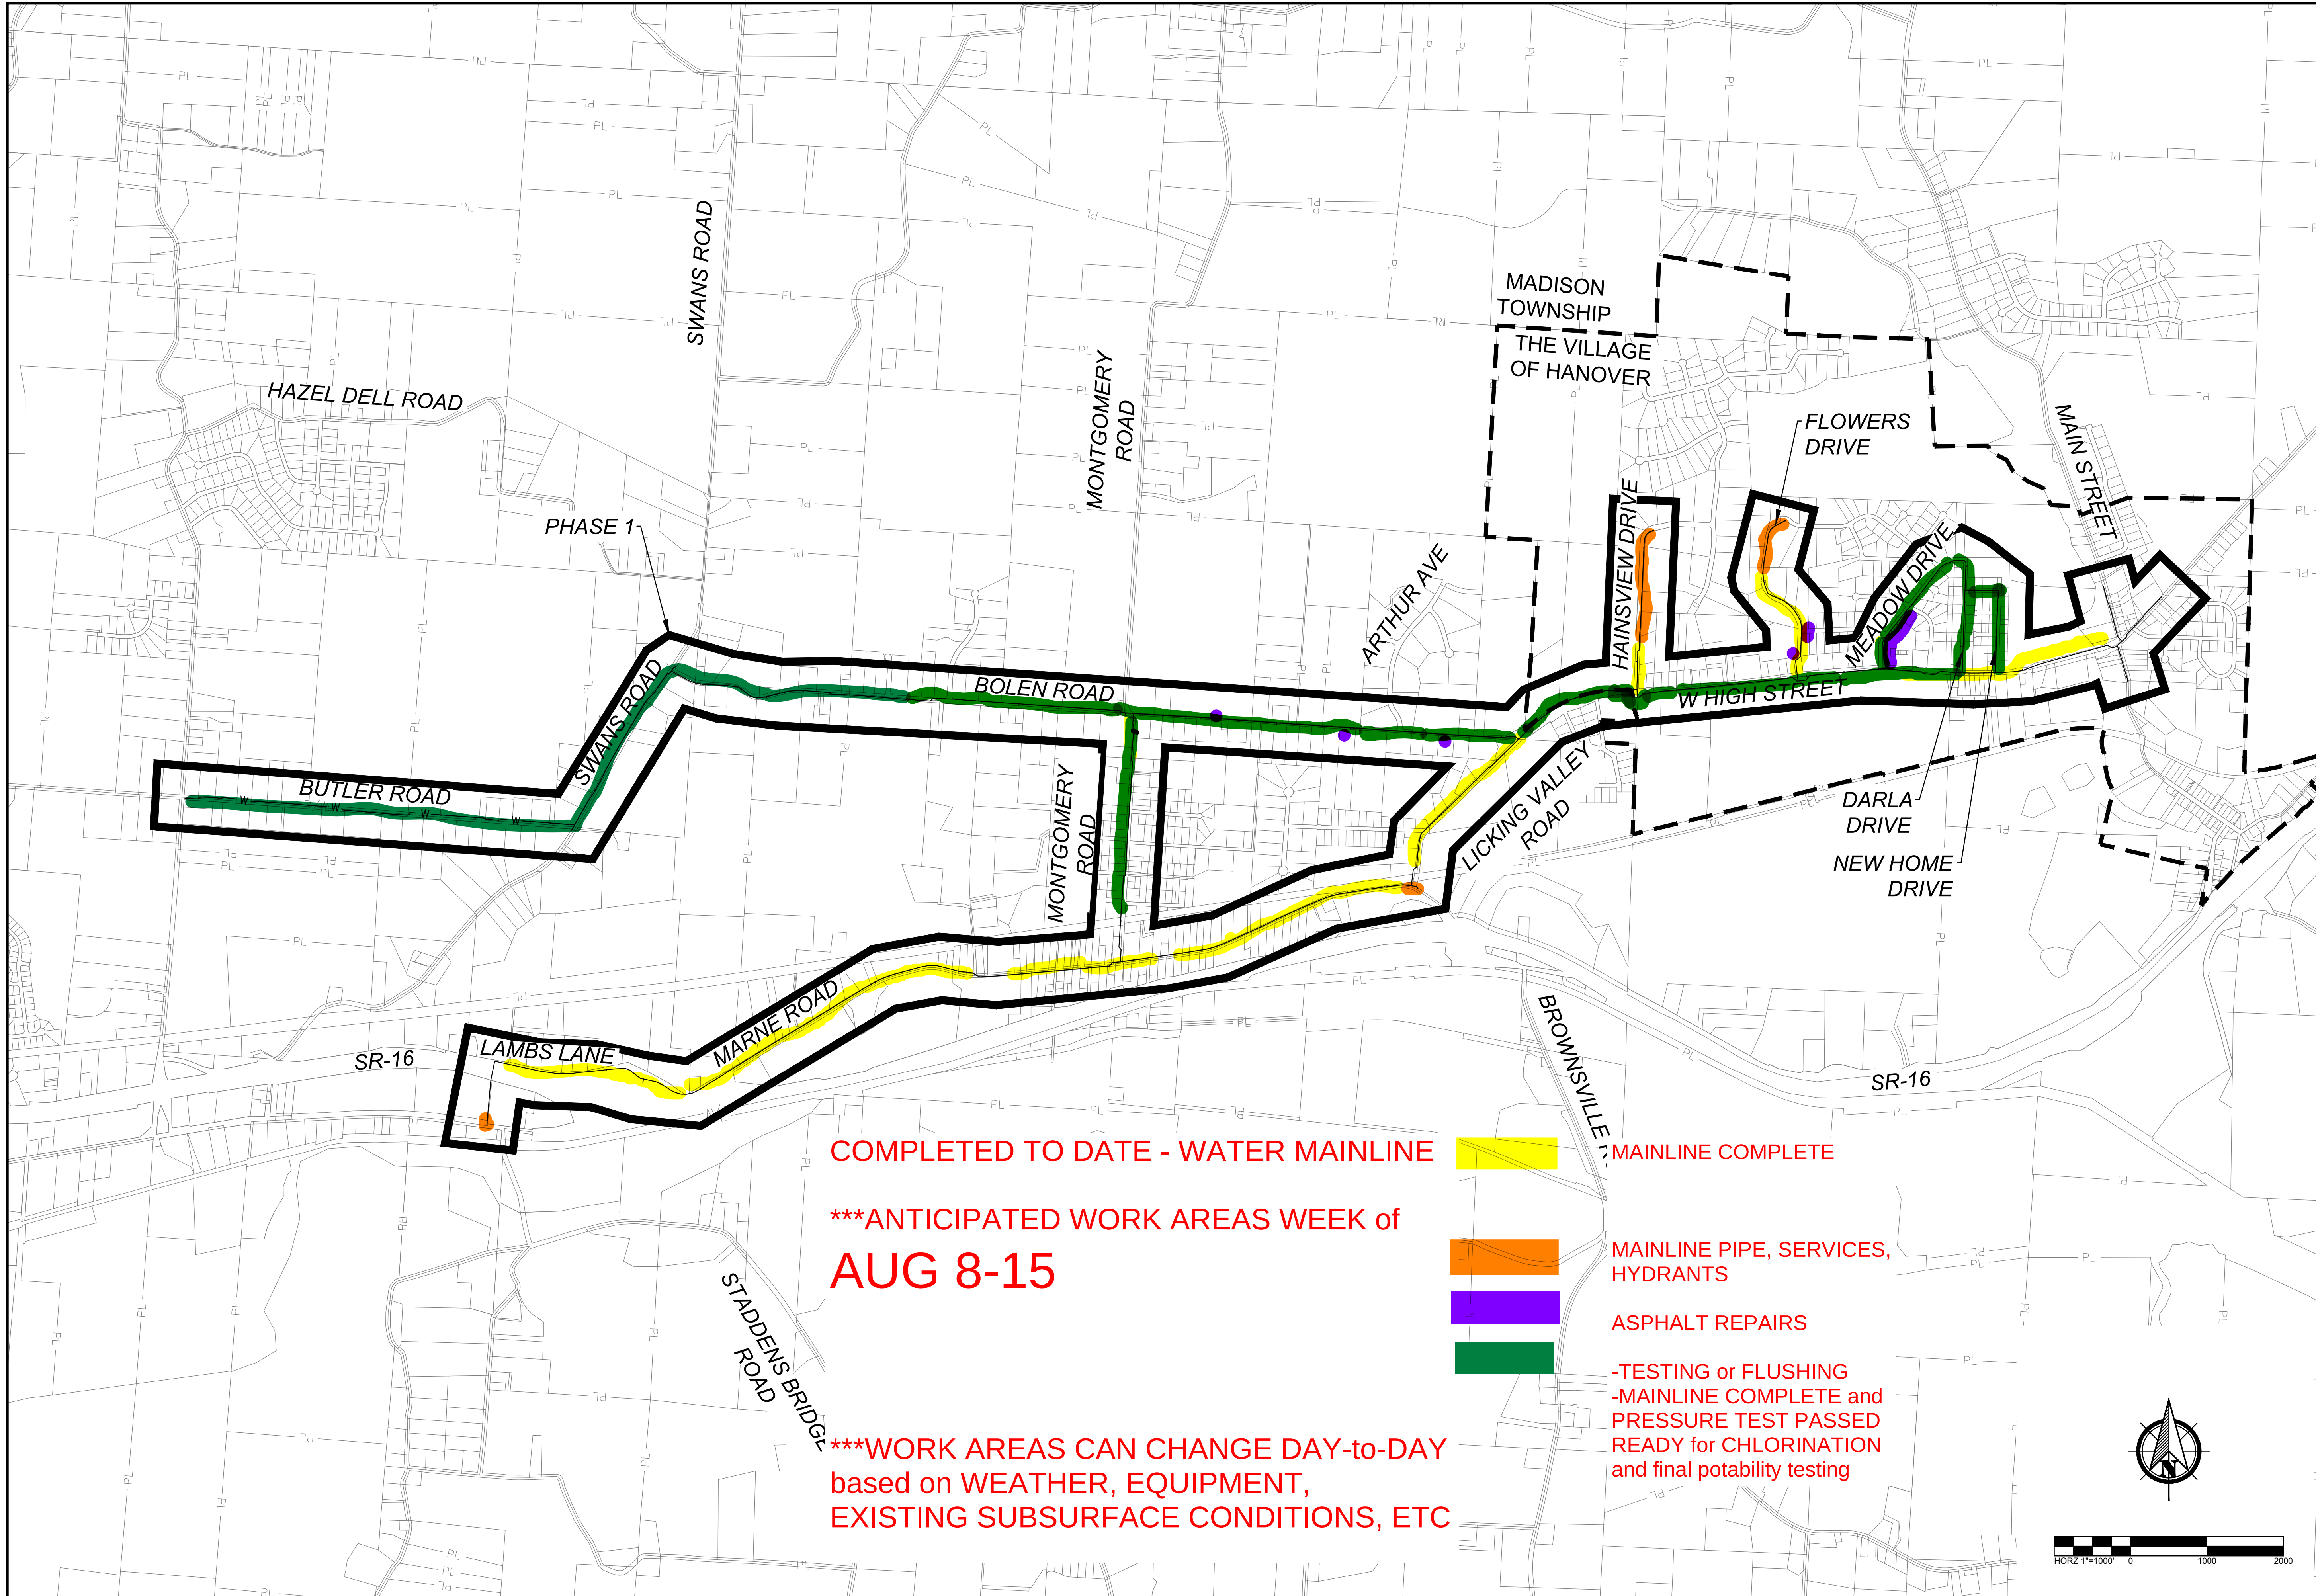

COMPLETED TO DATE - WATER MAINLINE

***ANTICIPATED WORK AREAS WEEK of
AUG 8-15

***WORK AREAS CAN CHANGE DAY-to-DAY
based on WEATHER, EQUIPMENT,
EXISTING SUBSURFACE CONDITIONS, ETC

MAINLINE COMPLETE

MAINLINE PIPE, SERVICES,
HYDRANTS

ASPHALT REPAIRS

-TESTING or FLUSHING
-MAINLINE COMPLETE and
PRESSURE TEST PASSED
READY for CHLORINATION
and final potability testing




CONSTRUCTION DOCUMENTS
FOR
**HANOVER WATER EXTENSION
PHASE 1**
CITY OF HANOVER, LICKING COUNTY, OHIO
OVERALL PLAN

REVISIONS	DATE	SHEET NO.	DESCRIPTION

DATE: 5/15/2026
DRAWN BY: MNA
CHECKED BY: BJM
JOB NUMBER: 2022.03308

C100

PLOT SCALE: 1"=100' DATE: 5/15/26 - 11:00 AM EDITED BY: MAHMOUD DRAWING FILE: C:\2022\03\308D.DRAWINGS\CIVIL\CONSTRUCTION\DOCUMENTS\ARCHIVE\2026-05-15\2022-03\308D.CE.OSP\DWG

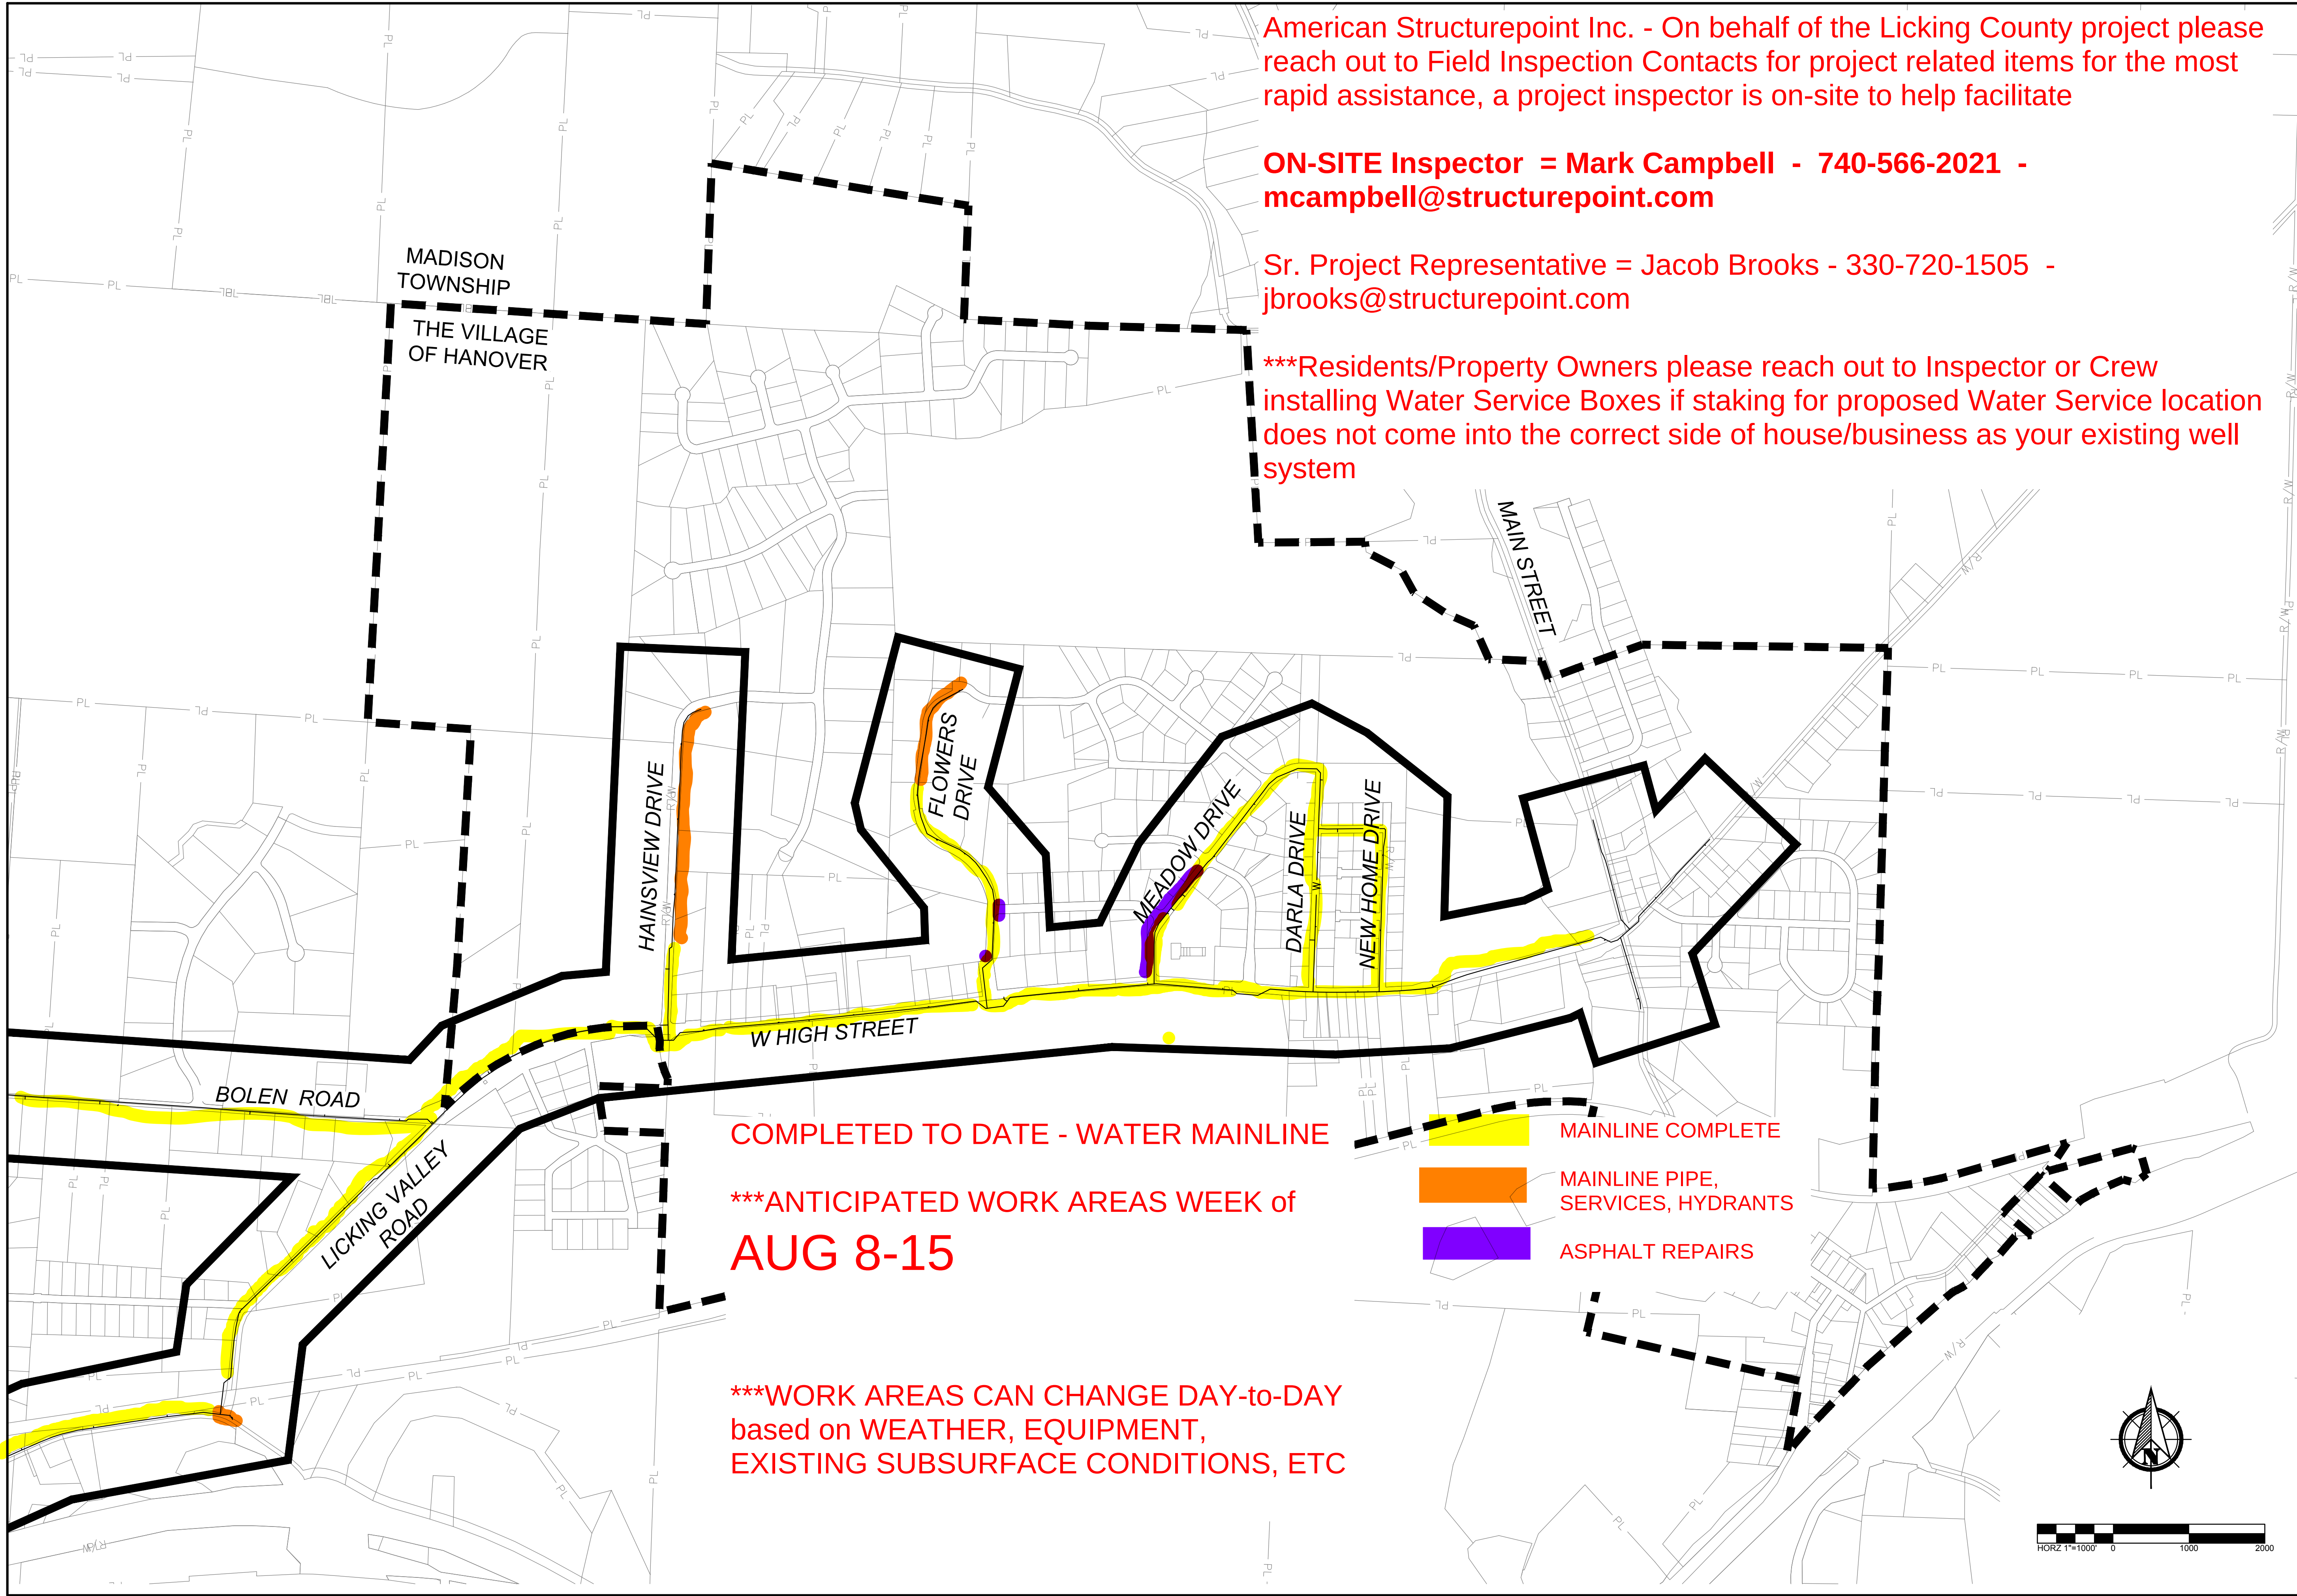

American Structurepoint Inc. - On behalf of the Licking County project please reach out to Field Inspection Contacts for project related items for the most rapid assistance, a project inspector is on-site to help facilitate

ON-SITE Inspector = Mark Campbell - 740-566-2021 - mcampbell@structurepoint.com

Sr. Project Representative = Jacob Brooks - 330-720-1505 - jbrooks@structurepoint.com

*****Residents/Property Owners please reach out to Inspector or Crew installing Water Service Boxes if staking for proposed Water Service location does not come into the correct side of house/business as your existing well system**



CONSTRUCTION DOCUMENTS
FOR
**HANOVER WATER EXTENSION
PHASE 1**
CITY OF HANOVER, LICKING COUNTY, OHIO
OVERALL PLAN

REVISIONS	DATE	SHEET NO.	DESCRIPTION

DATE: 5/15/2026
DRAWN BY: MNA
CHECKED BY: BJM
JOB NUMBER: 2022.03308

C100
