



AMERICAN
STRUCTUREPOINT
INC.



**MILLER
PIPELINE**



LICKING COUNTY, OHIO HANOVER WATERLINE EXTENSION – PHASE 1

Recent Progress – (8-17-26 to 8-27-26)

- **12” mainline trench/bore crew on FLOWERS DR – 100%**
- **12” mainline bore crew completed LICKING VALLEY RD – 90%** Complete, remained is the jack-bore under the railroad and the bore under the Licking Valley & Marne intersection
- **Asphalt repair crew** complete on Meadow from N end down to between Fleming and W High
 - **Concrete crew** completed damaged walk and curb at Primary School entrance and also several drive aprons on Darla
- **12” Watermain pressure testing** caught up with all installations as far as able.
 - Chlorination of the 8” Watermain in Township areas Butler/Swans/Bolen began on 8/26

Week Look Ahead – (8-27-26 to 9-5-26)

- **Miller Pipeline Pavement Repair Crew**
 - Complete MEADOW and CHESTER pavement repairs
- **Mainline Crew on FLOWERS repair a leak in first uphill curve section**
 - **THEN** return back to LAMBS LANE to continue excavation for BORE PITS for Jack-Bore under SR-16
- **12” Mainline Crew repair leak in W HIGH between Darla and Panther Pizza.**
 - **Then finish N end of Hainsview work near Panther Drive.**
 - **Then fall back to MARNE Rd. for one of two remaining creek bores.**
- **Flushing/Testing back on W and N side township side of project.** To run chlorine solution through passed watermain on Butler, Swans, Bolen for testing to verify system as potable and ready for active use section on BOLEN Rd. needs a repair to finish testing on Bolen.
- *Casing pipes now on site for SR-16 and two Railroad crossings (at LV Rd. and Montgomery Rd). Jack-bore crew could be scheduled anytime to begin these activities.*
- *Railroad has provided permit for work to proceed*

Traffic Impacts. WORK HOURS can range from 7am – 7pm

1. FLOWERS = Repair effort will have 1-lane, 2-way traffic with flaggers
2. W HIGH = Repair effort will have 1-lane, 2-way traffic with flaggers 9am-2pm
3. HAINSVIEW = Service installs will have 1-lane, 2-way traffic with flaggers 9am-2pm
4. LAMBS LANE = 1-lane, 2-way traffic with flaggers during work hours – automated signals may be needed for off-work hours and weekends to keep access to Wilson's Garden Center
5. MARNE = Mainline bore will have 1-lane, 2-way traffic with flaggers

Approx. project progress: 80% calendar (127 days of 639 days), 76.0% of pipe installed

***American Structurepoint Inc. - On behalf of the Licking County project please reach out to Field Inspection Contacts for project related items for the most rapid assistance, a project inspector is on-site to help facilitate, including concerns within Village and Township areas, please reach out as needed.

ON-SITE Inspector = Mark Campbell - 740-566-2021 - mcampbell@structurepoint.com

Sr. Project Representative = Jacob Brooks - 330-720-1505 - jbrooks@structurepoint.com

*****Residents/Property Owners please reach out to Inspector or Crew installing Water Service Boxes if staking for proposed Water Service location does not come into the correct side of house/business as your existing well system*****

DARLA drive apron and pavement repairs




Setting up access drive on E Main Street in Newark toward installs to go under SR-16



Ongoing efforts dewatering on LAMBS LANE for bore pit excavation



PLOT SCALE: 1"=100' DATE: 5/15/26 - 10:59 AM EDITED BY: MAHMOUD DRAWING FILE: C:\2022\03\308D_DRAINING\SS\CVIL\CONSTRUCTION DOCUMENTS\2022.03308 CE.CSP.DWG

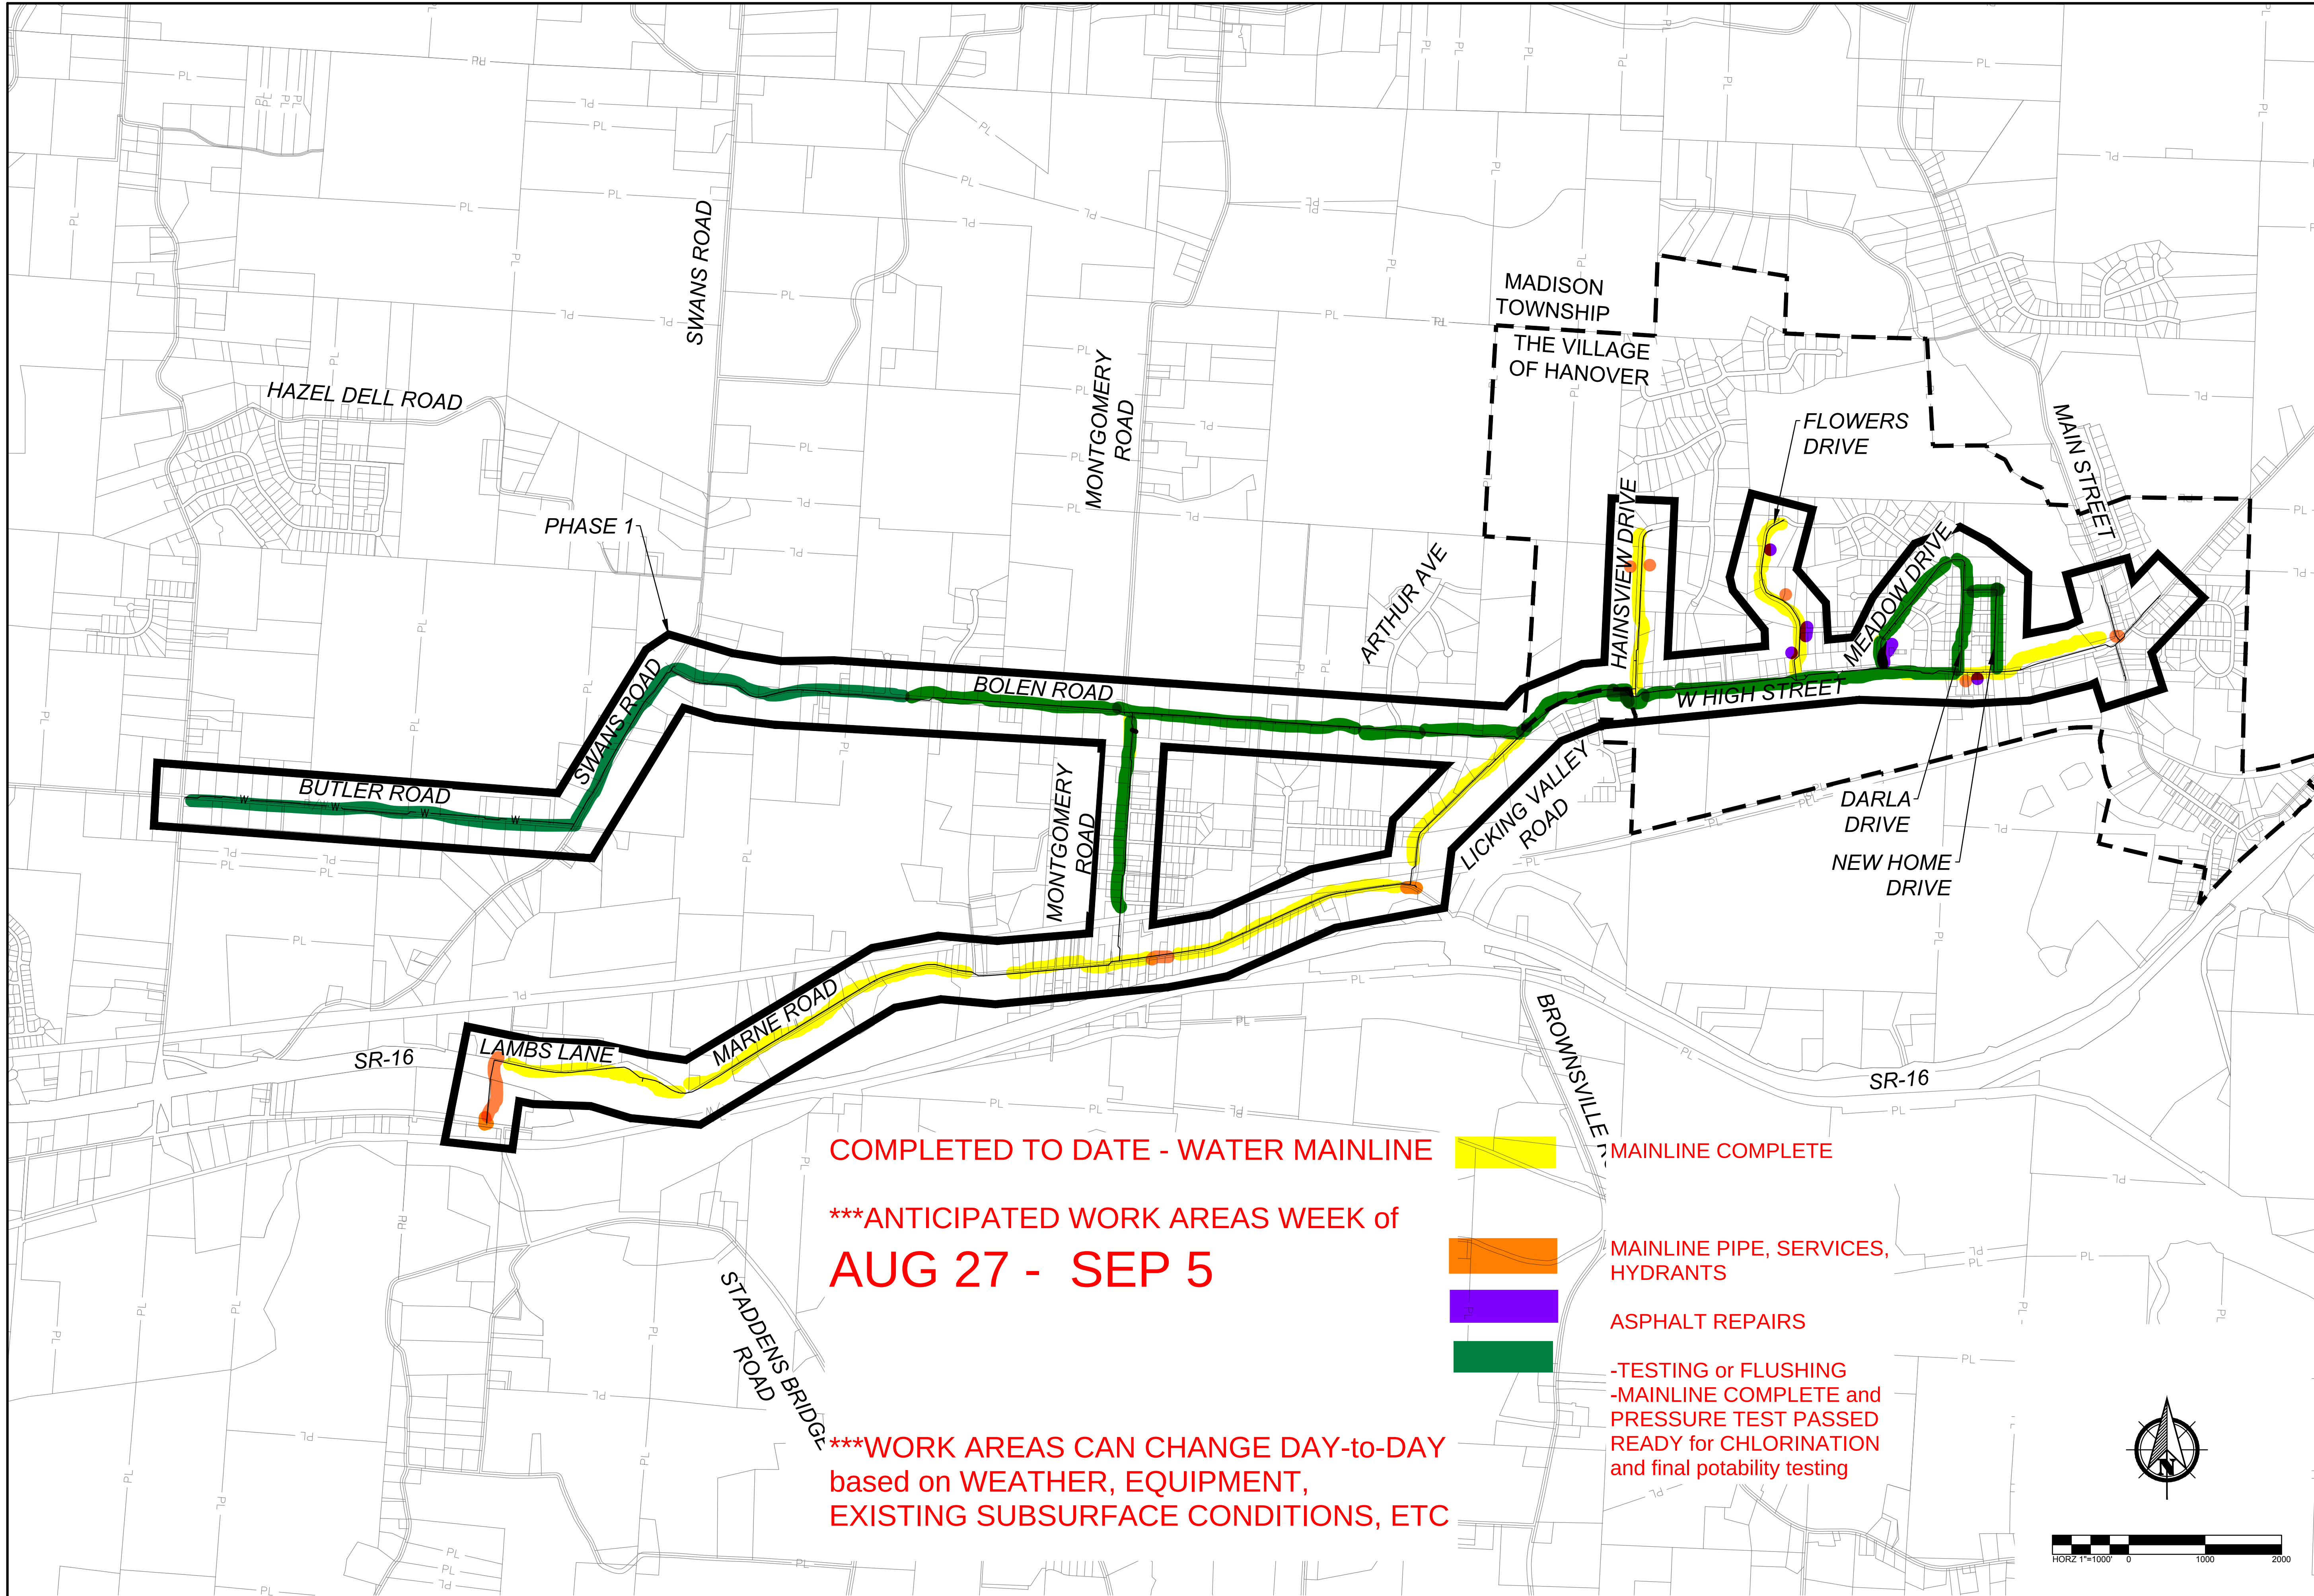

COMPLETED TO DATE - WATER MAINLINE

***ANTICIPATED WORK AREAS WEEK of
AUG 27 - SEP 5

***WORK AREAS CAN CHANGE DAY-to-DAY
based on WEATHER, EQUIPMENT,
EXISTING SUBSURFACE CONDITIONS, ETC

MAINLINE COMPLETE

MAINLINE PIPE, SERVICES,
HYDRANTS

ASPHALT REPAIRS

-TESTING or FLUSHING
-MAINLINE COMPLETE and
PRESSURE TEST PASSED
READY for CHLORINATION
and final potability testing




CONSTRUCTION DOCUMENTS
FOR
**HANOVER WATER EXTENSION
PHASE 1**
CITY OF HANOVER, LICKING COUNTY, OHIO
OVERALL PLAN

REVISIONS	DATE	SHEET NO.	DESCRIPTION

DATE: 5/15/2026
DRAWN BY: MNA
CHECKED BY: BJM
JOB NUMBER: 2022.03308

C100

PLOT SCALE: 1"=100' DATE: 5/15/26 - 11:00 AM EDITED BY: MAHMOUD DRAWING FILE: C:\2022\03308D.DRAWINGS\CIVIL\CONSTRUCTION\DOCUMENTS\ARCHIVE\2026-05-15\2022-03308D.CE.OSP\DWG

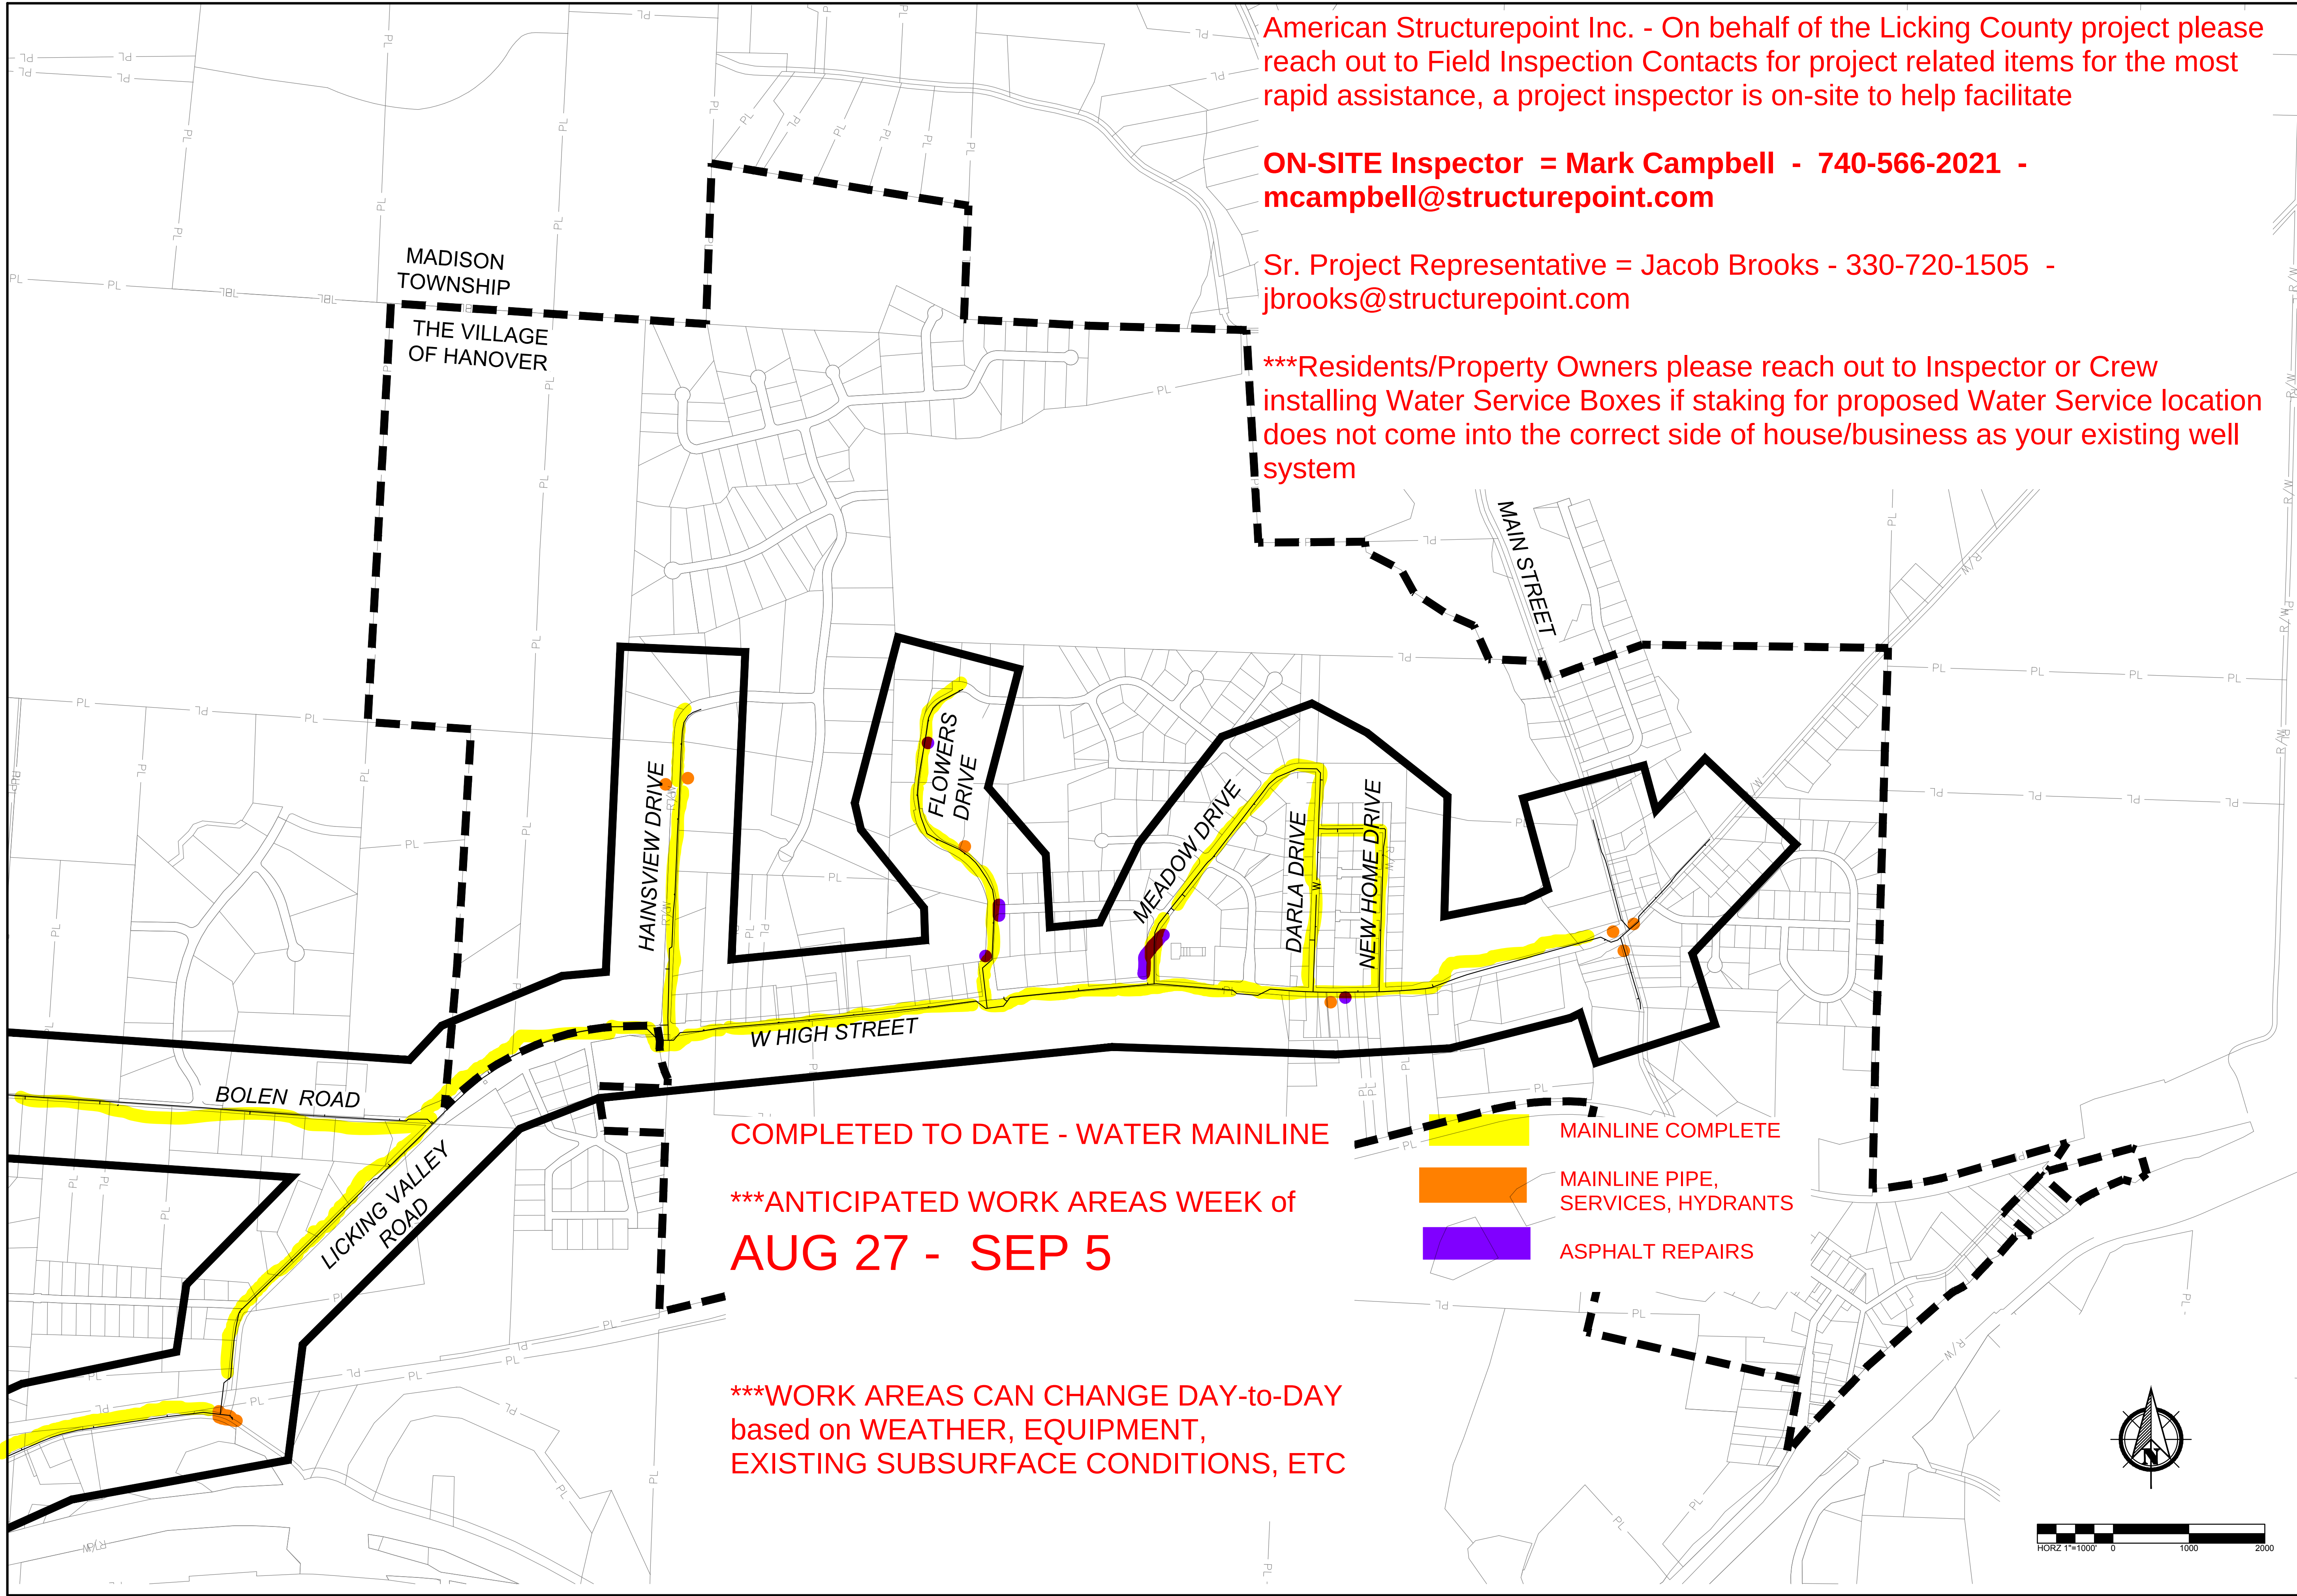

American Structurepoint Inc. - On behalf of the Licking County project please reach out to Field Inspection Contacts for project related items for the most rapid assistance, a project inspector is on-site to help facilitate

**ON-SITE Inspector = Mark Campbell - 740-566-2021 -
mcampbell@structurepoint.com**

**Sr. Project Representative = Jacob Brooks - 330-720-1505 -
jbrooks@structurepoint.com**

*****Residents/Property Owners please reach out to Inspector or Crew
installing Water Service Boxes if staking for proposed Water Service location
does not come into the correct side of house/business as your existing well
system**



CONSTRUCTION DOCUMENTS
FOR
**HANOVER WATER EXTENSION
PHASE 1**
CITY OF HANOVER, LICKING COUNTY, OHIO
OVERALL PLAN

REVISIONS	DATE	SHEET NO.	DESCRIPTION

DATE:	5/15/2026
DRAWN BY:	MNA
CHECKED BY:	BJM
JOB NUMBER:	2022.03308

C100

