



AMERICAN
STRUCTUREPOINT
INC.



LICKING COUNTY, OHIO HANOVER WATERLINE EXTENSION – PHASE 1

Recent Progress – (8-28-26 to 9-09-26)

- **12” mainline on HAINSVIEW, service leads, and hydrants – 95% - Completed 1 of 2 future 10” services to the school grounds**
- **12” mainline on MARNE Rd. – 95% - Completed bores under two creeks.**
- **Asphalt repair crew** completed two repairs on W HIGH Street and began on CHESTER
- **LAMBS LANE** – Crew began installing Hydrants and Water Services
- **Jack-bore crew on E MAIN to LAMBS LANE** – Receiving and Bore Pits excavated and secure, tracks for drill rig set, and pilot rod sent under SR-16 from pit to pit successfully on alignment

Week Look Ahead – (9-10-26 to 9-19-26)

- **Pavement Repair Crew**
 - Complete CHESTER pavement repairs, then other MISC repairs on FLOWERS, etc.
- JACK-BORE under SR-16 – 24” Steel Casing Pipe near 280 LF, then assemble 12” c-900 watermain with spacers through casing.
- Potentially begin jack-bore pits for Railroad crossing west side of MONTGOMERY Rd.
- **MARNE Rd. 12” watermain tie-ins** from completed waterway bores
- Pothole/explore existing utilities locations and depths at W HIGH/HICKMAN/S MAIN – goal to install watermain by bore-method in this area as much as able
- **Crew on or after 9/15 to finish 10” service under HAINSVIEW to school grounds**
- **Potable Water Testing on W and N side township side of project.** May get final results as soon as end of day 9/11.

Traffic Impacts. WORK HOURS can range from 7am – 7pm

1. CHESTER/FLOWERS = Local traffic around pavement repair crew
2. W HIGH = Pothole efforts at HICKMAN and S MAIN may be in street from 9am-2pm
3. HAINSVIEW = Service install will have 1-lane, 2-way traffic with flaggers 9am-2pm
4. LAMBS LANE = 1-lane, 2-way traffic with flaggers during work hours OR full closure where LAMBS LANE turns northward and access to Wilson's Garden Center will remain through their rear entrance. Garden Center has various signage in use to detour their customers.

Approx. project progress: 82.5% calendar (112 days of 639 days), 85.0% of pipe installed

***American Structurepoint Inc. - On behalf of the Licking County project please reach out to Field Inspection Contacts for project related items for the most rapid assistance, a project inspector is on-site to help facilitate, including concerns within Village and Township areas, please reach out as needed.

ON-SITE Inspector = Mark Campbell - 740-566-2021 - mcampbell@structurepoint.com

Sr. Project Representative = Jacob Brooks - 330-720-1505 - jbrooks@structurepoint.com

*****Residents/Property Owners please reach out to Inspector or Crew installing Water Service Boxes if staking for proposed Water Service location does not come into the correct side of house/business as your existing well system*****

MARNE Rd. bore under Bowling Green Run completed in one clean pull



12" Watermain being pulled under Bowling Green Run



Placing seed and straw to stabilize daily water service box install areas on MARNE Rd.




Jack-bore pit on South side of SR-16 to prepare to push casing pipe under roadway



Receiving pit for Jack-bore under SR-16 on Lambs Lane



PLOT SCALE: 1"=100' DATE: 5/15/26 - 10:59 AM EDITED BY: MAHMOUD DRAWING FILE: C:\2022\03\308D_DRAINING\SS\CVIL\CONSTRUCTION DOCUMENTS\2022.03308 CE.CSP.DWG

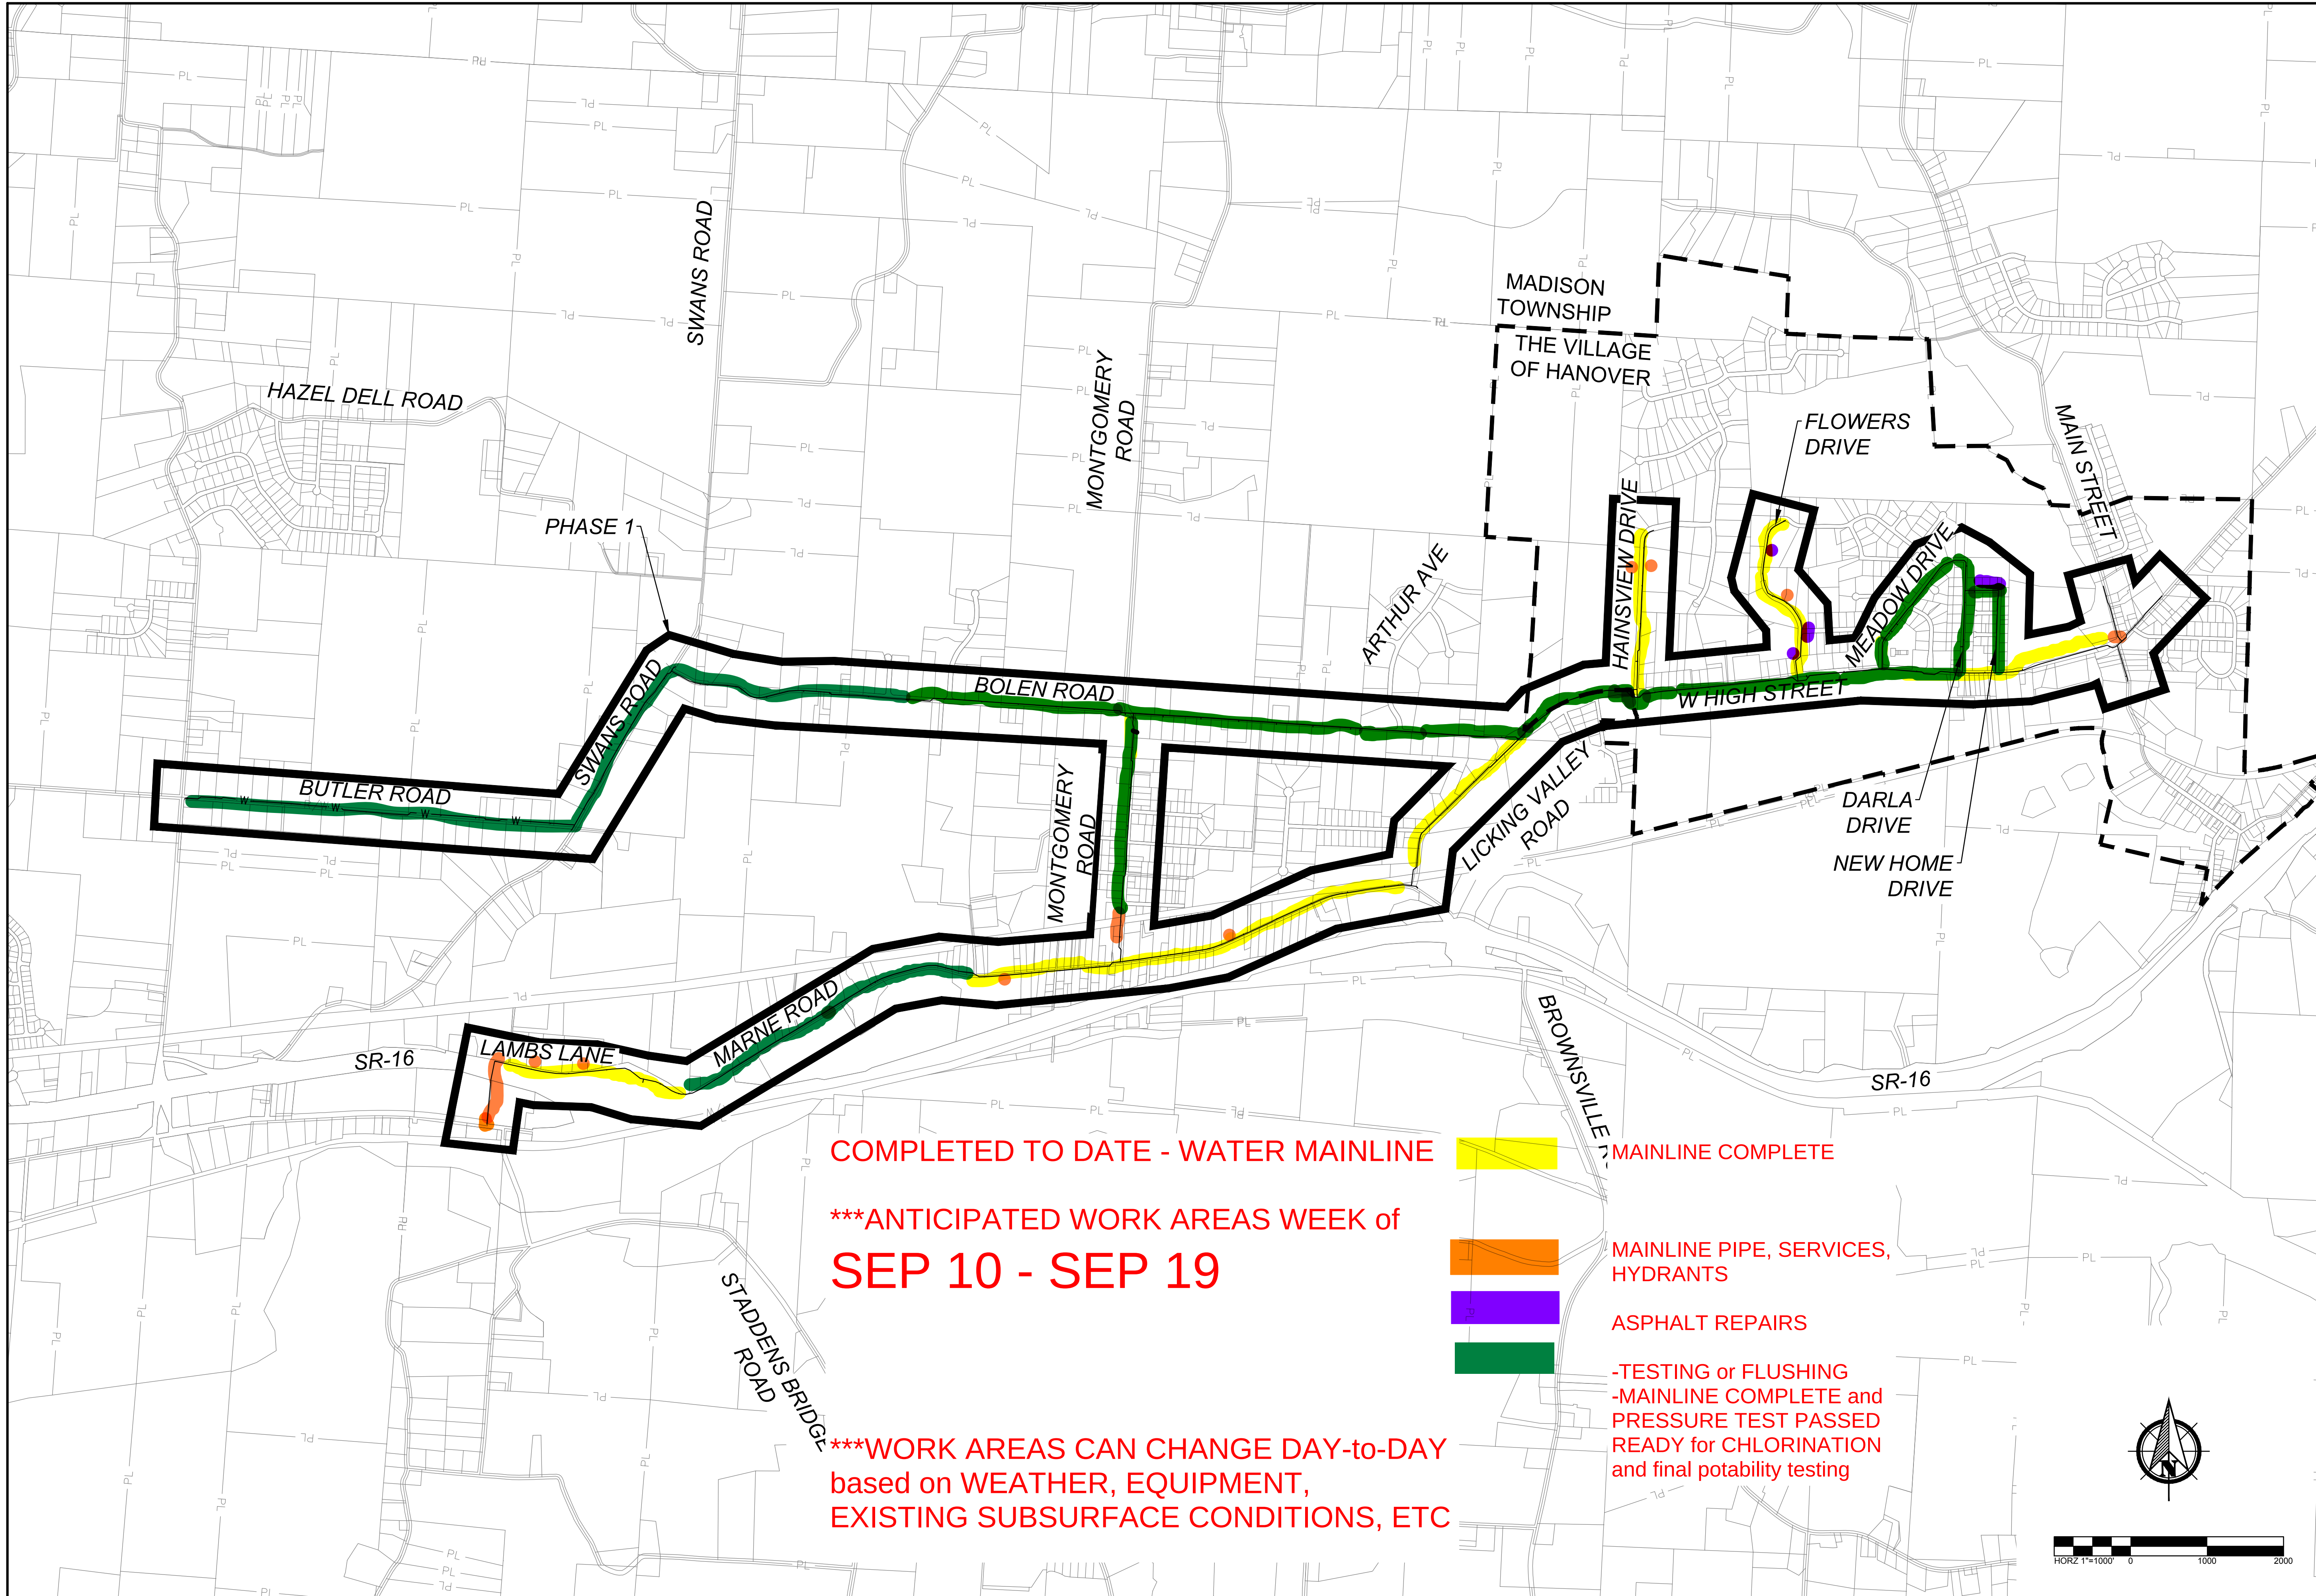



2550 Corporate Exchange Dr., Ste 300 | Columbus, Ohio 43231
TEL: 614.444.1226
www.structurepoint.com


CONSTRUCTION DOCUMENTS
FOR
**HANOVER WATER EXTENSION
PHASE 1**
CITY OF HANOVER, LICKING COUNTY, OHIO
OVERALL PLAN

REVISIONS	DATE	SHEET NO.	DESCRIPTION

DATE: 5/15/2026
DRAWN BY: MNA
CHECKED BY: BJM
JOB NUMBER: 2022.03308

C100

PLOT SCALE: 1"=100' DATE: 5/15/26 - 11:00 AM EDITED BY: MAHMOUD DRAWING FILE: C:\2022\03\308D.DRAWINGS\CIVIL\CONSTRUCTION\DOCUMENTS\ARCHIVE\2026-05-15\2022-03\308D.CE.OSHP\DWG

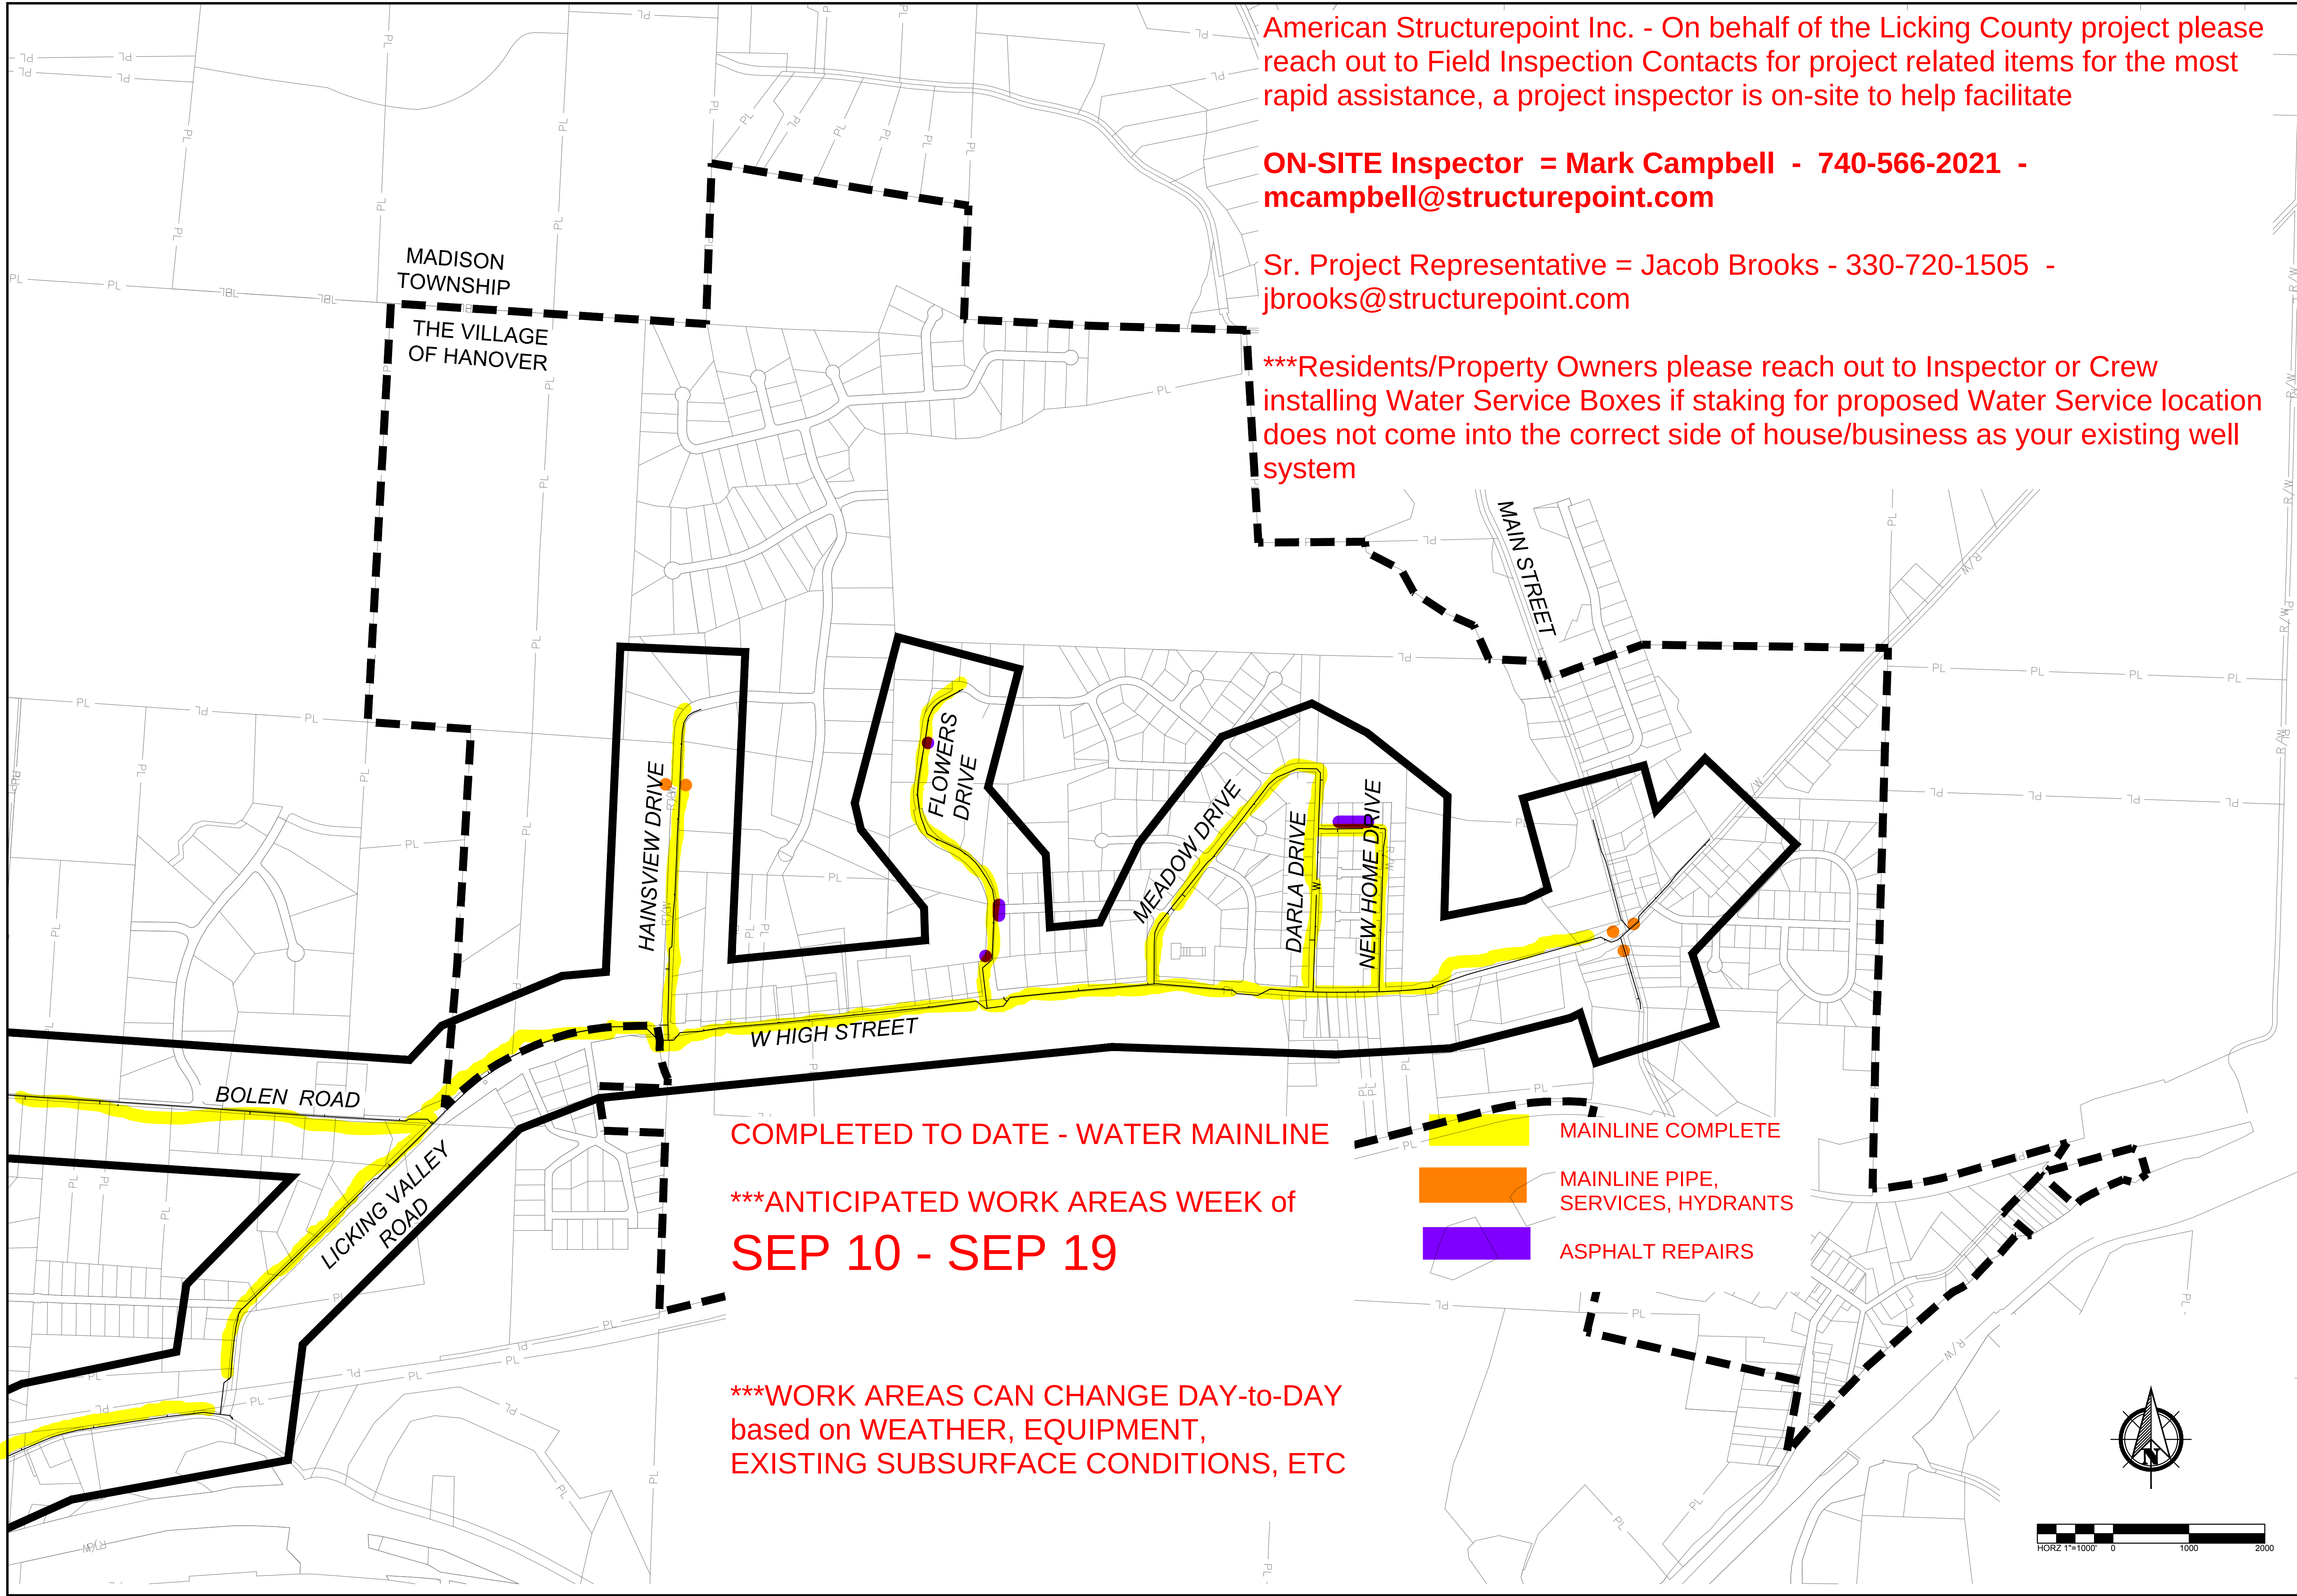

American Structurepoint Inc. - On behalf of the Licking County project please reach out to Field Inspection Contacts for project related items for the most rapid assistance, a project inspector is on-site to help facilitate

ON-SITE Inspector = Mark Campbell - 740-566-2021 - mcampbell@structurepoint.com

Sr. Project Representative = Jacob Brooks - 330-720-1505 - jbrooks@structurepoint.com


*****Residents/Property Owners please reach out to Inspector or Crew installing Water Service Boxes if staking for proposed Water Service location does not come into the correct side of house/business as your existing well system**

COMPLETED TO DATE - WATER MAINLINE

*****ANTICIPATED WORK AREAS WEEK of
SEP 10 - SEP 19**

*****WORK AREAS CAN CHANGE DAY-to-DAY
based on WEATHER, EQUIPMENT,
EXISTING SUBSURFACE CONDITIONS, ETC**

- MAINLINE COMPLETE**
- MAINLINE PIPE, SERVICES, HYDRANTS**
- ASPHALT REPAIRS**

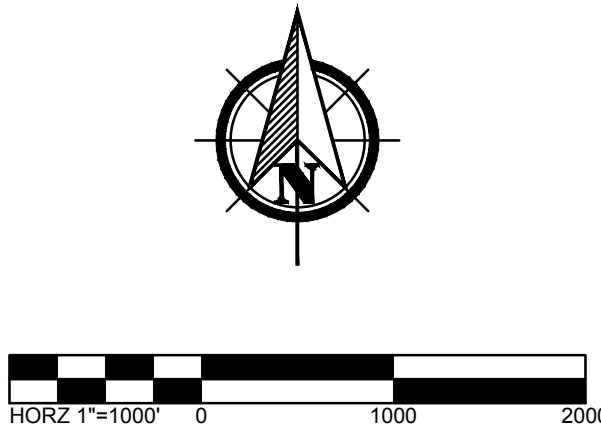

2550 Corporate Exchange Dr., Ste 300 | Columbus, Ohio 43231
TEL: 614-444-1226
www.structurepoint.com

CONSTRUCTION DOCUMENTS
FOR
**HANOVER WATER EXTENSION
PHASE 1**
CITY OF HANOVER, LICKING COUNTY, OHIO
OVERALL PLAN

REVISIONS	DATE	SHEET NO.	DESCRIPTION

DATE: 5/15/2026
DRAWN BY: MNA
CHECKED BY: BJM
JOB NUMBER: 2022.03308

C100
